



Ref No. MKCIL/ASSAM/PKG-07/225

Date: 04.06.2025

To,

The Team Leader.

M/s Technocrats Advisory Services Private Limited

In Association with MAV Associates LLP.

House No. NH-37, Maizdihi, Ward No.-2

(Near-Maa Kali Automobile) P.O. Settlement Road,

PS & Dist. Sribhumi, Assam, Pin-788712

Email: : iekarimganj@gmail.com

Subject: “Four Laning of NH-37 from Design Ch 0+000 on NH 8 near Karimganj to Design Ch. 14+250 near Sutarkandi (Spur connectivity to Indo/Bangladesh Border) Silchar- Churaibari Pkg-7 in the state of Assam”
– “Submission of Monthly Progress Report for the month of May-2025.”

Ref.:

1.LOA- NHIDCL/Assam/NH-37/Sil-Churai/Pkg-VII/233357/3087 dated 11.03.2024

2.Concession Agreement on dated 17th September 2024.

Dear Sir,

With reference to above cited subject, we are herewith submitting the Monthly Progress Report for the month of May, 2025 as per Clause 13.1 of Article 13 of Concession Agreement for your kind review and concurrence please.

Assuring you of our best services at all times.

Thanking you,

Your sincerely,

Project Manager

MKC Badarpur Churaibari Kamakhya (PKG-7) Highways Private Limited.

Encl.: As above.

Copy to: General Manager, NHIDCL, PMU-Karimganj, 2nd Floor, Bipin Paul Road, Ward No.- 24, Opp. Basak House, Karimganj, Assam- 788711, Email id- pmukarimganj@gmail.com

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

Monthly Progress Report

May - 2025



Authority		National Highways Infrastructure Development Corporation Limited
Independent Engineer		M/s Technocrafts Advisory Services Private Limited in association with M/s MAV Associates LLP
Concessionaire		MKC Badarpur Churaibari Kamakhya (PKG-7) Highways Pvt. Ltd.

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

TABLE OF CONTENTS


CHAPTERS	DESCRIPTIONS	PAGES
	TABLE OF CONTENTS	
	Project Road Location Map / Index Map	
	EXECUTIVE SUMMARY	
	1. The Project Road	
	2. Mobilization	
	3. Pre-Construction Activity	
	4. EPC Contractor	
	5. Status of Project Works Progress	
	6. Design & Drawing	
	7. Work Program	
	8. Quality Control & Material	
	9. Supervision and Monitoring of Project works	
	10. Site Visit and Meeting	
	11. Schedule Completion Date	
	12. Operation and Maintenance (O&M)	
	13. Area of Concern	
1	INTRODUCTION	
	General	
2	CONTRACT DATA	
3	SALIENT FEATURES OF PROJECT HIGHWAY	
	3.1 Pavement Composition (MCW)	
	3.2 Details of New/ Widening of Structures and Project Facilities	
4	SCOPE OF WORKS AND PROJECT FACILITIES	
	4.1 Scope of Works	
	4.2 Project Facilities	
5	PRE-CONSTRUCTION ACTIVITY	
	5.1 Obligations	
	5.2 Shifting of Utilities	
	5.3 Tree Cutting	
	5.4 Land Acquisition	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

	5.5 Hindrance, Payment Status and LA Status	
6	MOBILIZATION	
	6.1 Manpower Mobilization of Concessionaire	
	6.2 Organization Chart of Concessionaire	
7	DEPLOYMENT OF PLANTS AND EQUIPMENT / PROJECT SET UP PLAN	
	7.1 Plants and Equipment Deployed	
8	DESIGN AND DRAWING	
	8.1 Design	
	8.2 Drawing	
	8.3 Status of Drawings	
9	PROJECT WORK PROGRESS	
	9.1 Work Progress	
	9.2 Structure work Progress	
	9.3 Weightages of Components	
	9.4 S Curve of Project	
	9.5 Detailed Highway & Structure Works Progress	
10	QUALITY CONTROL AND MATERIAL	
	10.1 Quality Control	
	10.2 Site Laboratory	
	10.3 Material Testing	
	10.3.1 Soli and Aggregates	
	10.3.2 Cement	
	10.3.3 Reinforcement Steel	
	10.3.4 Status of Material Sources Approvals & Mix Designs	
	10.3.5 Details of QC Test conducted during the month	
11	CORRESPONDENCE	
12	NON-CONFORMANCE REPORT	
13	WEATHER REPORT	
14	ACCIDENT REPORT	
15	ROAD MAINTENANCE AND SAFETY REPORT	
16	PROJECT PROGRESS PHOTOGRAPHS	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

PROJECT ROAD LOCATION MAP / INDEX MAP

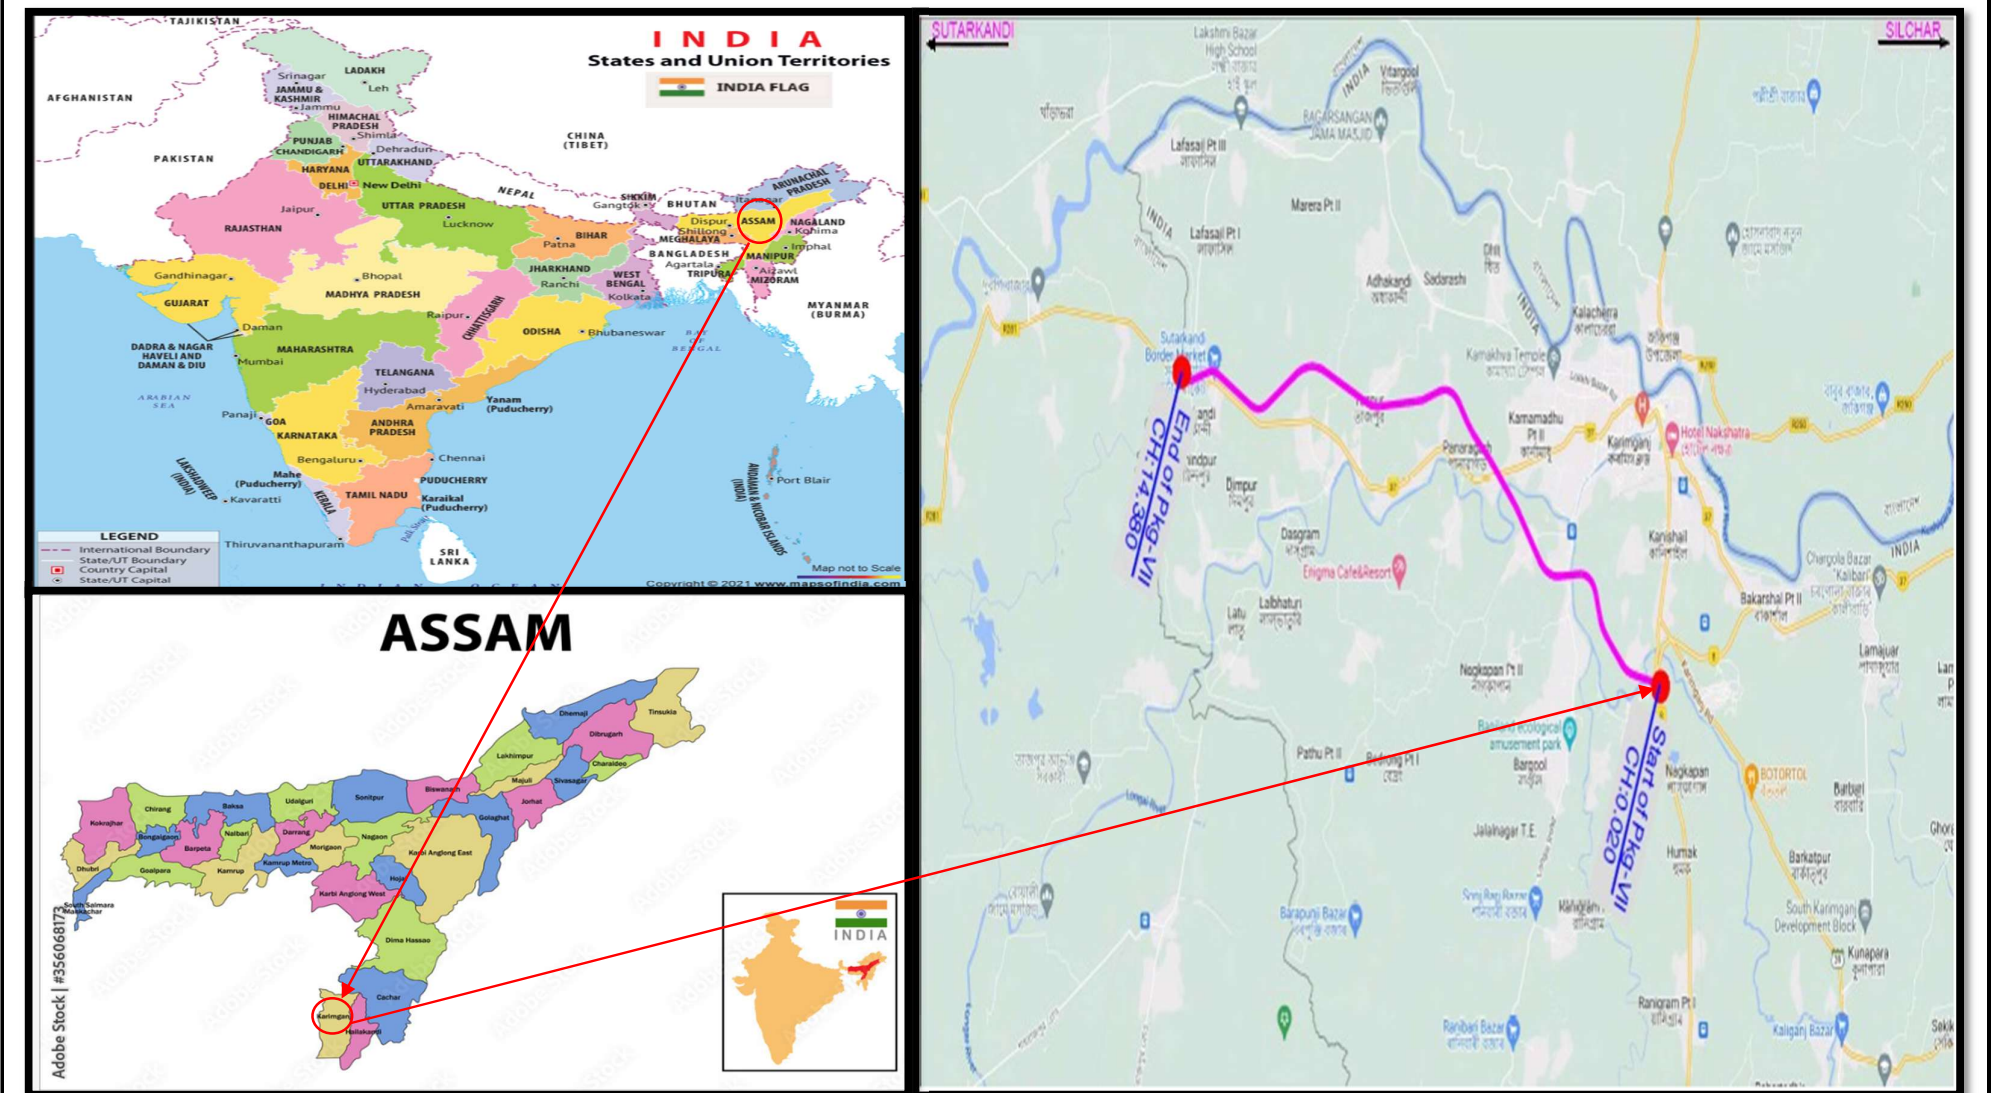

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

EXECUTIVE SUMMARY

The Concessionaire has signed the Concession Agreement with National Highway Infrastructure Development Corporation Limited (NHIDCL) on dated September 17, 2024. This Executive Summary presents the works progress of the Project Highway during the construction period from February 28, 2025 to February 27, 2027.

1. The Project Road:

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

2. Mobilization:

The Concessionaire has mobilized the required Engineers/ Staff Personnel, Machineries/Equipment's, Plants and established main Base Camp at CH: - 5+600 LHS (Darakona).

The details of Key staff personnel deployed are highlighted in the Chapter-6 of this report. The details of deployed Plants and Machineries are included in Chapter-7 of this report.

3. Pre-Construction Activity:

The Details of pre-construction activities have been included in Chapter-5 of this report.

4. EPC Contractor:

MKC Infrastructure Limited

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

The Details of project highway works have been included in Chapter-09 of this report.

1. Design and Drawing

The status of approval of Working Drawings for road works and structures submitted to Authority as on dated 31-05-2025 is given below.

Sr. No.	Description	UoM	Scope	Submitted	Approved	Balance	Remarks
1.	Plan & Profile (MCW)	Km.	14.360	14.360	0.00	14.360	
2.	Plan & Profile (SR)	Km.	4.16	0.00	0.00	4.16	
3.	RE Wall	SqM.	24984	0.00	0.00	24984.00	
4.	ROB	Nos.	1.00	0.00	0.00	1.00	
5.	Major Bridge	Nos.	3.00	0.00	0.00	3.00	
6.	Minor Bridge	Nos.	8.00	0.00	0.00	8.00	
7.	Underpasses	Nos.	16.00	4.00	0.00	16.00	
8.	Culvert	Nos.	72.00	16.00	0.00	72.00	

The details of design and drawing status have been included in this report on Chapter 8.

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

7. Work Program:

At the time of commencement of works, the Concessionaire submitted the Stage wise completion schedule Work Program Vide Letter No. MKCIL/ASSAM/PKG-07/162, dated 17.04.2025 for Authority/IE's approval. Based on the monthly works plan, the works is being carried out by the Concessionaire.

8. Quality Control and Material:

The works is being carried out by the Concessionaire as per Quality Assurance Plan submitted to Authority Vide Letter MKCIL/ASSAM/PKG-07/139 on dated 07.04.2025. Each construction activity is being checked/verified as per the RFI's submitted to Authority/IE by the Concessionaire.

9. Supervision and Monitoring of Project works:

The Authority/ IE along with the concessionaire is supervising and monitoring the execution of works as per requirements of Standard/ Specifications. The monitoring of works is being carried out through the RFI submitted by the Concessionaire and its approval/ rejection after necessary checking/ verification by the Authority/ IE.

10. Site Visit and Meeting:

The Authority/ IE Engineers are regularly visiting the Project Highway.

11. Schedule Completion Date:

As per Schedule-G of the Concession Agreement shall occur on the 730th day from the Appointed Date. The declared Appointed Date being February 28, 2025, the Scheduled completion Date shall occur on February 27, 2027.

12. Operation and Maintenance (O&M):

O&M Obligations – During Operation Period, the Concessionaire shall operate and maintain the project in accordance with this Agreement either by itself, or through the O&M Contractor and if required, modify repair or otherwise make improvements to the Project to comply with the provisions of this Agreement, Applicable Laws and Applicable Permits, and conform to Specifications and Standards and Good industry Practice. The obligations of the concessionaire shall be as per Article 17.

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

13. Area of Concern/ Availability of site for work:

Procurement of ROW- The existing ROW and the stretches of 11.510 km. are subjected to following:

a) Stretches/ Hindered Free Land 11.51 Km out of 14.36 Km:

Stretches/ Hindered Free Land				Encumbrances/ Hindered Land		
Sr. No.	Side	Length (Km)	%	Side	Length (Km)	%
1.	BHS	11.510	80.20%	BHS	2.850	19.80%

b) Hindered due to Tree Cutting:

Description	Total Nos.	Impacted Length (km)	Remarks
Total Trees	407	7.0	

c) Encumbrances due to Religious Structure:

Sr. No.	Types	Chainage	Side	Remarks
1.	Small Temple	2+750	RHS	
2.	Temple	4+150	LHS	
3.	Kabristan	4+300	BHS	
4.	Masjid	4+500	BHS	
5.	Kabristan	7+300	BHS	

d) Details of Hidered Land:

Sr. No.	Issue Description	Side	Chainage		Length Affected (Km)	Remarks
			From	To		
1.	Brick industry	BHS	0+300	0+400	0.100	
2.	Residential House	BHS	2+700	2+900	0.200	
3.	Assam Type House & Shade	BHS	2+900	3+000	0.100	
4.	Assam Type Residential House	BHS	3+800	4+200	0.400	
5.	RCC & Assam type House	BHS	4+200	4+500	0.300	
6.	Assam/ RCC Type Houses	LHS	5+500	5+600	0.100	
7.	Assam Type Residential House	RHS	5+600	5+650	0.050	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

8.	Assam Type Residential House	LHS	6+600	6+650	0.050	
9.	Assam Type Residential House	RHS	7+200	7+300	0.100	
10.	Assam Type Residential House	BHS	9+300	9+370	0.070	
11.	Assam Type Residential House	RHS	9+370	9+400	0.030	
12.	Assam Type Residential House	BHS	11+250	11+400	0.150	
13.	Assam type/ RCC Residential Building	BHS	11+900	12+000	0.100	
14.	Assam type/ RCC Residential Building	RHS	12+200	12+700	0.500	
15.	Assam type/ RCC Residential Building	BHS	12+700	12+900	0.200	
16.	Assam type/ RCC Residential Building	BHS	13+200	13+600	0.400	
Total Hindered Land					2.850	

CHAPTER-1

INTRODUCTION

General

The NHIDCL proposes to implement the development, maintenance, and management of the Spur from NH-8 near Karimganj to Sutarkandi (India-Bangladesh border) Km. 0.020 to Km. 14.380 into 4-lane access controlled corridor. The proposed project road has been selected to improve connectivity and reduce travel time from Assam to Tripura. Also, this connectivity will improve international road connectivity between India and Bangladesh. To achieve the above task, NHIDCL has appointed M/s. Aarvee Associates Architects Engineers and Consultants Pvt. Ltd. The Letter of Acceptance was communicated vide letter No. NHIDCL / Assam / DPR / SilcharChuraibari /222542/ 2581 and the agreement was signed on September 1st, 2023.

This executive summary is submitted along with the Final detailed project report to cover the key aspects of the project.

Project Overview

As described earlier the project road is a spur to NH-8 near Karimganj and ends at Sutarkandi. The proposed alignment passes through Karimganj district in the state of Assam connecting villages Karimganj, Fakirabazar, Jarpata and Sutarkandi.

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

CHAPTER-2

CONTRACT DATA

Sr. No.	Items	Description
1.	Name of Project	4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.
2.	Project Length	14.250 km
3.	Project Bid Cost	380.26 Cr.
4.	Authority	National Highways & Infrastructure Development Corporation Limited
5.	Independent Engineer	M/s Technocrats Advisory Services Private Limited in association with M/s MAV Associates LLP
6.	Concessionaire	MKC Badarpur Churaibari Kamakhya (PKG-7) Highways Private Limited
7.	Design Consultant	Geo Designs & Research Pvt. Ltd.
8.	DPR Consultant	Aarvee Associates Architects Engineers & Consultants Pvt. Ltd.
9.	LOA No. & Date	NHIDCL/ Assam/ NH-37/ Sil-Churai/ Pkg-VII/ 233357/ 3087 dated 11.03.2024
10.	Date of Concession Agreement	September 17, 2024
11.	Appointed Date	February 28, 2025
12.	Construction Period	730 days (from Appointed Date) [24-Months]
13.	Schedule Completion Date	February 27, 2027
14.	O&M Period	15 Years from the date of COD

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

14	Project Milestone	
	Milestone- I	The Project Milestone-I shall occur on the date falling on the 256th (two hundred and fifty sixth) day from the Appointed Date (i.e., February 28, 2025)- (The concessionaire shall have expended not less than 20% of the total capital cost set forth in the Financial Package and the Concessionaire shall have commenced construction of the Project and achieved 20% Physical Progress)
	Milestone- II	438th Day from Appointed Date (i.e., February 28, 2025)- (Prior to the occurrence of Project Milestone-II, the Concessionaire shall have expended not less than 35% of the total capital cost set forth in the Financial Package. Provided, however, that at least 70% of the expenditure referred to hereinabove shall have been incurred on physical works which shall not include advances of any kind to any person or expenditure of any kind on plant and machinery and the concessionaire shall have commenced construction of the project and achieved 35% Physical Progress.).
	Milestone- III	620th Day from Appointed Date (i.e., February 28, 2025) (The concessionaire shall have commenced construction of all Project Facilities and expended not less than 75% of the total capital cost set forth in the Financial Package and the concessionaire shall have commenced construction of the Project and achieved 75% Physical Progress).
	Scheduled Completion Date	730th Day from Appointed Date (i.e., February 27, 2025) The concessionaire shall have completed the Project in accordance with the Concession Agreement.

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

CHAPTER -3

SALIENT FEATURES OF PROJECT HIGHWAY

3.1 Pavement Composition (For Main Carriage Way/ Service Road)

Section	Design Chainage		Stretch in Km.	Pavement Composition in mm.						
	From	To		Sub-Grade	R-GSB	R-WMM	DBM	BC	DLC	PQC
MCW	00+020	12+900	12.880	500.00	200.00	180.00	50.00	40.00	-	-
	12+900	14+380	1.480	500.00	200.00	-	-	-		
				Sub-Grade	GSB	R-WMM	DBM	BC		
Service Road				500.00	200.00	180.00	50.00	30.00		

3.2 Details of New/ Widening of Structures and Project Facilities to be constructed along the project Highway:

Sr. No.	Description		Unit	As per CA	Remarks
1.	Road over Bridge	New Construction	Nos.	1	
2.	Major Bridge	New Construction	Nos.	3	
3.	Minor Bridge	New Construction	Nos.	7	
		Reconstruction	Nos.	1	
4.	VUP	New Construction	Nos.	2	
5.	LVUP	New Construction	Nos.	9	
6.	SVUP	New Construction	Nos.	1	
7.	Box Underpass	New Construction	Nos.	4	
8.	Box Culvert	New Construction	Nos.	28	
		Reconstruction	Nos.	4	
9.	Hume Pipe Culvert	New Construction	Nos.	20	
10.	Bus Bay		Nos.	2	
11.	Major Junction		Nos.	2	
12.	Minor Junction		Nos.	4	
13.	W-beam Single faced metal crash barrier		Rmt.	17602	
14.	Drain (covered)		Rmt.	2960	

CHAPTER -4

SCOPE OF THE WORKS AND PROJECT FACILITIES

4.1 Scope of Works

The Schedule-B of the Concession Agreement specifies the scope of works. The broad scope of the works includes the following:

- Reconstruction of existing 2 lane carriageway to 4 lane divided carriageway including strengthening existing carriageway by providing bituminous overlays in accordance with the Specifications and Standards.
- Construction of 1- ROB, 3- Major Bridge, 8- Minor Bridge, 16- Underpasses, 52- Culverts.
- Construction of Slip Road of 4.16 Km

4.2 Project Facilities

The Schedule-C of the Concession Agreement specifies the project facilities to be constructed for the project highway. The project facilities include the following:

- a) Toll Plaza
- b) Roadside Furniture
 - i. Kilometer and Hectometer Stones
 - ii. Traffic Signs
 - iii. Overhead Sign
 - iv. Road Marking
 - v. Road Delineators
 - vi. Reflective Pavement Markers & Solar Studs
 - vii. Traffic Impact Attenuators
 - viii. Boundary wall and Fencing
- c) Operation and Maintenance centres
- d) Way side Amenities/ Service Areas
- e) Truck Lay-byes
- f) Bus Bay and Bus Shelter
- g) Pedestrian Facilities
- h) Highway Lighting
- i) Rainwater Harvesting
- j) Environmental Management Plan
- k) Land Scaping and Tree Plantation
- l) Advanced Traffic Management System (ATMS)
- m) Highway Petrol Unit
- n) Emergency Medical Services
- o) Crane Services

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

CHAPTER -5

PRE-CONSTRUCTION ACTIVITIES

5.1 Obligations

Obligations of Authority-

Sr. No.	Clause No.	Obligation	Status	Remark/ Reference
1	Clause 4.1.2	Condition Precedent	Done	
2	Article 11	Utilities, Associated Roads and Trees	In Progress	
3	Clause 18.1.2	Safety Consultant	TBA	
4	Article 21	Appointment of Independent Engineer	Done	Awaited for Authority letter
5	Clause 10.3	Joint Memorandum	Done	

Obligations of Concessionaire-

Sr. No.	Clause No.	Obligation	Status	Remark/ Reference
1	Clause 9.1	Performance Security	Done	
2	Article 11	Shifting and Relocation Electrical Utilities	In Progress	
3	Article 26	Insurance	Done	
4	Clause 4.1.3 (Schedule-E)	Applicable Permits	Done	
5		A permission of State Govt. for boulders extraction		
6		Permission of Village Panchayet and Pollution Board for installation of crushers	Done	
7		License for use of explosives	N/A	
8		Permission of the State Govt. from drawing water from river/ reservoir	N/A	
9		Any other permits or clearance	In progress	
10		Labour Licence	Done	
11	Clause 12.1	Quality Assurance Plan	Done	MKCIL/ASSAM/PKG-07/139 dt. 07.04.2025
11		Construction Methodology	Done	MKCIL/ASSAM/PKG-07/150 dt. 14.04.2025

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

5.2 Shifting of Utilities

The project works includes shifting/relocation of various utility services along the project road. The details of the utilities/ Hindrances are required to be shifted/ relocated/ removed along the Project Highway is summarized below:

Sl. No.	Utility/ Hindrance Type	Unit	Nos.	Remarks
1.	HT/ LT Lines (including Transformer if any)	Nos.	88.00	
2.	HT/ LT crossing	Nos.	65.00	
3.	Water Pipelines	Kms	4.00	
4.	Water Pipeline Crossing	Nos.	14.00	

5.3 Tree Cutting

The tree cutting status is given below for the project highway.

Sr. No.	Description	Total	Remarks
1.	Total Number of Trees	407.00	
2.	Total Felling of Trees	7.00	
3.	Balance Trees	400.00	

5.4 Land Acquisition

The detailed working of Existing ROW, Proposed ROW and Land to be Acquired along the project highway are submitted by NHIDCL vide Joint Handover Memorandum on dated 28th of February ,2025.

The detail of affected area for construction of the project road including various project facilities which requires prime attention to accelerate the work progress is given below.

HINDRANCE LIST – CHAINAGE WISE DETAILS

Sr. No.	Issue Description	Side	Chainage		Length Affected (Km)	Remarks
			From	To		
1.	Brick industry	BHS	0+300	0+400	0.100	
2.	Residential House	BHS	2+700	2+900	0.200	
3.	Assam Type House & Shade	BHS	2+900	3+000	0.100	
4.	Assam Type Residential House	BHS	3+800	4+200	0.400	
5.	RCC & Assam type House	BHS	4+200	4+500	0.300	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

6.	Assam/ RCC Type Houses	LHS	5+500	5+600	0.100	
7.	Assam Type Residential House	RHS	5+600	5+650	0.050	
8.	Assam Type Residential House	LHS	6+600	6+650	0.050	
9.	Assam Type Residential House	RHS	7+200	7+300	0.100	
10.	Assam Type Residential House	BHS	9+300	9+370	0.070	
11.	Assam Type Residential House	RHS	9+370	9+400	0.030	
12.	Assam Type Residential House	BHS	11+250	11+400	0.150	
13.	Assam type/ RCC Residential Building	BHS	11+900	12+000	0.100	
14.	Assam type/ RCC Residential Building	RHS	12+200	12+700	0.500	
15.	Assam type/ RCC Residential Building	BHS	12+700	12+900	0.200	
16.	Assam type/ RCC Residential Building	BHS	13+200	13+600	0.400	
Total Hindered Land					2.850	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

CHAPTER -6


MOBILIZATION

6.1 Manpower Mobilization of Concessionaire

Sr. No.	Name of Employee	Designation	Department	Remarks
1	Ashish Kumar Pandey	Project Manager	Project	
2	Dhirendra Thapa	Asst. Manager	HR/Admin	
3	Golu Meena	Supervisor (Mess)	HR/Admin	
4	Deepak Sharma	Executive	Liaison	
5	Shyambabu Singh	Manager	Liaison	
6	Jagdish Pandey	Asst. Manager	Billing and Planning	
7	Bishwajit Santra	Manager	QA/QC	
8	Vageesh Tripathi	Senior Engineer	Structure	
9	Ranjan Kumar	Senior Engineer	Structure	
10	Ajitesh Shukla	Engineer	Structure	
11	Sujit Kumar Ray	Sr. Supervisor	Structure	
12	Ankit Chaurasia	Supervisor	Structure	
13	Avnish Kumar Pandey	Dy. Manager	Highway	
14	Samarjeet Singh	Engineer	Highway	
15	Tapas Basak	Engineer	Highway	
16	Jay Prakash Singh	Senior Supervisor	Highway	
17	Anmol	Supervisor	Highway	
18	Sadanand Yadav	Engineer	Highway	
19	Md. Mohbub Ahmed	Supervisor	Highway	
20	Imrat Ahirwar	Supervisor	Highway	
21	Krishna Singh	Supervisor	Highway	
22	Jayanta Mallick	Sr. Surveyor	Survey	
23	Amit Singh	Surveyor	Survey	
24	Subrata Dinda	Sr. Manager	P & M	
25	Ramkaran Sahu	Engineer	P & M	
26	Deepak Thakur	Executive	P & M	
27	Amit Bhadoria	Executive	Mechanical	
28	Amit Tiwari	Supervisor	P & M	
29	Alok Kumar Singh	Jr. Executive	Store	
30	Vishal Kumar	Supervisor	Store	
31	Ankit Kumar	Executive	Store	
32	Amit Dhara	Executive	Store	
33	Kapil Sharma	Executive	Accounts	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

6.2 Organization Chart of Concessionaire

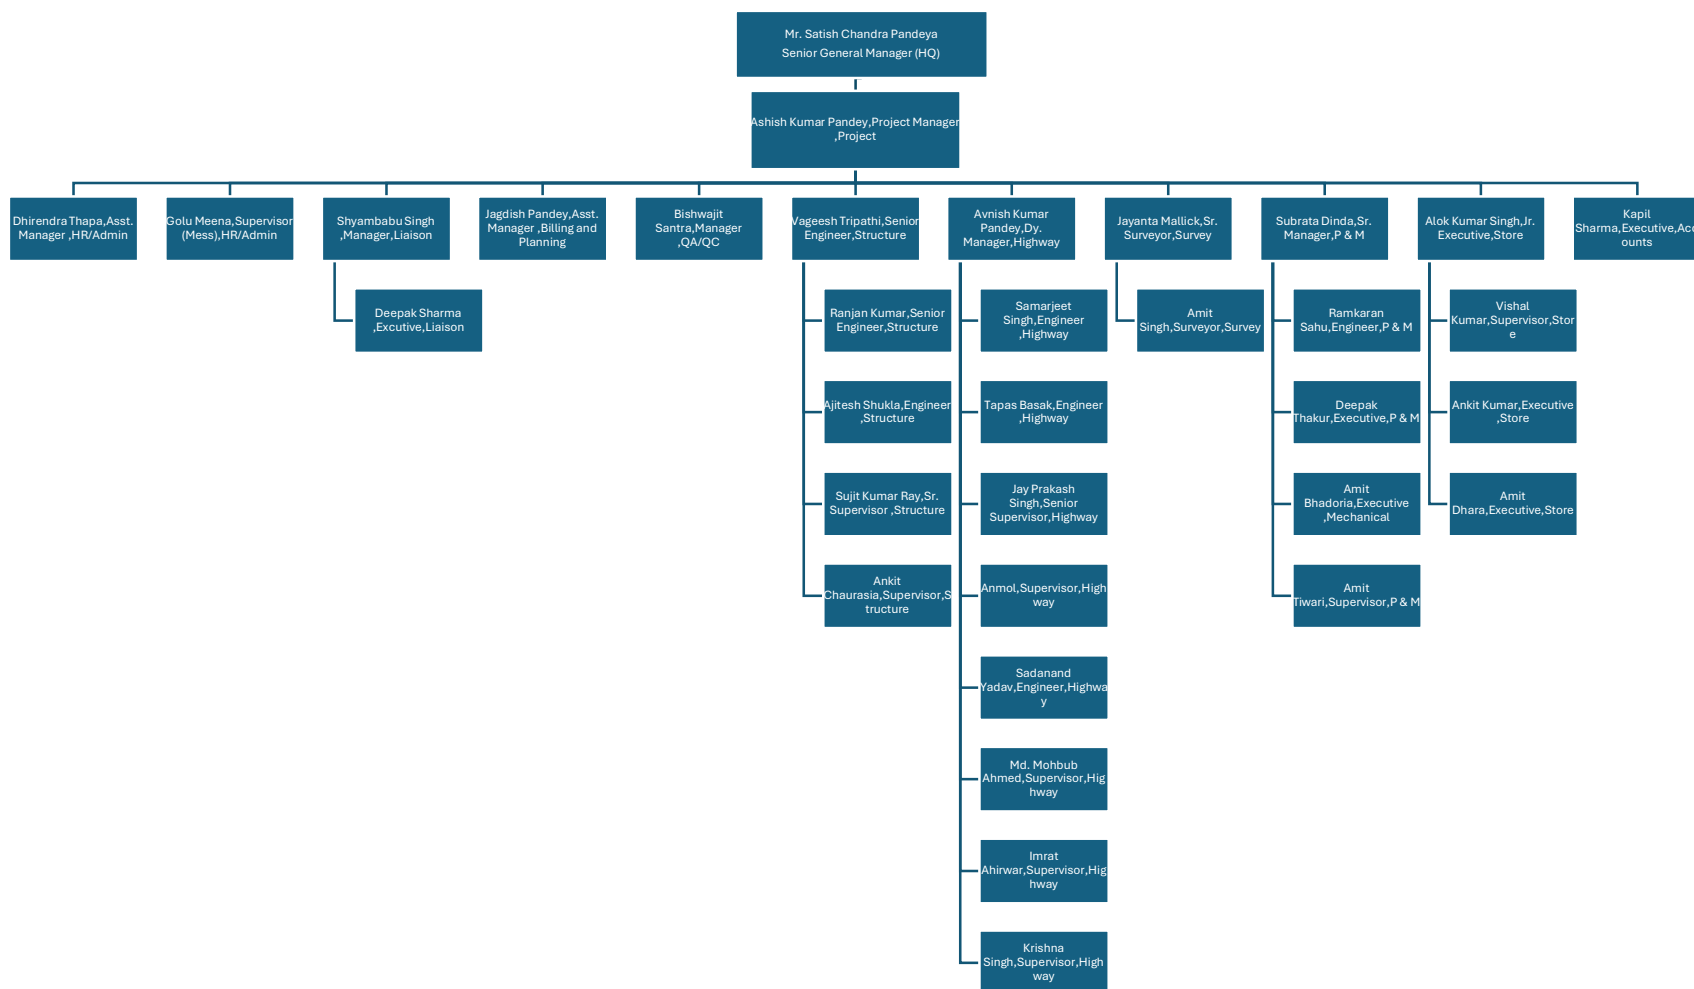

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

CHAPTER-7

DEPLOYMENT OF PLANTS AND EQUIPMENT / PROJECT SET UP PLAN

7.1 Plants and Equipment Deployed

Sr. No.	Type of Machine	Make	Model	Year of Manufacturing	Remarks
1.	Soil Compactor	HAMM	HC119i	2025	
2.	Soil Compactor	HAMM	HC119i	2025	
3.	Soil Compactor	HAMM	HC119i	2025	
4.	Soil Compactor	HAMM	HC119i	2025	
5.	Cement Silo	Schwing Stetter			
6.	Cement Silo	Schwing Stetter			
7.	Cement Silo	Schwing Stetter			
8.	RMC Plant	Schwing Stetter	HO.75NG		
9.	DG-125 kva	Kirloakar			
10.	DG-25 kva	Kirloskar		2024	
11.	Crusher	Puzzolana	TRAC SCREEN/PTS1552		
12.	Excavator	Hyundai	R215L SMART PLUS		
13.	Excavator	Hyundai	R215L SMART PLUS		
14.	Excavator	Hyundai	R215L SMART PLUS		
15.	Mobile Crusher	Propel	SC TMC-Q- 250/250TPH CONE		
16.	Mobile Crusher	Propel	SC TMJ-811 S/250 TPH JAW		

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

CHAPTER-8

DESIGN AND DRAWING

The project highway has been designed for four lane divided carriageway facility with provision of central raised median of 1.6m. The Concession Agreement envisages design of the project highway by the Concessionaire. The scope of design includes the design for road works, structure works and other project facilities. The drawings need to be prepared and approved for execution of each component of the project highway.

8.1 Design

The design of road works e.g., plans and profiles, cross sections and other miscellaneous items are being prepared by the Concessionaire for approval and execution of works accordingly. Similarly, the design of various structures e.g., Major bridge, Minor bridges, Vehicular Underpasses, Box Culverts, Hume Pipe Culverts etc. are also being prepared by the Concessionaire for review by Authority/ IE.

8.2 Drawings

As per requirement of the Contract Agreement various drawings are being prepared for execution and completion of the works. The working drawings of road works and structure works are being prepared by the Concessionaire and submitted to the Authority/ Independent Engineer prior to execution of works at site.

8.3 Status of Approval of Drawings

The status of drawing submission and approval of GAD for road and structure works as on March 31, 2025, is enclosed in this chapter of the report.

Road Works

S N	Description	Unit	Total	Submitted	Approval	Review Balance	Remarks
1.	Plan & Profile MCW	Km	14.360	14.360	0.000	14.360	
2.	Plan & Profile SR	Km	4.164	4.164	0.000	4.164	
3.	Typical Cross Section	Nos	1.00	1.00	0.00	1.00	
4.	Pavement Design Report	Nos	1.00	1.00	0.00	1.00	
5.	RE Wall	Nos	20820.00	-	-	-	
6.	Major Junction	Nos	2.00	-	-	-	
7.	Minor Junction	Nos	4.00	-	-	-	
8.	Bus Bay Drawing	Nos	2.00	-	-	-	
9.	Road Signage Plan	Km	14.360	-	-	-	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

Structure Works

S N	Type of Str.	Ch.	Span Arrangement	Submission Letter No.	Date	Status	IE Letter No.	Date	Remarks
1	Box Culvert	00+043	1 x 3.0						
2	Box Culvert	00+207	1 x 3.0	MKCIL/ASSAM/ PKG-07/136	05-04-2025				
3	Box Culvert	00+341	1 x 3.0	MKCIL/ASSAM/ PKG-07/136	05-04-2025				
4	Box Culvert	01+254	1 x 2.0	MKCIL/ASSAM/ PKG-07/135	05-04-2025				
5	Box Culvert	01+652	1 x 2.0	MKCIL/ASSAM/ PKG-07/134	05-04-2025				
6	Box Culvert	01+973	1 x 2.0	MKCIL/ASSAM/ PKG-07/134	05-04-2025				
7	Box Culvert	02+143	1 x 2.0	MKCIL/ASSAM/ PKG-07/134	05-04-2025				
8	Box Culvert	02+440	1 x 2.0	MKCIL/ASSAM/ PKG-07/135	05-04-2025				
9	Box Culvert	03+418	1 x 2.0						
9a	SR	03+418	1 x 2.0						
10	Box Culvert	03+646	1 x 2.0	MKCIL/ASSAM/ PKG-07/134	05-04-2025				
11	Box Culvert	03+925	1 x 2.0						
11a	SR	03+925	1 x 2.0						
12	Box Culvert	04+018	1 x 5.0	MKCIL/ASSAM/ PKG-07/186	05-05-2025				
12a	SR	04+018	1 x 5.0	MKCIL/ASSAM/ PKG-07/186	05-05-2025				
13	Box Culvert	04+340	1 x 3.0	MKCIL/ASSAM/ PKG-07/136	05-04-2025				
14	Box Culvert	04+847	1 x 2.0						
15	Box Culvert	05+126	1 x 2.0	MKCIL/ASSAM/ PKG-07/135	05-04-2025				
16	Box Culvert	05+920	1 x 2.0	MKCIL/ASSAM/ PKG-07/140	07-04-2025				
17	Box Culvert	06+190	1 x 2.0	MKCIL/ASSAM/ PKG-07/140	07-04-2025				
18	Box Culvert	06+642	1 x 3.0						
19	Box Culvert	07+668	1 x 2.0	MKCIL/ASSAM/ PKG-07/179	29-04-2025				
20	Box Culvert	07+832	1 x 2.0	MKCIL/ASSAM/ PKG-07/140	07-04-2025				
21	Box Culvert	08+188	1 x 2.0	MKCIL/ASSAM/ PKG-07/185	05-05-2025				
22	Box Culvert	08+576	1 x 2.0	MKCIL/ASSAM/ PKG-07/185	05-05-2025				
23	Box Culvert	09+543	1 x 2.0	MKCIL/ASSAM/ PKG-07/179	29-04-2025				
24	Box Culvert	09+779	1 x 2.0	MKCIL/ASSAM/ PKG-07/179	29-04-2025				
25	Box Culvert	10+529	1 x 2.0	MKCIL/ASSAM/ PKG-07/179	29-04-2025				
26	Box Culvert	11+073	1 x 2.0	MKCIL/ASSAM/ PKG-07/179	29-04-2025				
27	Box Culvert	11+921	1 x 2.0	MKCIL/ASSAM/ PKG-07/179	29-04-2025				
27a	SR	11+921	1 x 2.0	MKCIL/ASSAM/ PKG-07/179	29-04-2025				
28	Box Culvert	12+223	1 x 2.0						
29	Box Culvert	12+663	1 x 2.0	MKCIL/ASSAM/ PKG-07/140	07-04-2025				

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

29a	SR	12+663	1 x 2.0	MKCIL/ASSAM/ PKG-07/140	07-04-2025				
30	Box Culvert	13+065	1 x 2.0	MKCIL/ASSAM/ PKG-07/140	07-04-2025				
31	Box Culvert	13+380	1 x 2.0	MKCIL/ASSAM/ PKG-07/140	07-04-2025				
32	Box Culvert	13+740	1 x 2.0						
1	MNB	00+742	1x20						
2	MNB	01+768	1x15	MKCIL/ASSAM/ PKG-07/159	17-04-2025				
3	MNB	06+313	1x15						
4	MNB	07+306	1x6	MKCIL/ASSAM/ PKG-07/159	17-04-2025				
5	MNB	09+003	1x6	MKCIL/ASSAM/ PKG-07/159	17-04-2025				
6	MNB	09+293	1x6	MKCIL/ASSAM/ PKG-07/159	17-04-2025				
7	MNB	11+363	2x10						
8	MNB	14+195	1x12	MKCIL/ASSAM/ PKG-07/159	17-04-2025				
1	MJB	00+526	3x35						
2	MJB	02+880	3x37.5	MKCIL/ASSAM/ PKG-07/097	21-03-2025				Test Pile
3	MJB	05+322	3x37.5	MKCIL/ASSAM/ PKG-07/040 MKCIL/ASSAM/ PKG-07/052	21-01-2025 31-01-2025				Test Pile
1	ROB	04+624	1x20+2x37.28+ 1x20	MKCIL/ASSAM/ PKG-07/218					Pile mark P1,P2,P3 are submitted
1	Box Underpass	02+340	1x4	MKCIL/ASSAM/ PKG-07/147	10-04-2025				
2	Box Underpass	04+534	1x4	MKCIL/ASSAM/ PKG-07/146	10-04-2025				
3	Box Underpass	07+906	1x4	MKCIL/ASSAM/ PKG-07/147	10-04-2025				
4	Box Underpass	08+296	1x4	MKCIL/ASSAM/ PKG-07/147	10-04-2025				
1	VUP	02+999	1x20						
2	VUP	05+622	1x20						
1	SVUP	03+728	1x7						
1	LVUP	01+142	1x12	MKCIL/ASSAM/ PKG-07/145	10-04-2025				
2	LVUP	03+886	1x12	MKCIL/ASSAM/ PKG-07/141	07-04-2025				
3	LVUP	04+212	1x12	MKCIL/ASSAM/ PKG-07/155	15-04-2025				
4	LVUP	05+414	1x12	MKCIL/ASSAM/ PKG-07/155	15-04-2025				
5	LVUP	07+213	1x12	MKCIL/ASSAM/ PKG-07/065	17-02-2025				
6	LVUP	09+332	1x12	MKCIL/ASSAM/ PKG-07/155	15-04-2025				
7	LVUP	10+098	1x12	MKCIL/ASSAM/ PKG-07/141	07-04-2025				
8	LVUP	10+834	1x18						
9	LVUP	12+310	1x12	MKCIL/ASSAM/ PKG-07/065	17-02-2025				
1	Typical Pre-Cast		1 x 2.0	MKCIL/ASSAM/ PKG-07/055	07-02-2025				

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

CHAPTER-9

PROJECT WORK PROGRESS

9.1 Work Progress:


Progress as per Schedule G for the month May-2025.

Project Name :-	"Four Laning of Karimganj - Sutarkandi section of NH-37 from Design chainage 0.020 (Assam-Agartala Road NH-8 near Kanisail Pt II) to Km. 14.380 (Sutarkandi, India-Bangladesh Border) in the state of Assam (Package-7)".						
Authority Engineer :-	National Highways & Infrastructure Development Corporation Limited						
Independent Engineer :-	M/s Technocrats Advisory Services Pvt. Ltd. in association with M/s MAV Associates LLP						
Concessionaire :-	MKC Badarpur Churaibari Kamakhya (PKG-7) Highways Pvt. Ltd.						
Item	Stage for measurement of Physical Progress	Unit	Qty.	Weightage in percentage to the contract price	Qty.	Physical Progress in %	Finacial Progress in %\
Road works including cutverts, minor bridges, underpasses, overpasses, approaches to ROB/RUB/ Major Bridges/ Structures (but excluding service roads)	B- New 4 Lane Realignment/Bypass						
	(1) Earthwork upto top of Sub-grade	L-Km	27.23	19.59%	-	0.00%	0.000%
	(2) Granular work (Sub-base, base,shoulder)						
	(a) GSB	L-Km	27.23	5.04%	-	0.00%	0.000%
	(b) WMM	L-Km	24.27	2.97%	-	0.00%	0.000%
	(4) Bituminous Work						
	(a) DBM	L-Km	24.274	2.09%	-	0.00%	0.000%
	(b) BC	L-Km	24.27	1.78%	-	0.00%	0.000%
	(5) Rigid Pavement (MCW)						
	(a) DLC	L-Km	2.96	0.38%	-	0.00%	0.000%
	(b) PQC	L-Km	2.96	1.45%	-	0.00%	0.000%
	Sub Total-B						
	C- New Culverts, Minor Bridges, underpasses, overpasses on existing road, realignment, bypasses:						
	1) Culverts	No.	72.00	5.52%	-	0.00%	0.000%
	2) Minor Bridge						
	a) Foundation	No.	8.00	3.00%	-	0.00%	0.000%
	b) Sub-Structure	No.	8.00	1.38%	-	0.00%	0.000%
	c) Super-Structure (including Crash Barrier etc. Complete)						
	i) Girder Type - Precast Girder (40%)	No.	3.00	0.41%	-	0.00%	0.000%
	ii) Girder Type - Cast in situ superstructure (60%)	No.	3.00	0.61%	-	0.00%	0.000%
	iii) Box Type - Cast-in-situ superstructure	No.	5.00	0.87%	-	0.00%	0.000%
	5) Grade Separated Structures						
	a) Underpasses (Box Underpass, SVUP, LVUP, VUP)						
	i) Foundation	No.	16.00	3.55%	1.00	6.25%	0.222%
	ii) Sub-Structure	No.	16.00	2.26%	-	0.00%	0.000%
	iii) Super-Structure (including Crash Barrier etc. Complete)						
	- Girder Type - Precast Girder (40%)	No.	3.00	0.20%	-	0.00%	0.000%
	- Girder Type - Cast in situ superstructure (60%)	No.	3.00	0.30%	-	0.00%	0.000%
	- Box Type - Cast-in-situ superstructure	No.	13.00	1.94%	-	0.00%	0.000%
Major Bridge works and ROB/RUB	C- New Major Bridges						
	(1)Foundation (Pile Foundation)	No.	3.00	6.50%	-	0.00%	0.000%
	(2) Sub-structure	No.	3.00	1.77%	-	0.00%	0.000%
	(3)Super-structure (including crash barriers etc. complete)						
	-Super-structure - Precast Girder (40%)	No.	3.00	1.22%	-	0.00%	0.000%
	-Super-structure - Cast in situ superstructure (60%)	No.	3.00	1.82%	-	0.00%	0.000%
	D- New rail-road bridges						
	(a) ROB						
	(1)Foundation	No.	1.00	2.74%	-	0.00%	0.000%
	(2) Sub-structure	No.	1.00	1.13%	-	0.00%	0.000%
Structures (Elevated Section, Reinforced earth)	(3)Super-structure (including crash barriers etc. complete)						
	-Super-structure - Precast Girder (40%)	No.	1.00	0.98%	-	0.00%	0.000%
	-Super-structure - Cast in situ superstructure (60%)	No.	1.00	1.48%	-	0.00%	0.000%
	4) Reinforced Earth Wall (includes Approaches of ROB,Underpasses, Over passes, Flyover etc.)						
Electrical and Public Health Utilities	i) On Casting (5%)	Sq.m	24,984.00	0.04%	-	0.00%	0.000%
	ii) On Erection (95%)	Sq.m	24,984.00	0.70%	-	0.00%	0.000%
	UTILITY SHIFTING						
	HT/LT lines (including Transformers if any)	Km	4.36	0.04%	1.10	25.23%	0.009%
Other Works	HT/LT crossings	No.	65.00	1.00%	18.00	27.69%	0.276%
	Water pipeline	Km	4.65	0.16%	-	0.00%	0.000%
	Water pipeline crossings	No.	14.00	0.36%	-	0.00%	0.000%
	OTHER WORKS						
	i) Service Road / Slip Road	Km	4.16	2.19%	-	0.00%	0.000%
	iii) Road Side Drain						
	a) Line Drain/RCC Cover Drain	L-Km	2.96	0.48%	-	0.00%	0.000%
	b) Unlined Drain	L-Km	22.37	0.06%	-	0.00%	0.000%
	c) Chute Drain	L-Km	5.22	0.05%	-	0.00%	0.000%
	d) Median Drain	Km	5.18	0.13%	-	0.00%	0.000%
	iv) - Road signs,markings, Km Stone, Safety devices						
	(a) Road signs, markings, Km Stone	L-Km	14.36	0.34%	-	0.00%	0.000%
	(b) Concrete Crash Barrier/W Beam Crash Barrier in Road work						
	- Concrete Crash Barrier	Km	13.30	1.27%	-	0.00%	0.000%
	- W Beam Crash Barrier	Km	17.60	1.34%	-	0.00%	0.000%
	v) - Project Facilities						
	(a) Bus bay	No.	2.00	0.04%	-	0.00%	0.000%
	(b) Rain Water Harvesting	No.	28.00	0.18%	-	0.00%	0.000%
	viii) Protection Work						
	(a) Boulder Pitching on Slopes	Km	6.66	6.69%	-	0.00%	0.000%
	(b) Toe Wall / Retaining Wall	Km	13.81	12.11%	-	0.00%	0.000%
	x) Miscellaneous						
	(a) Street Lightning	No.	280.00	0.11%	-	0.00%	0.000%
	(b) Junction/Interchange	No.	6.00	0.23%	-	0.00%	0.000%
	(c) Boundary Wall	L-Km	27.23	0.89%	-	0.00%	0.000%
	(d) ATMS	L-Km	28.72	0.60%	-	0.00%	0.000%
Grand Total :-				100.00%			0.51%

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

9.2 S Curve

S Curve

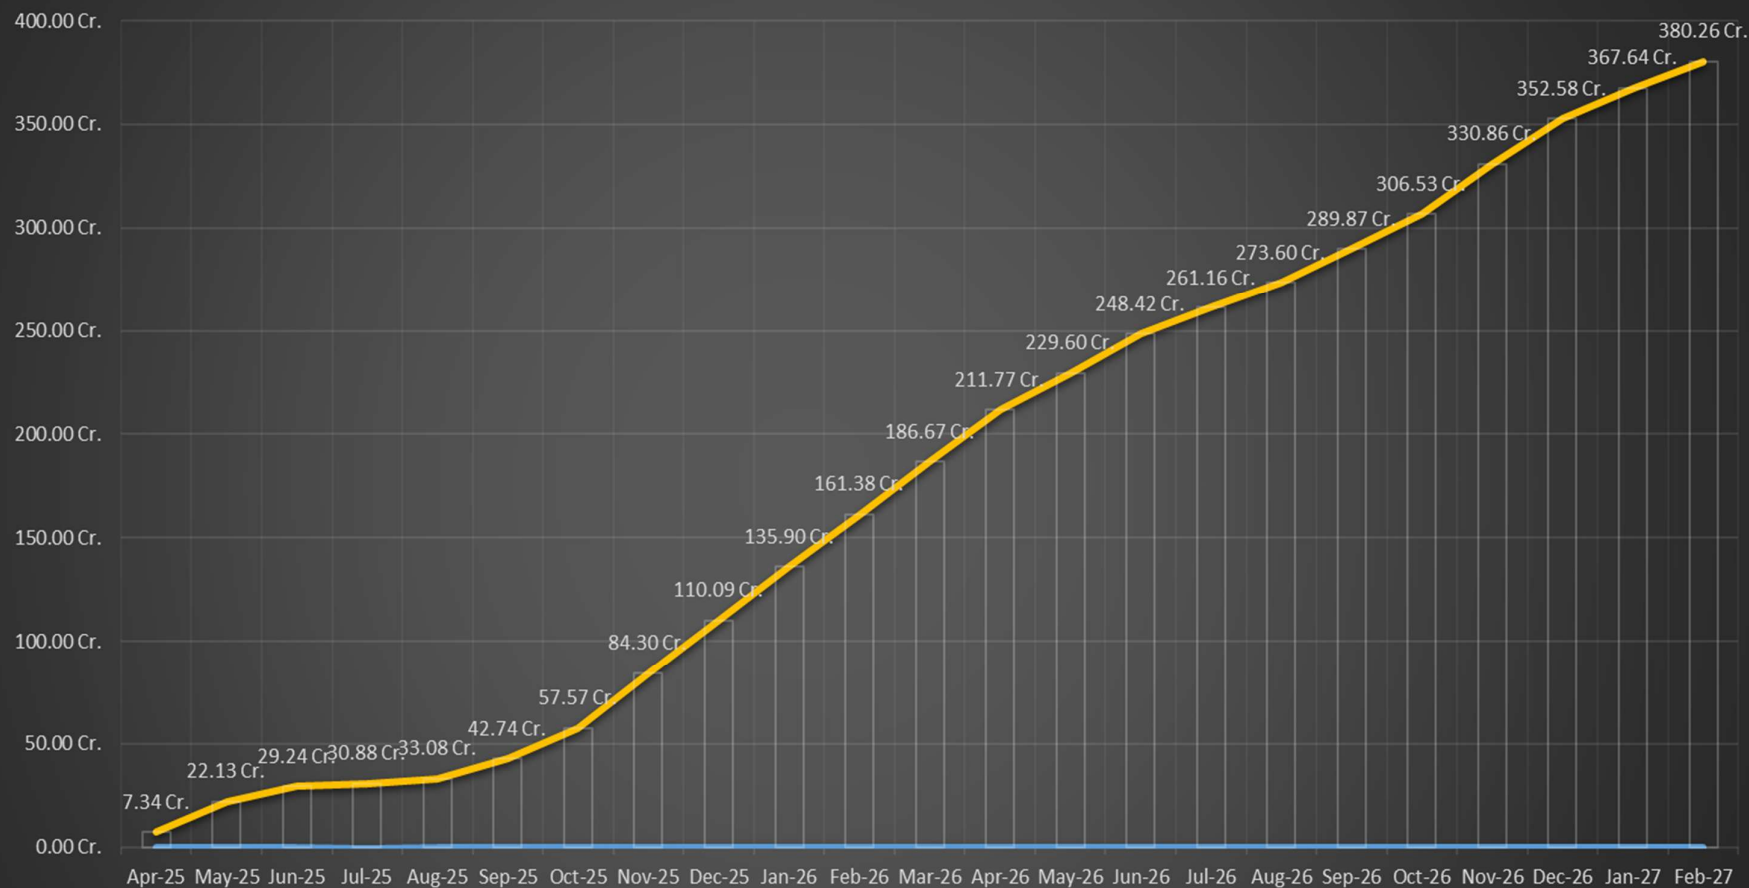


	Apr-25	May-25	Jun-25	Jul-25	Aug-25	Sep-25	Oct-25	Nov-25	Dec-25	Jan-26	Feb-26	Mar-26	Apr-26	May-26	Jun-26	Jul-26	Aug-26	Sep-26	Oct-26	Nov-26	Dec-26	Jan-27	Feb-27
Plan in %	1.93%	3.89%	1.87%	0.43%	0.58%	2.54%	3.90%	7.03%	6.78%	6.79%	6.70%	6.65%	6.60%	4.69%	4.95%	3.35%	3.27%	4.28%	4.38%	6.40%	5.71%	3.96%	3.32%
Cumulative Amount	7.34 Cr	22.13 Cr	29.24 Cr	30.88 Cr	33.08 Cr	42.74 Cr	57.57 Cr	84.30 Cr	110.09 Cr	135.90 Cr	161.38 Cr	186.67 Cr	211.77 Cr	229.60 Cr	248.42 Cr	261.16 Cr	273.60 Cr	289.87 Cr	306.53 Cr	330.86 Cr	352.58 Cr	367.64 Cr	380.26 Cr

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.


9.3 Weightages

Work Description	% of Each sub components	Amount (Cr.)
Sub Grade	19.59%	74,50,23,653.02
Granular Work	8.00%	30,43,19,594.30
Bituminous Work	3.88%	14,73,67,994.90
Rigid Pavement	1.83%	6,97,20,197.81
Culverts	5.52%	20,99,29,557.88
Minor Bridges	6.26%	23,80,73,489.15
Grade Separated Structures	8.25%	31,37,15,716.05
Major Bridge	11.31%	43,00,02,339.39
ROB	6.33%	24,07,16,649.18
RE Wall	0.73%	2,78,77,340.41
Utility Shifting	1.56%	5,92,90,359.01
Slip Road	2.19%	8,34,60,380.79
Road Side Drain & Median Drain	0.73%	2,77,26,745.67
Road Signs, Marking, Km Stone, & etc.	2.94%	11,19,05,564.92
Project Facilities	0.23%	86,55,010.23
Protection Work	18.80%	71,50,69,588.19
Miscellaneous Work	1.83%	6,97,45,819.09
Total	100.00%	3,80,26,00,000.00

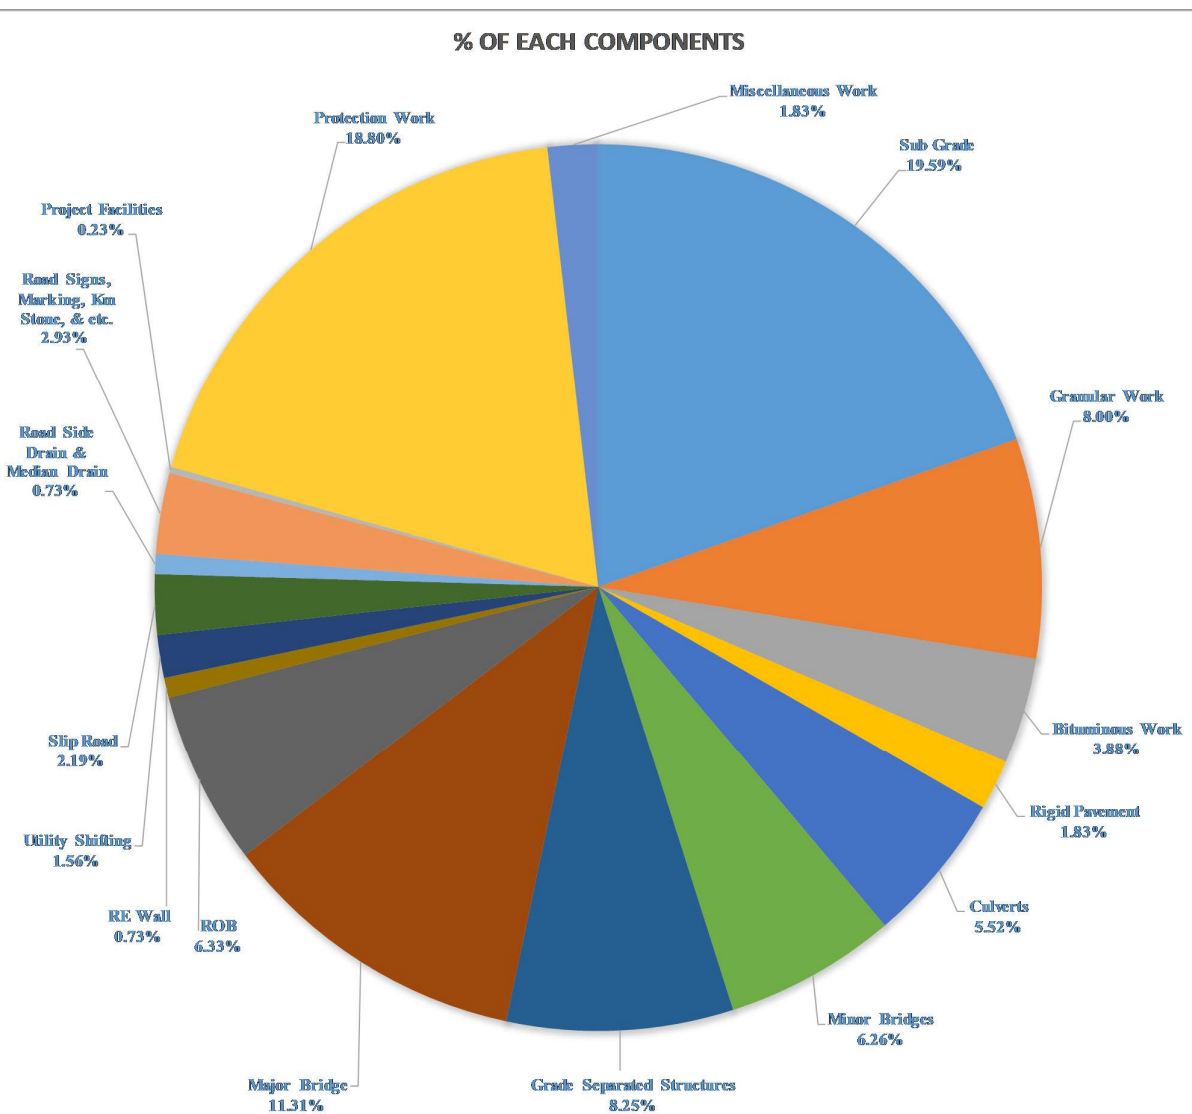

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

9.4 Strip Chart of Highway:

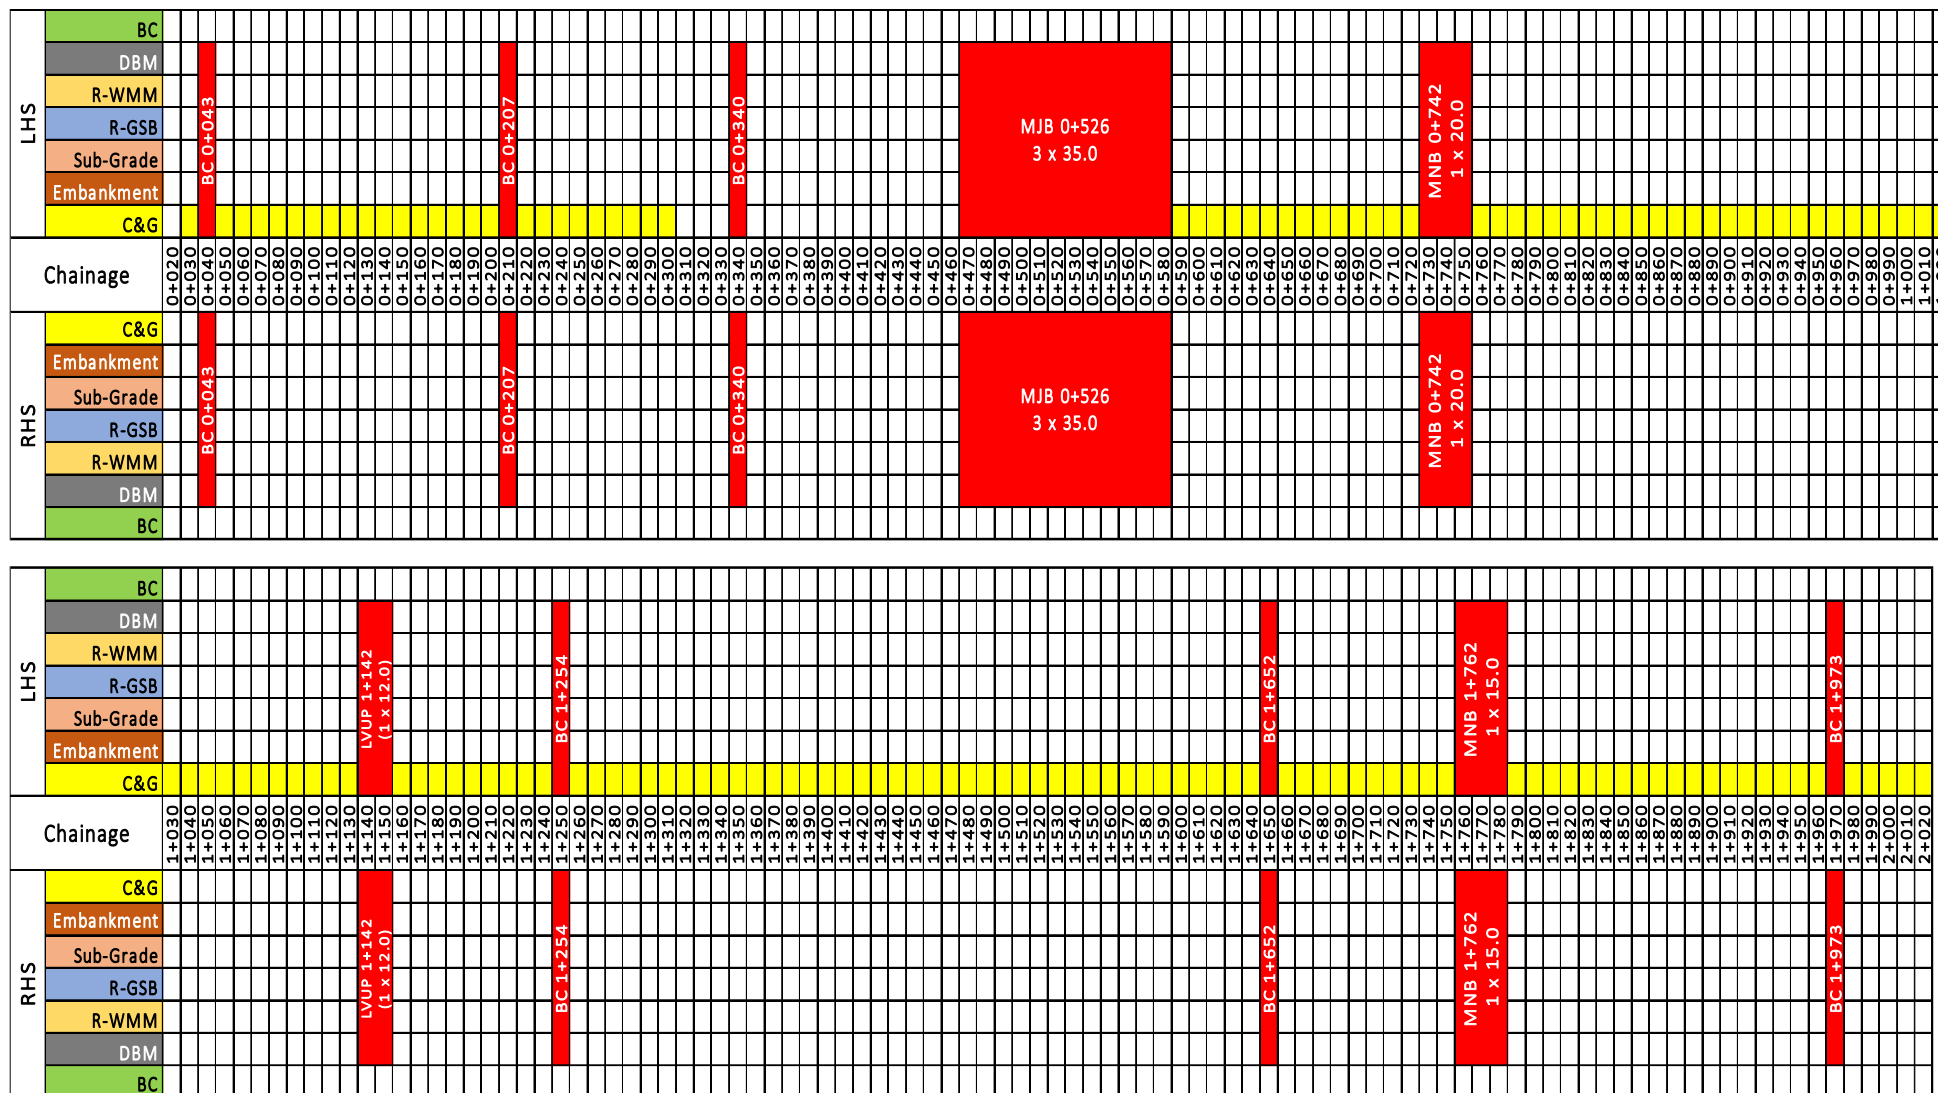

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

RHS	LHS						Chainage																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								
	BC	DBM	R-WMM	R-GSB	Sub-Grade	Embankment		C&G																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
							2+030																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								

RHS	Chainage						LHS																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									
	BC	DBM	R-WMM	R-GSB	Sub-Grade	Embankment																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										
	C&G						C&G																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																									

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

		LHS							RHS						Chainage						LHS																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
		BC	DBM	R-WMM	R-GSB	Sub-Grade	Embankment	C&G							BC	DBM	R-WMM	R-GSB	Sub-Grade	Embankment	C&G																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	
								4+030												4+030																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

LHS	BC	
	DBM	
	R-WMM	
	R-GSB	
	Sub-Grade	
	Embankment	
	C&G	
Chainage		6+030
		6+040
		6+050
		6+060
		6+070
		6+080
		6+090
		6+100
		6+110
		6+120
		6+130
		6+140
		6+150
		6+160
		6+170
		6+180
		BC 6+190
		6+200
		6+210
		6+220
		6+230
		6+240
		6+250
		6+260
		6+270
		6+280
		6+290
		6+300
		6+310
		MNB 6+313 (1x15.0)
		6+320
		6+330
		6+340
		6+350
		6+360
		6+370
		6+380
		6+390
		6+400
		6+410
		6+420
		6+430
		6+440
		6+450
		6+460
		6+470
		6+480
		6+490
		6+500
		6+510
		6+520
		6+530
		6+540
		6+550
		6+560
		6+570
		6+580
		6+590
		6+600
		6+610
		6+620
		6+630
		BC 6+642
		6+640
		6+650
		6+660
		6+670
		6+680
		6+690
		6+700
		6+710
		6+720
		6+730
		6+740
		6+750
		6+760
		6+770
		6+780
		6+790
		6+800
		6+810
		6+820
		6+830
		6+840
		6+850
		6+860
		6+870
		6+880
		6+890
		6+900
		6+910
		6+920
		6+930
		6+940
		6+950
		6+960
		6+970
		6+980
		6+990
		7+000
		7+010
		7+020

LHS	BC	
	DBM	
	R-WMM	
	R-GSB	
	Sub-Grade	
	Embankment	
	C&G	
Chainage		7+030
		7+040
		7+050
		7+060
		7+070
		7+080
		7+090
		7+100
		7+110
		7+120
		7+130
		7+140
		7+150
		7+160
		7+170
		7+180
		7+190
		7+200
		LVUP 7+213 (1x12.0)
		7+210
		7+220
		7+230
		7+240
		7+250
		7+260
		7+270
		7+280
		7+290
		7+300
		MNB 7+306 (1x6.0)
		7+310
		7+320
		7+330
		7+340
		7+350
		7+360
		7+370
		7+380
		7+390
		7+400
		7+410
		7+420
		7+430
		7+440
		7+450
		7+460
		7+470
		7+480
		7+490
		7+500
		7+510
		7+520
		7+530
		7+540
		7+550
		7+560
		7+570
		7+580
		7+590
		7+600
		7+610
		7+620
		7+630
		7+640
		7+650
		7+660
		BC 7+668
		7+670
		7+680
		7+690
		7+700
		7+710
		7+720
		7+730
		7+740
		7+750
		7+760
		7+770
		7+780
		7+790
		7+800
		7+810
		7+820
		BC 7+832
		7+830
		7+840
		7+850
		7+860
		7+870
		7+880
		7+890
		7+900
		7+910
		7+920
		7+930
		7+940
		7+950
		7+960
		7+970
		7+980
		7+990
		8+000
		8+010
		8+020

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

	RHS	Chainage	LHS
	BC	8+030	C&G
	DBM	8+040	Embarkment
	R-WMM	8+050	R-GSB
	R-GSB	8+060	Sub-Grade
	R-WMM	8+070	
	DBM	8+080	
	BC	8+090	
		8+100	
		8+110	
		8+120	
		8+130	
		8+140	
		8+150	
		8+160	
		8+170	
		8+180	BC 8+188
		8+190	
		8+200	
		8+210	
		8+220	
		8+230	
		8+240	
		8+250	
		8+260	
		8+270	
		8+280	
		8+290	
		8+300	
		8+310	
		8+320	
		8+330	
		8+340	
		8+350	
		8+360	
		8+370	
		8+380	
		8+390	
		8+400	
		8+410	
		8+420	
		8+430	
		8+440	
		8+450	
		8+460	
		8+470	
		8+480	
		8+490	
		8+500	
		8+510	
		8+520	
		8+530	
		8+540	
		8+550	
		8+560	
		8+570	BC 8+576
		8+580	
		8+590	
		8+600	
		8+610	
		8+620	
		8+630	
		8+640	
		8+650	
		8+660	
		8+670	
		8+680	
		8+690	
		8+700	
		8+710	
		8+720	
		8+730	
		8+740	
		8+750	
		8+760	
		8+770	
		8+780	
		8+790	
		8+800	
		8+810	
		8+820	
		8+830	
		8+840	
		8+850	
		8+860	
		8+870	
		8+880	
		8+890	
		8+900	
		8+910	
		8+920	
		8+930	
		8+940	
		8+950	
		8+960	
		8+970	
		8+980	
		8+990	
	MNB 9+003 (1x6.0)	9+000	MNB 9+003 (1x6.0)
		9+010	

RHS		Chainage	LHS						
BC	DBM		R-WMM	R-GSB	Sub-Grade	Embankment	C&G		
		9+030							
	C&G	9+040							BC
	Embankment	9+050							DBM
	Sub-Grade	9+060							R-WMM
	R-GSB	9+070							R-GSB
	R-WMM	9+080							Sub-Grade
	DBM	9+090							Embankment
		9+100							C&G
		9+110							
		9+120							
		9+130							
		9+140							
		9+150							
		9+160							
		9+170							
		9+180							
		9+190							
		9+200							
		9+210							
		9+220							
		9+230							
		9+240							
		9+250							
		9+260							
		9+270							
		9+280							
	MNB 9+293 (1x6.0)	9+290						MNB 9+293 (1x6.0)	
		9+300							
		9+310							
		9+320							
	LVUP 9+332 (1x12.0)	9+330						LVUP 9+332 (1x12.0)	
		9+340							
		9+350							
		9+360							
		9+370							
		9+380							
		9+390							
		9+400							
		9+410							
		9+420							
		9+430							
		9+440							
		9+450							
		9+460							
		9+470							
		9+480							
		9+490							
		9+500							
		9+510							
		9+520							
		9+530							
	BC 9+543	9+540						BC 9+543	
		9+550							
		9+560							
		9+570							
		9+580							
		9+590							
		9+600							
		9+610							
		9+620							
		9+630							
		9+640							
		9+650							
		9+660							
		9+670							
		9+680							
		9+690							
		9+700							
		9+710							
		9+720							
		9+730							
		9+740							
		9+750							
		9+760							
		9+770							
	BC 9+779	9+780						BC 9+779	
		9+790							
		9+800							
		9+810							
		9+820							
		9+830							
		9+840							
		9+850							
		9+860							
		9+870							
		9+880							
		9+890							
		9+900							
		9+910							
		9+920							
		9+930							
		9+940							
		9+950							
		9+960							
		9+970							
		9+980							
		9+990							
		10+000							
		10+010							

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

RHS	Chainage	LHS						RHS	Chainage	LHS																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																							
		BC	DBM	R-WMM	R-GSB	Sub-Grade	Embankment			C&G	BC	DBM	R-WMM	R-GSB	Sub-Grade	Embankment	C&G																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																
																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																	</

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

RHS	Chainage	LHS	
		BC	DBM
BC	12+030		
DBM	12+040		
R-WMM	12+050		
R-GSB	12+060		
Sub-Grade	12+070		
Embankment	12+080		
C&G	12+090		
	12+100		
	12+110		
	12+120		
	12+130		
	12+140		
	12+150		
	12+160		
	12+170		
	12+180		
	12+190		
	12+200		
	12+210		
	12+220		
	12+230		
	12+240		
	12+250		
	12+260		
	12+270		
	12+280		
	12+290		
	12+300		
	12+310		
	12+320		
	12+330		
	12+340		
	12+350		
	12+360		
	12+370		
	12+380		
	12+390		
	12+400		
	12+410		
	12+420		
	12+430		
	12+440		
	12+450		
	12+460		
	12+470		
	12+480		
	12+490		
	12+500		
	12+510		
	12+520		
	12+530		
	12+540		
	12+550		
	12+560		
	12+570		
	12+580		
	12+590		
	12+600		
	12+610		
	12+620		
	12+630		
	12+640		
	12+650		
	12+660		
	12+670		
	12+680		
	12+690		
	12+700		
	12+710		
	12+720		
	12+730		
	12+740		
	12+750		
	12+760		
	12+770		
	12+780		
	12+790		
	12+800		
	12+810		
	12+820		
	12+830		
	12+840		
	12+850		
	12+860		
	12+870		
	12+880		
	12+890		
	12+900		
	12+910		
	12+920		
	12+930		
	12+940		
	12+950		
	12+960		
	12+970		
	12+980		
	12+990		
	13+000		
	13+010		

RHS	Chainage	LHS	
		Sub-Grade	Embankment
BC	13+030	BC	
DBM	13+040	DBM	
R-WMM	13+050	R-WMM	
R-GSB	13+060	R-GSB	
Sub-Grade	13+070	Sub-Grade	
Embankment	13+080	Embankment	
C&G	13+090	C&G	
	13+100		
	13+110		
	13+120		
	13+130		
	13+140		
	13+150		
	13+160		
	13+170		
	13+180		
	13+190		
	13+200		
	13+210		
	13+220		
	13+230		
	13+240		
	13+250		
	13+260		
	13+270		
	13+280		
	13+290		
	13+300		
	13+310		
	13+320		
	13+330		
	13+340		
	13+350		
	13+360		
	13+370		
	13+380		
	13+390		
	13+400		
	13+410		
	13+420		
	13+430		
	13+440		
	13+450		
	13+460		
	13+470		
	13+480		
	13+490		
	13+500		
	13+510		
	13+520		
	13+530		
	13+540		
	13+550		
	13+560		
	13+570		
	13+580		
	13+590		
	13+600		
	13+610		
	13+620		
	13+630		
	13+640		
	13+650		
	13+660		
	13+670		
	13+680		
	13+690		
	13+700		
	13+710		
	13+720		
	13+730		
	13+740		
	13+750		
	13+760		
	13+770		
	13+780		
	13+790		
	13+800		
	13+810		
	13+820		
	13+830		
	13+840		
	13+850		
	13+860		
	13+870		
	13+880		
	13+890		
	13+900		
	13+910		
	13+920		
	13+930		
	13+940		
	13+950		
	13+960		
	13+970		
	13+980		
	13+990		
	14+000		
	14+010		

[illegible]

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

9.5 Detailed Structure Work Progress

9.5.1 Status of Box Culvert

S _N	LHS											Box Culvert Chainage	RHS											
	Protection Work	Parapet Wall	Top Slab	Top Haunch	Wall Final Lift	Wall 2nd Lift	Wall 1st Lift	Haunch	Raft	PCC/Granular Bed	Layout & Excavation		Abutment	Layout & Excavation	PCC/Granular Bed	Raft	Haunch	Wall 1st Lift	Wall 2nd Lift	Wall Final Lift	Top Haunch	Top Slab	Parapet Wall	Protection Work
1												A1	00+043	A1										
												A2		A2										
2												A1	00+207	A1										
												A2		A2										
3												A1	00+341	A1										
												A2		A2										
4												A1	01+254	A1										
												A2		A2										
5												A1	01+652	A1										
												A2		A2										
6												A1	01+973	A1										
												A2		A2										
7												A1	02+143	A1										
												A2		A2										
8												A1	02+340	A1										
												A2		A2										
9												A1	02+440	A1										
												A2		A2										
10												A1	03+418	A1										
												A2		A2										
11												A1	03+646	A1										
												A2		A2										

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

SN	LHS												Box Culvert Chainage	RHS											
	Protection Work	Parapet Wall	Top Slab	Top Haunch	Wall Final Lift	Wall 2nd Lift	Wall 1st Lift	Haunch	Raft	PCC/Granular Bed	Layout & Excavation	Abutment		Abutment	Layout & Excavation	PCC/Granular Bed	Raft	Haunch	Wall 1st Lift	Wall 2nd Lift	Wall Final Lift	Top Haunch	Top Slab	Parapet Wall	Protection Work
12												A1	03+925	A1											
												A2		A2											
13												A1	04+018	A1											
												A2		A2											
14												A1	04+340	A1											
												A2		A2											
15												A1	04+534	A1											
												A2		A2											
16												A1	04+847	A1											
												A2		A2											
17												A1	05+126	A1											
												A2		A2											
18												A1	05+920	A1											
												A2		A2											
19												A1	06+190	A1											
												A2		A2											
20												A1	06+642	A1											
												A2		A2											
21												A1	07+668	A1											
												A2		A2											
22												A1	07+832	A1											
												A2		A2											

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

SN	LHS											Box Culvert Chainage	RHS												
	Protection Work	Parapet Wall	Top Slab	Top Haunch	Wall Final Lift	Wall 2nd Lift	Wall 1st Lift	Haunch	Raft	PCC/Granular Bed	Layout & Excavation		Abutment	Layout & Excavation	PCC/Granular Bed	Raft	Haunch	Wall 1st Lift	Wall 2nd Lift	Wall Final Lift	Top Haunch	Top Slab	Parapet Wall	Protection Work	
23												A1	07+906	A1											
												A2		A2											
24												A1	08+188	A1											
												A2		A2											
25												A1	08+926	A1											
												A2		A2											
26												A1	08+576	A1											
												A2		A2											
27												A1	09+543	A1											
												A2		A2											
28												A1	09+779	A1											
												A2		A2											
29												A1	10+529	A1											
												A2		A2											
30												A1	11+073	A1											
												A2		A2											
31												A1	11+921	A1											
												A2		A2											
32												A1	12+223	A1											
												A2		A2											
33												A1	12+663	A1											
												A2		A2											
34												A1	13+065	A1											
												A2		A2											
35												A1	13+380	A1											
												A2		A2											
36												A1	13+740	A1											
												A2		A2											
1	Not Available																								
2	In Progress																								
3	Completed																								

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

9.5.2 Status of Minor Bridge

SN	LHS												Minor Bridge Chainage	RHS													
	Miscellaneous Item	Crash Barrier	Approach Slab	Desk Slab	PSC Girder	Pedestal	Dirt Wall	Abutment Cap	Abutment Wall	Abutment Pile Cap	Abutment Pile	Layout & Excavation		Abutment	Abutment	Layout & Excavation	Abutment Pile	Abutment Pile Cap	Abutment Wall	Abutment Cap	Dirt Wall	Pedestal	PSC Girder	Desk Slab	Approach Slab	Crash Barrier	Miscellaneous Item
1													A1	00+742	A1												
													A2		A2												
2													A1	01+768	A1												
													A2		A2												
3													A1	06+313	A1												
													A2		A2												
4													A1	07+306	A1												
													A2		A2												
5													A1	09+003	A1												
													A2		A2												
6													A1	09+293	A1												
													A2		A2												
7													A1	11+363	A1												
													A2		A2												
8													A1	14+195	A1												
													A2		A2												

1	Not Available	1
2	In Progress	
3	Completed	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

9.5.3 Status of Major Bridge & ROB

SN	LHS														Major Bridge & ROB Chainage	RHS															
	Miscellaneous Item	Crash Barrier	Approach Slab	Desk Slab	PSC Girder	Pedestal	Dirt Wall	Pier Cap	Pier Column	Abutment/ Pier Cap	Abutment Wall	Abutment/ Pier Pile Cap	Abutment/ Pier Pile	Layout & Excavation		Abutment	Layout & Excavation	Abutment/ Pier Pile	Abutment/ Pier Pile Cap	Abutment Wall	Abutment/ Pier Cap	Pier Column	Pier Cap	Dirt Wall	Pedestal	PSC Girder	Desk Slab	Approach Slab	Crash Barrier	Miscellaneous Item	
1															A1	00+526	A1														
															P1		P1														
															P2		P2														
															A2		A2														
2															A1	02+880	A1														
															P1		P1														
															P2		P2														
															A2		A2														
3															A1	05+322	A1														
															P1		P1														
															P2		P2														
															A2		A2														
1															A1	ROB 04+624	A1														
															P1		P1														
															P2		P2														
															P3		P3														
															A2		A2														

1	Not Available	1
2	In Progress	
3	Completed	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

9.5.4 Status of VUP

SN	LHS												VUP Chainage	RHS													
	Miscellaneous Item	Crash Barrier	Approach Slab	Desk Slab	PSC Girder	Pedestal	Dirt Wall	Abutment Cap	Abutment Wall	Abutment Pile Cap	Abutment Pile	Layout & Excavation		Abutment	Abutment	Layout & Excavation	Abutment Pile	Abutment Pile Cap	Abutment Wall	Abutment Cap	Dirt Wall	Pedestal	PSC Girder	Desk Slab	Approach Slab	Crash Barrier	Miscellaneous Item
1													A1	02+999	A1												
													A2		A2												
2													A1	05+622	A1												
													A2		A2												

1	Not Available	1
2	In Progress	
3	Completed	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

9.5.4 Status of LVUP & SVUP

SN	LHS											LVUP & SVUP Chainage	RHS											
	Protection Work	Parapet Wall	Top Slab	Top Haunch	Wall Final Lift	Wall 2nd Lift	Wall 1st Lift	Haunch	Raft	PCC/Granular Bed	Layout & Excavation		Abutment	Layout & Excavation	PCC/Granular Bed	Raft	Haunch	Wall 1st Lift	Wall 2nd Lift	Wall Final Lift	Top Haunch	Top Slab	Parapet Wall	Protection Work
1												A1	01+142	A1										
												A2		A2										
2												A1	03+886	A1										
												A2		A2										
3												A1	04+212	A1										
												A2		A2										
4												A1	05+414	A1										
												A2		A2										
5												A1	07+213	A1										
												A2		A2										
6												A1	09+332	A1										
												A2		A2										
7												A1	10+098	A1										
												A2		A2										
8												A1	10+834	A1										
												A2		A2										
9												A1	12+310	A1										
												A2		A2										
10												A1	SVUP 03+728	A1										
												A2		A2										
1	Not Available			1																				
2	In Progress																							
3	Completed																							

CHAPTER-10

QUALITY CONTROL AND MATERIAL

10.1 Quality Control

The execution of works is mainly governed by the specified Technical Specifications for the project. The quality control of the works is required to be monitored on daily basis both at site and in the laboratory. Standard formats have been devised to control the required quality of the works. The Concessionaire Engineers are monitoring the required quality control works and maintaining the records accordingly for each item of works being executed.

10.2 Site Laboratory

The Site Laboratory is established at Base Camp located at CH: -5+600. All the required material tests are being conducted in the laboratory for the project road.

10.3 Materials Testing & Third Party Test

The testing to be carried out in the site laboratory includes tests of soil, aggregates, cement, steel, sand, embankment fill, sub grade, granular subbase and cement concrete. The details of test conducted up to 31st March, 2025 are enclosed.

10.3.1 Soil and Agreegates

The test reports for borrow area earth for available borrow area are approved & test reports for Aggregates are also approved for the available Quarry. Test reports for new borrow area earth are submitted to IE for approval.

10.3.2 Cement

The Concessionaire is using approved sources of Cement as Black Tiger (OPC 43 Grade), Dalmia Cement (OPC 43 Grade), Star Cement (OPC 43 Grade), Amrit Cement (OPC 43 Grade) & Max Cement (OPC 43 Grade) for the project work.

10.3.3 Reinforcement Steel

The Concessionaire is using approved sources of TMT from M/s Rashmi Metaliks Limited, M/s Shyam Steel Industries limited, M/s SRMB Srijan Private Limited, M/s Shyam Metalics and Energy Limited.

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

10.3.4 Status of materials source approval & Mix Design

Cement				
Sr. No.	Brand Name	Letter No.	Status	IE Letter No.
1.	Black Tiger Cement	MKCIL/ASSAM/PKG-07/106 dt. 24.03.2025		
2.	Dalmia Cement	MKCIL/ASSAM/PKG-07/107 dt. 24.03.2025		
3.	Max Cement	MKCIL/ASSAM/PKG-07/108 dt. 24.03.2025		
4.	Star Cement	MKCIL/ASSAM/PKG-07/109 dt. 24.03.2025		
5.	Amrit Cement	MKCIL/ASSAM/PKG-07/110 dt. 24.03.2025		

Reinforcement Steel				
Sr. No.	Brand Name	Letter No.	Status	IE Letter No.
1.	Rashmi Metaliks Limited	MKCIL/ASSAM/PKG-07/111 dt. 24.03.2025		
2.	Shyam Steel industries Ltd.	MKCIL/ASSAM/PKG-07/112 dt. 24.03.2025		
3.	SRMB Srijan Pvt. Ltd.	MKCIL/ASSAM/PKG-07/113 dt. 24.03.2025		
4.	Shyam Metalics & Energy Ltd.	MKCIL/ASSAM/PKG-07/132 dt. 04.04.2025		

Admixture				
Sr. No.	Brand Name	Letter No.	Status	IE Letter No.
1.	Berger Paints Pvt. Ltd.	MKCIL/ASSAM/PKG-07/101 dt. 24.03.2025		
2.	CHRYSO India Pvt. Ltd	MKCIL/ASSAM/PKG-07/102 dt. 24.03.2025		
3.	CICO Technologies Ltd.	MKCIL/ASSAM/PKG-07/103 dt. 24.03.2025		
4.	FOSROC Chemicals (India) Ltd.	MKCIL/ASSAM/PKG-07/104 dt. 24.03.2025		
5.	Vista Chemtech Pvt. Ltd.	MKCIL/ASSAM/PKG-07/105 dt. 24.03.2025		

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

Monthly Laboratory Report

Summary of Quality Control Test For The Month of May-2025																	
Sr.No.	Name of test	Reference as per IS/ MoRT&H	Frequency of Tests	Total Tests Conducted upto Previous Month			No. of Tsts Conducted during this Month			No. of Tests Conducted upto this Month			No. of Tests cChecked by IE			% Checked by IE	Remarks
				Tested	Passed	Failed	Tested	Passed	Failed	Tested	Passed	Failed	Tested	Passed	Failed		
LAB & FIELD TEST'S																	
(I). OGL Samples		IRC:36-2010															
1.1	Free Swelling Index (FSI)	IS: 2720 (P-40)	1 Test / Every 500 m Interval's	32	32	0	0	0	0	32	32	0	0	0	0	0.00	
1.2	Grain size analysis	IS: 2720 (P-4)	1 Test / Every 500 m Interval's	32	32	0	0	0	0	32	32	0	0	0	0	0.00	
1.3	Liquid limits (LL)	IS: 2720 (P-5)	1 Test / Every 500 m Interval's	32	32	0	0	0	0	32	32	0	0	0	0	0.00	
1.4	Plasticity Index (PI)	IS: 2720 (P-5)	1 Test / Every 500 m Interval's	32	32	0	0	0	0	32	32	0	0	0	0	0.00	
1.5	Proctor test (MDD & OMC)	IS: 2720 (P-8)	1 Test / Every 500 m Interval's	32	32	0	0	0	0	32	32	0	0	0	0	0.00	
1.6	California Bearing Ratio Test (CBR)	IS: 2720 (P-16)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
1.7	Field Compaction Test (OGL)	IS: 2720 (P-28)	1 Set / 3000 Sqm. (1Set = 10 Pit's)	322	309	13	0	0	0	322	309	13	0	0	0	0.00	
(II). Borrow area Samples (EMB/SG)		MoRT&H (Clause-305)															
2.1	Free Swelling Index (FSI)	IS: 2720 (P-40)	2 Test's / 3000 Cum.	15	15	0	0	0	0	15	15	0	0	0	0	0.00	
2.2	Grain size analysis (GSA)	IS: 2720 (P-4)	2 Test's / 3000 Cum.	15	15	0	0	0	0	15	15	0	0	0	0	0.00	
2.3	Liquid limits (LL)	IS: 2720 (P-5)	2 Test's / 3000 Cum.	15	15	0	0	0	0	15	15	0	0	0	0	0.00	
2.4	Plasticity Index (PI)	IS: 2720 (P-5)	2 Test's / 3000 Cum.	15	15	0	0	0	0	15	15	0	0	0	0	0.00	
2.5	Proctor test (MDD & OMC)	IS: 2720 (P-8)	2 Test's / 3000 Cum.	15	15	0	0	0	0	15	15	0	0	0	0	0.00	
2.6	California Bearing Ratio Test (CBR)	IS: 2720 (P-16)	1 Test's / 3000 Cum.	8	8	0	0	0	0	8	8	0	0	0	0	0.00	
2.7	Field Compaction Test (Emb)	IS: 2720 (P-28)	1 Set / 3000 Sqm. (1Set = 10 Pit's)	293	272	21	0	0	0	293	272	21	0	0	0	0.00	
2.8	Field Compaction Test (Subgrade)	IS: 2720 (P-28)	1 Set / 2000 Sqm. (1Set = 10 Pit's)	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
(III). Coarse Agg. for Concrete Work's		MoRT&H Table -900-6															
4.1	Gradation of Coarse Aggregate	IS: 2386 (P-1)	1 Test / Every day's work	14	14	0	17	17	0	31	31	0	3	3	0	17.65	
4.2	Flakiness Index (FI)	IS: 2386 (P-1)	1 Test for source / Weekly	5	5	0	4	4	0	9	9	0	1	1	0	25.00	
4.3	Aggregate Impact Value (A.I.V)	IS: 2386 (P-4)	1 Test for source / Weekly	5	5	0	4	4	0	9	9	0	1	0	0	25.00	
4.4	Specific Gravity	IS: 2386 (P-3)	1 Test / Source	3	3	0	0	0	0	3	3	0	0	0	0	0.00	
4.5	Water Absorption	IS: 2386 (P-3)	1 Test / Source	3	3	0	0	0	0	3	3	0	0	0	0	0.00	
4.6	Deleterious Constituents	IS: 2386 (P-2)	1 Test / As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
4.7	Moisture correction	IS: 2386 (P-3)	1 Test / Day	3	3	0	17	17	0	20	20	0	3	3	0	17.65	
4.8	Soundness	IS: 2386 (P-5)	1 Test / Source	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
4.9	Alkali Aggregate Reactivity	IS: 2386 (P-7)	1 Test / Source	0	0	0	0	0	0	0	0	0	0	0	0	0.00	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

(IV). Fine Agg. for Concrete		MoRT&H Table -900-6														
5.1	Gradation	IS : 383	1 Test / Every day's work	9	9	0	17	17	0	26	26	0	4	4	0.0	23.53
5.2	Specific Gravity	IS : 2386 (P-3)	1 Test / Source	3	3	0	0	0	0	3	3	0	0	0	0.0	0.00
5.3	Water Absorption	IS : 2720 (P-3)	1 Test / Source	3	3	0	0	0	0	3	3	0	0	0	0.0	0.00
5.4	Silt Content	IS : 383	1 Test / Weekly	5	5	0	4	4	0	9	9	0	1	1	0.0	25.00
5.5	Moisture correction	IS : 2386 (P-3)	1 Test / Every day's work	3	3	0	17	17	0	20	20	0	3	3	0.0	17.65
(V). Concrete Cube's Compressive Strength Test		IS: 516														
Grade of Concrete : M-10 PCC																
6.1	for 7 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	9	9	0	9	9	0	1	1	0	11.11
6.2	for 28 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	14	14	0	14	14	0	2	2	0	14.29
Grade of Concrete : M-15 PCC																
6.3	for 7 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00
6.4	for 28 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00
Grade of Concrete : M-20 PCC																
6.5	for 7 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00
6.6	for 28 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00
Grade of Concrete : M-20 RCC																
6.7	for 7 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00
6.8	for 28 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00
Grade of Concrete : M-20 for KERB																
6.9	for 7 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00
6.1	for 28 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00
Grade of Concrete : M-25 RCC																
6.11	for 7 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00
6.12	for 28 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00
Grade of Concrete : M-30 RCC																
6.13	for 7 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	17	17	0	17	17	0	2	2	0	11.76
6.14	for 28 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	34	34	0	34	34	0	5	5	0	14.71
Grade of Concrete : M-35 RCC																
6.15	for 7 days	IS : 516	As per Frequency MoRT&H Table 1700-09	1	1	0	0	0	0	1	1	0	0	0	0	0.00
6.16	for 28 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	3	3	0	3	3	0	0	0	0	0.00

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

..	Grade of Concrete : M-35 Pile																
6.17	for 7 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
6.18	for 28 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
..	Grade of Concrete : M-35 RE BLOCK																
6.19	for 7 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
6.2	for 28 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
..	Grade of Concrete : M-40 RCC																
6.21	for 7 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
6.22	for 28 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
..	Grade of Concrete : M-45 RCC/PSC																
6.23	for 7 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
6.24	for 28 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
..	Grouting of PSC Girders																
6.25	for 7 days	IS : 516	As per Frequency MoRT&H	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
6.26	for 28 days	IS : 516	As per Frequency MoRT&H	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
(VI). Cement tests																	
7.1	Fineness of Cement	IS : 4031 (P-1)	1 Test Every Batch of Cement	2	2	0	0	0	0	2	2	0	0	0	0	0.00	
7.2	Normal Consistency	IS : 4031 (P-4)	1 Test Every Batch of Cement	2	2	0	0	0	0	2	2	0	0	0	0	0.00	
7.3	Initial Setting Time	IS : 4031 (P-5)	1 Test Every Batch of Cement	2	2	0	0	0	0	2	2	0	0	0	0	0.00	
7.4	Final Setting time	IS : 4031 (P-5)	1 Test Every Batch of Cement	2	2	0	0	0	0	2	2	0	0	0	0	0.00	
7.5	Compressive Strength (03 Days)	IS : 516	1 Test Every Batch of Cement	3	2	0	0	0	0	3	2	0	0	0	0	0.00	
7.6	Compressive Strength (07 Days)	IS : 516	1 Test Every Batch of Cement	2	3	0	0	0	0	2	3	0	0	0	0	0.00	
7.7	Compressive Strength (28 Days)	IS : 516	1 Test Every Batch of Cement	2	0	0	0	0	0	2	0	0	0	0	0	0.00	
7.8	Soundness	IS : 4031 (P-3)	1 Test Every Batch of Cement	0	0	0	0	0	0	0	0	0	0	0	0	0.0	
7.9	Specific Gravity	IS : 4031 (P-11)	1 Test Every Batch of Cement	0	0	0	0	0	0	0	0	0	0	0	0	0.0	
(VII). Granular Sub-Base (GSB)		MoRT&H Clause - 401															
8.1	Gradation	Table 400-2	1 Test /400 Cum.	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
8.2	Liquid limits (LL)	IS : 2720 (P-5)	1 Test /400 Cum.	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
8.3	Plasticity Index (PI)	IS : 2720 (P-5)	1 Test /400 Cum.	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
8.4	Moisture Prior to Compaction Test	IS : 2720 (P-2)	1 Test /400 Cum.	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
8.5	Proctor test (MDD & OMC)	IS : 2720 (P-8)	1 Test Per Source / As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
8.6	California Bearing Ratio Test (CBR)	IS : 2720 (P-16)	1 Test Per Source / As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
8.7	Water Absorption	IS : 2720 (P-3)	1 Test Per Source / As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
8.8	Aggregate Impact Value (AIV)	IS : 2386 (P-4)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
8.9	Field Compaction Test (GSB)	IS : 2720 (P-28)	1 Set / 1000 Sqm. (1Set = 3 Pit's)	0	0	0	0	0	0	0	0	0	0	0	0	0.00	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

(VIII). Cement Treated Sub Base (CTSB)		MoRT&H Clause - 403 & IRC-37: 2018														
9.1	Gradation	MoRT&H Table 400-4	1 Test 400 Cum.	0	0	0	0	0	0	0	0	0	0	0	0	0.00
9.2	Liquid limits (LL)	IS : 2720 (P-5)	1 Test 400 Cum.	0	0	0	0	0	0	0	0	0	0	0	0	0.00
9.3	Plasticity Index (PI)	IS : 2720 (P-5)	1 Test 400 Cum.	0	0	0	0	0	0	0	0	0	0	0	0	0.00
9.4	Proctor test (MDD & OMC)	IS : 2720 (P-8)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
9.5	Unconfined Compressive Strength (UCS)	IS: 516	3 Specimens each 400 ton/ Minimum 2 tests per day	0	0	0	0	0	0	0	0	0	0	0	0	0.00
9.6	Cement Content	IS: 516	3 Specimens each 400 ton/ Minimum 2 tests per day	0	0	0	0	0	0	0	0	0	0	0	0	0.00
9.7	Flexural Strength	IS: 516	3 Specimens each 400 ton/ Minimum 2 tests per day	0	0	0	0	0	0	0	0	0	0	0	0	0.00
9.8	Soundness Test	BIS: 4332 (P-4)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
9.9	Field Compaction Test (CTSB)	IS : 2720 (P-28)	2 Test's 500 Sqm.	0	0	0	0	0	0	0	0	0	0	0	0	0.00
(IX). Cement Treated Base (CTB)		MoRT&H Clause - 403 & IRC-37: 2018														
10.1	Gradation	MoRT&H Table 400-4	1 Test 400 Cum.	0	0	0	0	0	0	0	0	0	0	0	0	0.00
10.2	Proctor test (MDD & OMC)	IS : 2720 (P-8)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
10.3	Unconfined Compressive Strength (UCS)	IS: 516	3 Specimens each 400 ton/ Minimum 2 tests per day	0	0	0	0	0	0	0	0	0	0	0	0	0.00
10.4	Cement Content	IS: 516	3 Specimens each 400 ton/ Minimum 2 Tests per day	0	0	0	0	0	0	0	0	0	0	0	0	0.00
10.5	Flexural Strength	IS: 516	3 Specimens each 400 ton/ Minimum 2 Tests per day	0	0	0	0	0	0	0	0	0	0	0	0	0.00
10.6	Soundness Test	BIS: 4332 (P-4)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
10.7	Field Compaction Test (CTSB)	IS : 2720 (P-28)	2 Test's 500 Sqm.	0	0	0	0	0	0	0	0	0	0	0	0	0.00
(X). Wet Mix Macadam (WMM)		MoRT&H-406														
11.1	Gradation	Table 400-13	1 Test /200 Cum.	0	0	0	0	0	0	0	0	0	0	0	0	0.00
11.2	Atterberg limits (LL & PI)	IS : 2720 (P-5)	1 Test /200 Cum.	0	0	0	0	0	0	0	0	0	0	0	0	0.00
11.3	Proctor test (MDD Vs OMC)	IS : 2720 (P-8)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
11.4	Aggregate Impact Value (A.I.V)	IS : 2386 (P-4)	1 Test / 1000 Cum	0	0	0	0	0	0	0	0	0	0	0	0	0.00
11.5	Combined Flakiness & Elongation (FI & FI ₁)	IS : 2386 (P-1)	1 Test /500 Cum	0	0	0	0	0	0	0	0	0	0	0	0	0.00
11.6	Water Absorption	IS : 2386 (P-3)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
11.7	Soundness	IS : 2386 (P-3)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
11.8	Field Compaction Test (WMM)	IS : 2720 (P-28)	1 Set / 1000 Sqm. (1Set = 3 Pit's)	0	0	0	0	0	0	0	0	0	0	0	0	0.00
(XI). Aggregate Inter Layer (AIL)		MoRT&H-406														
12.1	Gradation	Table 400-13	1 Test /200 Cum.	0	0	0	0	0	0	0	0	0	0	0	0	0.00
12.2	Atterberg limits (LL & PI)	IS : 2720 (P-5)	1 Test /200 Cum.	0	0	0	0	0	0	0	0	0	0	0	0	0.00
12.3	Proctor test (MDD & OMC)	IS : 2720 (P-8)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
12.4	Aggregate Impact Value (A.I.V)	IS : 2386 (P-4)	1 Test / 1000 Cum	0	0	0	0	6	0	0	6	0	0	0	0	0.00
12.5	Combined Flakiness & Elongation (FI & FI ₁)	IS : 2386 (P-1)	1 Test /500 Cum	0	0	0	0	0	0	0	0	0	0	0	0	0.00
12.6	Water Absorption	IS : 2386 (P-3)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
12.7	Soundness	IS : 2386 (P-3)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
12.8	Field Compaction Test (AIL)	IS : 2720 (P-28)	1 Set / 1000 Sqm. (1Set = 3 Pit's)	0	0	0	0	0	0	0	0	0	0	0	0	0.00

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

(XII). Dense Bituminous Macadam (DBM)			MoRT&H-500														
13.1	Binder Content & Gradation	As per MoRT&H	1 Test / 400 Tonnes	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
13.2	Mix Combined Gradation	As per MoRT&H	1 Test / 400 Tonnes	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
13.3	Marshall Test (In Sets)	ASTM-D:1559	1 Set/ 400 Tonnes	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
13.4	Aggregate Impact Value (A.I.V)	IS : 2386 (P-4)	1 Test / 350 Cum	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
13.5	Combined Flakiness & Elongation (FI & EI)	IS : 2386 (P-1)	1 Test / 350 Cum	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
13.6	Water Absorption & Specific Gravity	IS : 2386 (P-3)	1 Test/ Source & As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
13.7	Stripping Value	IS : 6241	1 Test/ Source & As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
13.8	Maximum Sp.Gravity(Gmm)	ASTM D 2041	1 Set/ 400 MTMix	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
13.9	Density of compacted layer	MoRT&H Sec 900	1 Test / 700 Sq.m	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
13.10	Soundness	IS : 2386 (P-3)	1 Test/ Source & As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
13.11	Sand equivalent test	IS : 2720 (P-37)	1 Test/ Source & As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
13.12	plasticity Index	MoRT&H Sec 900	1 Test/ Source & As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
13.13	percentage of Fractured face	MoRT&H Sec 900	1 Test/ Source & As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
13.14	Polished Stone Value	BS 812 (P-114)	1 Test/ Source & As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
(XIII). Bituminous Concrete (BC)			MoRTH-500														
14.1	Binder Content & Gradation	As per MoRT&H	1 Test / 400 Tonnes	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
14.2	Mix Combined Gradation	As per MoRT&H	1 Test / 400 Tonnes	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
14.3	Marshall Test (In Sets)	ASTM-D:1559	1 Test/ 400 Tonnes	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
14.4	Aggregate Impact Value (A.I.V)	IS : 2386 (P-4)	1 Test / 350 Cum	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
14.5	Combined Flakiness & Elongation (FI & EI)	IS : 2386 (P-1)	1 Test / 350 Cum	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
14.6	Water Absorption & Specific Gravity	IS : 2386 (P-3)	1 Test/ Source & As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
14.7	Stripping Value	IS : 6241	1 Test/ Source & As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
14.8	Maximum Sp.Gravity(Gmm)	ASTM D 2041	1 set/ 400 MTMix	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
14.9	Density of Compacted Layer	MoRT&H Sec 900	1 test / 700 Sq.m	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
14.10	Soundness	IS : 2386 (P-3)	1 Test/ Source & As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
14.11	Sand equivalent test	IS : 2720 (P-37)	1 Test/ Source & As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
14.12	plasticity Index	MoRT&H Sec 900	1 Test/ Source & As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
14.13	percentage of Fractured face	MoRT&H Sec 900	1 Test/ Source & As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
14.14	Polished Stone Value	BS: 812 (P-114)	1 Test/ Source & As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
(XIV). Bitumen (VG-40)																	
15.1	Softening Point(°c)	IS : 1205	1 Test Per Lot	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
15.2	Penetration at 25°C 100gm 5 Sec	IS : 1203	1 Test Per Lot	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
15.3	Ductility at 25°C	IS : 1208	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
15.4	Absolute Viscosity at 60°/135°C (CST)	IS : 1206 (P-2)	1 Test Per Lot	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
15.5	Kinematic Viscosity at 135°C (CST)	IS : 1206 (P-3)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0	
15.6	Specific Gravity at 27°C	IS : 2380 (P-4)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
15.7	Flash Pint	IS : 1209 (IS: 1448 P-69)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0	
15.8	Solubility Test	IS : 1216	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

(XV). MODIFIED BITUMEN (PMB 76E-10)																	
16.1	Specific Gravity at 27°C	IS: 2380 (P-4)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
16.2	Softening Point (°C)	IS: 1205	1 Test Per Lot	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
16.3	Seperation, Difference in Softening Point (0°C)	IS: 15462: 2019	1 Test Per Lot	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
16.4	Elastic Recovery at 15°C	IS: 15462: 2019	1 Test Per Lot	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
(XVI). Emulsion (SS-1)																	
17.1	Viscosity @ 25°C	IS: 8887:2004	1 Test Per Lot	0	0	0	0	0	0	0	0	0	0	0	0	0	
17.2	Water Content	IS: 8887:2004	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0	
17.3	Prime coat	IS: 8887:2004	3 test / Day	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
(XVII). Emulsion (RS-1)																	
18.1	Viscosity @ 50°C	IS: 8887:2004	1 Test Per Lot	0	0	0	0	0	0	0	0	0	0	0	0	0	
18.2	Water Content	IS: 8887:2004	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0	
18.3	Tack Coat	IS: 8887:2004	3 test / Day	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
(XVIII). Lean Concrete (DLC)			MoRT&H-600														
13.1	Gradation	Table 600-1	1 test / day	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
13.2	Field Compaction Test	IS: 2720 (P-28)	1 Set(3 pit) of tests / 2000 sqm.	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
13.3	Proctor test (MDD & OMC)	IS: 2720 (P-8)	As required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
13.4	Aggregate Impact Value (A.I.V)	IS: 2386 (P-4)	As required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
13.5	Flakiness & Elongation (FI & EI)	IS: 2386 (P-1)	As required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
13.6	Water Absorption	IS: 2386 (P-3)	As required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
13.7	Moisture correction	IS: 2386 (P-3)	1 test / Day	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
13.8	Compressive Strength (07 day's)	IS: 516	07 days/ Each Day 5 Cube's	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
(XIX). Pavement Quality Concrete (PQC)			MoRT&H-600														
14.1	Gradation	Table 600-1	1 Test / Day	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
14.2	Aggregate Impact Value (A.I.V)	IS: 2386 (P-4)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
14.3	Flakiness & Elongation (FI & EI)	IS: 2386 (P-1)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
14.4	Water Absorption	IS: 2386 (P-3)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
14.5	Slump Test	IS: 1199	1 Test Each Dumper	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
14.6	Compressive Strength (07 day's)	IS: 516	Compressive Strength (07 day's)	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
14.7	Compressive Strength (28 day's)	IS: 516		0	0	0	0	0	0	0	0	0	0	0	0	0.00	
14.8	Flexural Strength (07 day's)	IS: 516	As per Frequency 02 Beam's /150 Cum (Min. 6 Beam's)	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
14.9	Flexural Strength (28 day's)	IS: 516		0	0	0	0	0	0	0	0	0	0	0	0	0.00	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

THIRD PARTY TESTS (NABL ACCREDITED LABORATORY)																
(XX). Course Aggregates																
181	Gradation	IS : 2386 (P-1)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
182	Fl & El	IS : 2386 (P-1)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
183	Aggregate Impact Value	IS : 2386 (P-4)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
184	Specific Gravity	IS : 2386 (P-3)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
185	Water Absorption	IS : 2386 (P-3)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
186	Deleterious Content	IS : 2386 (P-1)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
187	L.A.V.	IS : 2386 (P-4)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
188	Alkali Aggregate Reactivity	IS : 2386 (P-7)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
189	Soundness	IS : 2386(P-5)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
1810	Petrographic Examination	IS : 2386 (P-8)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
1811	Stone Polished Value	BS-812 (P-114)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
(XXI). Fine Aggregates																
191	Gradation	IS : 383	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
192	Specific Gravity	IS : 2386 (P-3)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
193	Water Absorption	IS : 2386 (P-3)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
194	Deleterious Content	IS : 2386 (P-1)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
195	Silt Content	IS : 2386 (P-4)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
196	Alkali Aggregate Reactivity	IS : 2386 (P-7)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
197	Soundness	IS : 2386(P-5)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
198	Organic Impurities	IS : 2386 (P-8)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
199	Fineness Modulus	IS : 383	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
(XXII). TMT Bar's (Steel)																
201	Physical properties	IS : 1786	< 10mm - 1 sample/25 MT, 10-16mm- 1sample/35 MT,	0	0	0	0	0	0	0	0	0	0	0	0	0.00
202	Chemical properties	IS : 1786	> 16mm - 1 sample/45 MT	0	0	0	0	0	0	0	0	0	0	0	0	0.00
(XXIII). Construction Water																
211	Suitability for construction	IS : 456	1 Test Per Source / As Required	1	1	0	0	0	0	1	1	0	0	0	0	0.00

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

(XXIV). Chemical Admixture																	
22.1	Physical & Chemical properties	IS : 9103	1 Test / Per Lot	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
(XXV). Cement (OPC-53 Grade)																	
23.1	Physical & Chemical properties	IS : 8112	1 Test / Source	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
(XXVI). Soil - Borrow Area																	
24.1	Mechanical	IS : 2720 (P-39)	1 Test / Source	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
(XXVII). NP-4 Hume Pipe Test										0	0						
25.1	600 MM	IS : 458	1 test per Lot /of 50 Pipes	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
(XXVIII). Bitumen (Emulsion)																	
26.1	Bitumen Emulsion SS-1	IS : 8887	1 Test / Per Lot	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
26.2	Bitumen Emulsion RS-1	IS : 8887	1 Test / Per Lot	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
(XXIX). Bitumen (VG-40)																	
27.1	Bitumen VG-40	IS : 73	1 Test / Per Lot	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
(XXX). Bitumen (PMB)																	
28.1	Bitumen PMB	IS : 15462-2019	1 Test / Per Lot	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
(XXXI). Curing Compound																	
29.1	Physical & Chemical properties	ASTM C309	1 Test / Per Lot	0	0	0	0	0	0	0	0	0	0	0	0	0.00	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

**CHAPTER-11
CORRESPONDENCE**

11.1 Outward Letter

Sr. No.	Letter No.	Date	Subject	To	Remarks
1	<u>MKCIL/ASSAM/P KG-07/001</u>	19-04-2024	Documents Required for Details Design.	DGM (PMU Silchar)	
2	<u>MKCIL/ASSAM/P KG-07/003</u>	19-07-2024	Signing Authorization for letter correspondence and submission of SPSs & IPCs for Satish Chandra Pandeya (Sr. GM Tech & Operations)	DGM (PMU Silchar)	
3	<u>MKCIL/ASSAM/S PL/001</u>	31-07-2024	Submission of Presentation for above Said Project	GM (RO)	
4	<u>MKCIL/ASSAM/P KG-07/005</u>	09-08-2024	Indent through online portal of Minor Minerals for the execution of above said project	GM (PMU Karimganj)	
5	<u>MKCIL/ASSAM/P KG-07/008</u>	21-08-2024	Indent through online portal of Minerals for the execution of above said project	GM (PMU Karimganj)	
6	<u>MKCIL/ASSAM/P KG-07/013</u>	29-08-2024	Reg. Notification for non-receipt of General Arrangement Drawing (GAD) of Road Over Bridge Under Bridges at level crossing.	GM (PMU Karimganj)	
7	<u>MKCIL/ASSAM/P KG-07/015</u>	03-09-2024	Reg. Revised Indent through online portal of Minor Minerals for the execution of above said project."	GM (PMU Karimganj)	
8	<u>MKCIL/ASSAM/P KG-07/017</u>	04-09-2024	Reg. Drone videography survey as per Clause 13.6 of CA	GM (PMU Karimganj)	
9	<u>MKCIL/ASSAM/P KG-07/021</u>	08-10-2024	Regarding Request to issuing Form - III for applying of Labour License.	GM (PMU Karimganj)	
10	<u>MKCIL/ASSAM/P KG-07/030</u>	07-12-2024	Reg. Compliance of Conditions Precedent as per Article 4.1.3 of the Concession Agreement.	GM (PMU Karimganj)	
11	MKCIL/ASSAM/P KG-07/035	09.01.2025	Request for providing a consent letter to the APDCL	GM (PMU Karimganj)	
12	<u>MKCIL/ASSAM/P KG-07/038</u>	16-01-2025	Regarding Submission of Contract Price Weightage as per Annexure - I of Schedule - G.	GM (PMU Karimganj)	
13	<u>MKCIL/ASSAM/P KG-07/040</u>	21-01-2025	Regarding Submission of Test Pile Drawing for Major Bridge at Ch. 05+322	GM (PMU Karimganj)	
14	<u>MKCIL/ASSAM/P KG-07/045</u>	21-1-2025	Reg. Joint Inspection for Identification for extraction of Soil for Road Works.	GM (PMU Karimganj)	
15	<u>MKCIL/ASSAM/P KG-07/046</u>	24.01.2025	Reg. Joint Inspection for Identification for extraction of Soil for Road Works.	GM (PMU Karimganj)	
16	<u>MKCIL/ASSAM/P KG-07/048</u>	25-01-2025	Reg. Submission of lower TDS deduction certificate	GM (PMU Karimganj)	
17	MKCIL/ASSAM/P KG-07/055	07.02.2025	Regarding Submission of Typical Design & Drawing for Precast Box Culvert (1x2x2).	GM (PMU Karimganj)	
18	<u>MKCIL/ASSAM/P KG-07/069</u>	24-02-2025	Reg. Request for Provisional Appointment Date for commencement of work.	GM (PMU Karimganj)	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

19	MKCIL/ASSAM/P KG-07/074	28.02.2025	Reg. Compliance of Condition Precedent as per Article of 4.1.3 of Concession Agreement.	GM (PMU Karimganj)	
20	<u>MKCIL/ASSAM/P KG-07/075</u>	01-03-2025	Reg. Compliance of Condition Precedent as per Sub Clause (d) of Article of 4.1.3 of Concession Agreement	GM (PMU Karimganj)	
21	MKCIL/ASSAM/P KG-07/078	03.03.2025	Submission of Aggregate 10mm, 20mm, Water, Fine aggregate (River Sand) Samples for Conducting Third Party Test	Managing Director (Avian Test Lab Guwahati)	
22	<u>MKCIL/ASSAM/P KG-07/080</u>	05-03-2025	Appointment of Independent Engineer as per Article 21-Independent Engineer, Clause 21.1 of Concession Agreement.	GM (PMU Karimganj)	
23	MKCIL/ASSAM/P KG-07/087	13.03.2025	Regarding Submission of Typical RE Block Drawing.	GM (PMU Karimganj)	
24	MKCIL/ASSAM/P KG-07/090	15.03.2025	Regarding Submission of Concession Agreement Volumes.	GM (PMU Karimganj)	
25	MKCIL/ASSAM/P KG-07/095	19.03.2025	Appointment of Authorized Representative.	GM (PMU Karimganj)	
26	MKCIL/ASSAM/P KG-07/101	24.03.2025	Submission Profile & Credential of Berger Paints Pvt. Ltd. for Source Approval of Admixture.	GM (PMU Karimganj)	
27	MKCIL/ASSAM/P KG-07/102	24.03.2025	Submission Profile & Credential of CHRYSO India Pvt. Ltd. for Source Approval of Admixture.	GM (PMU Karimganj)	
28	MKCIL/ASSAM/P KG-07/103	24.03.2025	Submission Profile & Credential of CICO Technologies Limited for Source Approval of Admixture.	GM (PMU Karimganj)	
29	MKCIL/ASSAM/P KG-07/104	24.03.2025	Submission Profile & Credential of FOSROC Chemicals (India) Pvt. Ltd. for Source Approval of Admixture.	GM (PMU Karimganj)	
30	MKCIL/ASSAM/P KG-07/105	24.03.2025	Submission Profile & Credential of VISTA Chemtech Pvt. Ltd. for Source Approval of Admixture.	GM (PMU Karimganj)	
31	MKCIL/ASSAM/P KG-07/106	24.03.2025	Submission Profile & Credential of Black Tiger Cement for Source Approval of Cement.	GM (PMU Karimganj)	
32	MKCIL/ASSAM/P KG-07/107	24.03.2025	Submission Profile & Credential of Dalmia Cement (Bharat) Limited for Source Approval of Cement.	GM (PMU Karimganj)	
33	MKCIL/ASSAM/P KG-07/108	24.03.2025	Submission Profile & Credential of Max Cement for Source Approval of Cement.	GM (PMU Karimganj)	
34	MKCIL/ASSAM/P KG-07/109	24.03.2025	Submission Profile & Credential of Star Cement Limited for Source Approval of Cement.	GM (PMU Karimganj)	
35	MKCIL/ASSAM/P KG-07/110	24.03.2025	Submission Profile & Credential of Amrit Cement Limited for Source Approval of Cement.	GM (PMU Karimganj)	
36	MKCIL/ASSAM/P KG-07/111	24.03.2025	Submission Profile & Credential of Rashmi Metaliks Limited for Source Approval of TMT Bar.	GM (PMU Karimganj)	
37	MKCIL/ASSAM/P KG-07/112	24.03.2025	Submission Profile & Credential of Shyam Steel Industries Limited for Source Approval of TMT Bar.	GM (PMU Karimganj)	
38	MKCIL/ASSAM/P KG-07/113	24.03.2025	Submission Profile & Credential of SRMB Srijan Pvt. Ltd. for Source Approval of TMT Bar.	GM (PMU Karimganj)	
39	MKCIL/ASSAM/P KG-07/114	24.03.2025	Submission Profile & Credential of Avian Test Lab Pvt. Ltd. for Third Party Laboratory.	GM (PMU Karimganj)	
40	MKCIL/ASSAM/P KG-07/115	24.03.2025	Submission Profile & Credential of Delhi Test House for Third Party Laboratory.	GM (PMU Karimganj)	
41	MKCIL/ASSAM/P KG-07/118	25.03.2025	Procurement of Earth/Soil with respect to the referred Govt. Initiative.	GM (PMU Karimganj)	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

42	MKCIL/ASSAM/P KG-07/120	27.03.2025	Consent for Utility Shifting Work.	GM (PMU Karimganj)	
43	MKCIL/ASSAM/P KG-07/122	31.03.2025	Submission of Contractor's All Risks (CAR) Insurance Police	GM (PMU Karimganj)	
44	MKCIL/ASSAM/P KG-07/125	31.03.2025	Submission of Third Party test Report of Aggregate 10mm, 20mm, Water, Fine Aggregate (River Sand) reg.	GM (PMU Karimganj)	
45	MKCIL/ASSAM/P KG-07/126	01.04.2025	Delay in Mobilization/Appointment of Independent Engineer as per Article 21- Independent Engineer, Clause 21.1 of Concession Agreement- (Reminder)	GM (PMU Karimganj)	
46	MKCIL/ASSAM/P KG-07/128	02.04.2025	Regarding Submission of Plan & Profile with TCS for Main Carriageway & Service Road	GM (PMU Karimganj)	
47	MKCIL/ASSAM/P KG-07/129	02.04.2025	Regarding Submission of Design Report for Main Carriageway & Service/Slip Road.	GM (PMU Karimganj)	
48	MKCIL/ASSAM/P KG-07/131	04.04.2025	Request Letter to provide access to Vehicles & Construction Machineries under Railway Bridge at Chainage 194+4.5 from Railway Department	GM (PMU Karimganj)	
49	MKCIL/ASSAM/P KG-07/132	04.04.2025	Submission Profile & Credential of Shyam Metalics & Energy Limited for Source Approval of TMT.	GM (PMU Karimganj)	
50	MKCIL/ASSAM/P KG-07/134	05.04.2025	Regarding Submission of GADs for 4 Nos. of Precast Box Culvert (1x2x2) (01+652, 01+973, 02+143, 03+646)	GM (PMU Karimganj)	
51	MKCIL/ASSAM/P KG-07/135	05.04.2025	Regarding Submission of Design & Drawings for 3 Nos. of Cast-in-Situ Box Culvert (1x2x2) (01+254, 02+440, 05+126).	GM (PMU Karimganj)	
52	MKCIL/ASSAM/P KG-07/136	05.04.2025	Regarding Submission of Design & Drawings for Box Culvert (1x3x3) (0+207, 0+341, & 4+340).	GM (PMU Karimganj)	
53	MKCIL/ASSAM/P KG-07/139	07.04.2025	Submission of Quality Assurance Plan	GM (PMU Karimganj)	
54	MKCIL/ASSAM/P KG-07/140	07.04.2025	Regarding Submission of GADs for 6 Nos. of Precast Box Culvert (1x2x2) (05+920, 06+190, 07+832, 12+663, 13+065, 13+380)	GM (PMU Karimganj)	
55	MKCIL/ASSAM/P KG-07/141	07.04.2025	Regarding Submission of Design & Drawings for LVUP at Ch. (03+886, & 10+098)	GM (PMU Karimganj)	
56	MKCIL/ASSAM/P KG-07/142	07.04.2025	Regarding Submission of Lower TDS deduction certificate.	GM (PMU Karimganj)	
57	MKCIL/ASSAM/P KG-07/145	10.04.2025	Regarding Submission of Design & Drawings for LVUP at Ch. (01+142) (1x12)	GM (PMU Karimganj)	
58	MKCIL/ASSAM/P KG-07/146	10.04.2025	Regarding Submission of Design & Drawings for Box Underpass at Ch. (04+534) (1x4x4)	GM (PMU Karimganj)	
59	MKCIL/ASSAM/P KG-07/147	10.04.2025	Regarding Submission of Design & Drawings for Box Underpass at Ch. (02+340, 07+906, & 08+296) (1x4x4)	GM (PMU Karimganj)	
60	MKCIL/ASSAM/P KG-07/150	14.04.2025	Submission of Construction Methodology	GM (PMU Karimganj)	
61	MKCIL/ASSAM/P KG-07/154	15.04.2025	Submission of Concrete Mix Design.	GM (PMU Karimganj)	
62	MKCIL/ASSAM/P KG-07/155	15.04.2025	Regarding Submission of D&D for LVUP at Ch. (04+212, 05+414, & 09+332).	GM (PMU Karimganj)	
63	MKCIL/ASSAM/P KG-07/158	17.04.2025	Regarding Compliance on Observation of Submitted 4Nos. GADs of Precast Box Culvert (1x2x2)	GM (PMU Karimganj)	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

64	MKCIL/ASSAM/P KG-07/159	17.04.2025	Regarding Submission of Design & Drawing for 5Nos. Of MNB at Ch. (06+313, 07+306, 09+003, 09+293, 14+195)	GM (PMU Karimganj)	
65	MKCIL/ASSAM/P KG-07/161	17.04.2025	Reg. Confirmation of communication Address & official Mail ID for correspondence	GM (PMU Karimganj)	
66	<u>MKCIL/ASSAM/P KG-07/162</u>	17.04.2025	Submission of Work Porgarm along with S-Curve.	GM (PMU Karimganj)	
67	<u>MKCIL/ASSAM/P KG-07/164</u>	18.04.2025	Regarding Submission of Typical Design & Drawing for Drain (GFRP Bar)	GM (PMU Karimganj)	
68	<u>MKCIL/ASSAM/P KG-07/167</u>	19.04.2025	Submission of profile & crdential of Elegant steel for source approval	GM (PMU Karimganj)	
69	<u>MKCIL/ASSAM/P KG-07/169</u>	19.04.2025	Regarding Compliance on Observation of Submitted D&D Box Culvert Ch. 0+207, 0+341 & 4+340 (1x3x3).	GM (PMU Karimganj)	
70	<u>MKCIL/ASSAM/P KG-07/170</u>	19.04.2025	Regarding Compliance on Observation of Submitted D&D for 3Nos. Cast-in-Situ Box Culvert (1x2x2) (01+254, 02+440, & 05+126)	GM (PMU Karimganj)	
71	<u>MKCIL/ASSAM/P KG-07/174</u>	21.04.2025	Request for provide permission through APDCL for Transformer installation by third party supply.	GM (PMU Karimganj)	
72	<u>MKCIL/ASSAM/P KG-07/175</u>	26.04.2025	Request for the clearance of hindrance of structures along with religious structures.	GM (PMU Karimganj)	
73	<u>MKCIL/ASSAM/P KG-07/176</u>	22.04.2025	Request to provide permission for movement of the construction vehicle on PWD road From PWD dept.	GM (PMU Karimganj)	
74	<u>MKCIL/ASSAM/P KG-07/177</u>	22.04.2025	Regarding Submission of Typical Design & Drawing for Friction Slab Crash Barrier (GFRP Bar)	GM (PMU Karimganj)	
75	<u>MKCIL/ASSAM/P KG-07/178</u>	29.04.2025	Notifying the delay in approval of Design & Drawing-reg	GM (PMU Karimganj)	
76	<u>MKCIL/ASSAM/P KG-07/179</u>	29.04.2025	Regarding Submission of GADs for 6 Nos. of Precast Box Culvert (1x2x2) (07+668, 09+543, 09+779, 10+529, 11+073, 11+921)	GM (PMU Karimganj)	
77	<u>MKCIL/ASSAM/P KG-07/180</u>	23.04.2025	Request to provide permission for movement of the construction vehicles during No Entry in day time period in Karimganj Town portion by District Administration for the Construction of National Highway Project Under Bharatmala of Public Interest.	GM (PMU Karimganj)	
78	<u>MKCIL/ASSAM/P KG-07/183</u>	24.04.2025	Regarding Submission of Typical Design & Drawing for ToeWall	GM (PMU Karimganj)	
79	<u>MKCIL/ASSAM/P KG-07/185</u>	05.05.2025	Regarding Submission of Pre-cast Box Culvert (1x2x2) GAD at Ch 08+188 & 08+576.	GM (PMU Karimganj)	
80	<u>MKCIL/ASSAM/P KG-07/186</u>	05.05.2025	Regarding Submission of Design & Drawing for Box Culvert at Ch. 04+018 (1x5x3)	GM (PMU Karimganj)	
81	<u>MKCIL/ASSAM/P KG-07/187</u>	06.05.2025	Submission of Project Video Recording.	GM (PMU Karimganj)	
82	<u>MKCIL/ASSAM/P KG-07/190</u>	08.04.2025	Submission of Monthly Progress Report for the month of April 2025	GM (PMU Karimganj)	
83	<u>MKCIL/ASSAM/P KG-07/195</u>	12.05.2025	Regarding Re-Submission of Pavement Design Report for Main Carriageway & Service /Slip Road	GM (PMU Karimganj)	
84	<u>MKCIL/ASSAM/P KG-07/204</u>	19.05.2025	Submission of Contract Price Weightage as per Annexure - I of Schedule-G of Concession Agreement	TL (TASPL)	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

85	<u>MKCIL/ASSAM/P KG-07/210</u>	22.05.2025	Regarding Damages of the PWD Rural Roads due to carrying of forest materials under Bharat Mala Project.	GM (PMU Karimganj)	
86	<u>MKCIL/ASSAM/P KG-07/211</u>	23.05.2025	Submission of Clarification Regarding illegal Excavation & Encroachment.	GM (PMU Karimganj)	
87	<u>MKCIL/ASSAM/P KG-07/215</u>	29.05.2025	Regarding Delay in Tree felling work Permission by the Forest Department.	GM (PMU Karimganj)	
88	<u>MKCIL/ASSAM/P KG-07/216</u>	29.05.2025	Regarding Compliance Submission on Observations for Project Design & Drawings Approval.	TL (TASPL)	
89	<u>MKCIL/ASSAM/P KG-07/218</u>	31.05.2025	Regarding Submission of Design & Drawing for ROB at Ch. 04+624 (P1, P2, & P3)	GM (PMU Karimganj)	

11.2 Inward Letter (NHIDCL)

Sr. No.	Letter No.	Date	Subject	From	Remarks
1	RO-GHY/Meeting Notice/0132/15036	27.05.2024	Review Meeting under the Chairmanship of ED (P), RO-Guwahati regarding the project awarded	RO (Guwahati)	
2	RO-GHY/Meeting Notice/0132/15561	30.07.2024	Director Sir shall be reviewing the projects under implementation in the State of Assam.	RO (Guwahati)	
3	NHIDCL/Assam/NH-37/Sil-Churai/Pkg-7/233357/3087	11.03.2024	Letter of Award	"NHIDCL (PMU-Karimganj)"	
4	NHIDCL/RO-GHY/2021/Labour/17178	19.03.2025	Issuance of FORM-III for Labour License under Contract Labour (Regulation & Abolition) Central Rules, 1971.	RO (Guwahati)	
5	NHIDCL/Assam/NH-37/Sil-Churai/Pkg-7/Part-I/46	21.03.2025	Declaration of Appointed Date	NHIDCL	
6	NHIDCL/PMU-Karimganj/SBC/Pkg-7/2024-25/54	03.09.2024	Regarding Indent through online portal of mineral minerals for the execution of above said project	GM (P), PMU Karimganj	
7	NHIDCL/PMU-Karimganj/MKC/APDCL/2024-25/138	29.11.2024	Provisional approval for construction and installation of 33kv, 11 kv, LT DTRs	GM PMU Karimganj	
8	<u>NHIDCL/PMU-Karimganj/MKC/Land/2024-25/140</u>	29.11.2024	Certificate of handing over and taking over of allotted land reg.	GM PMU Karimganj	
9	<u>NHIDCL/PMU-Karimganj/MKC/Pkg-7/2024-25/165</u>	23.12.2024	Signed Copy of GAD of ROB under Silchar-Churaibari PKG-7	NHIDCL (PMU-Karimganj)	
10	<u>NHIDCL/PMU-Karimganj/MKC/Pkg-7/2024-25/168</u>	23.12.2024	Possession certificate	GM PMU Karimganj	
11	<u>NHIDCL/PMU-Karimganj/APDCL/Pkg-7/2024-25/184</u>	14.01.2025	Consent Letter	NHIDCL (PMU-Karimganj)	
12	<u>NHIDCL/PMU-Karimganj/DC/Pkg-7/2024-25/192</u>	29.01.2025	Joint inspection for identification for extraction of Soil for Road works.	NHIDCL (PMU-Karimganj)	
13	<u>NHIDCL/PMU-Karimganj/DC/Pkg-7/2024-25/194</u>	29.01.2025	Joint inspection for identification for extraction of Soil for Road works.	NHIDCL (PMU-Karimganj)	
14	<u>NHIDCL/PMU-Karimganj/BSF/Pkg-7/2024-25/208</u>	15.02.2025	Permission with BSF-Work Intimation & Permission to Start Utility Shifting Works	NHIDCL (PMU-Karimganj)	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

15	<u>NHIDCL/PMU-Karimganj/MKC/Pkg-7/2024-25/216</u>	24.02.2025	Issue From-III under rule (Principal for obtaining Labour License).	Executive Director (RO Guwahati)	
16	<u>NHIDCL/PMU-Karimganj/MKC/Pkg-7/2024-25/231</u>	06.03.2025	Observation on submission of Contract Price Weightage as per Annexure-1 of Schedule-G.	GM (P), PMU Karimganj	
17	<u>NHIDCL/PMU-Karimganj/MKC/Pkg-7/2024-25/246</u>	26.03.2025	Estimates of Utility Shifting.	NHIDCL (PMU-Karimganj)	
18	<u>NHIDCL/PMU-Karimganj/DC/2024-25/250</u>	27.03.2025	Procurement of Earth/Soil under the Scheme of Amrit Sarovar	NHIDCL (PMU-Karimganj)	
19	<u>NHIDCL/PMU-Karimganj/Pkg-7/2025-26/262</u>	09.04.2025	Declaration of Appointed Date	NHIDCL (PMU-Karimganj)	
20	<u>NHIDCL/PMU-Karimganj/MKC/Pkg-7/2025-26/271</u>	15.04.2025	Observation on Submitted Pavement Design Report for Main Carriageway & Service/Slip	NHIDCL (PMU-Karimganj)	
21	<u>NHIDCL/PMU-Karimganj/MKC/Pkg-7/2025-26/275</u>	16.04.2025	Submission of Work Program along with S-Curve	NHIDCL (PMU-Karimganj)	
22	<u>NHIDCL/PMU-Karimganj/MKC/Pkg-7/2025-26/276</u>	16.04.2025	Observation on Submitted Design & Drawing for Box Culvert (1*3*3) at ch. 0+207, 0+341, & 4+340.	NHIDCL (PMU-Karimganj)	
23	<u>NHIDCL/PMU-Karimganj/MKC/Pkg-7/2025-26/277</u>	16.04.2025	Observation on Submitted Design & Drawing for 3Nos. Of Cast-in-Situ Box Culvert (1*2*2).	NHIDCL (PMU-Karimganj)	
24	<u>NHIDCL/PMU-Karimganj/MKC/Pkg-7/2025-26/278</u>	16.04.2025	Observation on Submitted GADs for 4Nos. Of Precast Box Culvert (1*2*2).	NHIDCL (PMU-Karimganj)	
25	<u>NHIDCL/PMU-Karimganj/MKC/Pkg-7/2025-26/307</u>	21.05.2025	Regarding illegal excavation & encroachment in SBC Pkg-07	NHIDCL (PMU-Karimganj)	
26	<u>NHIDCL/PMU-Karimganj/MKC/Pkg-7/2025-26/311</u>	21.05.2025	Regarding damages of the PWD rural roads due to carrying of forest materials under Bharat mala Project	NHIDCL (PMU-Karimganj)	
27	<u>TASPL-MAV/NH-37/MKCIL/2025/MAY/05</u>	22.05.2025	Source approval of CICO Technologies Limited.	TASPL	
28	<u>TASPL-MAV/NH-37/MKCIL/2025/MAY/07</u>	22.05.2025	Source approval of Dalmia Cement (Bharat) Limited.	TASPL	
29	<u>TASPL-MAV/NH-37/MKCIL/2025/MAY/08</u>	22.05.2025	Reg: Source approval of Reinforcement Steel for manufacturer Rashmi Metaliks Limited, SRMB Srijan Pvt.Ltd, Shyam Metaliks and Energy Limited, Elegant steel, Elegant Steel.	TASPL	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

CHAPTER-12

NON-CONFORMANCE REPORT

NIL

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

**CHAPTER-13
WEATHER REPORT**

<i>Sl no.</i>	<i>Date</i>	<i>Temperature (In °c)</i>		<i>Humidity (In %)</i>		<i>Rainfall (mm)</i>	<i>Weather Condition</i>
		<i>Maximum</i>	<i>Minimum</i>	<i>Maximum</i>	<i>Minimum</i>		
1	01-05-2025	27.8	25.3	86.0	79.0	6	Sunny/Cloudy
2	02-05-2025	27.5	25.0	84.0	78.0	0	Sunny/Cloudy
3	03-05-2025	29.1	26.1	80.0	72.0	0	Sunny
4	04-05-2025	29.5	26.4	75.0	69.0	20	Sunny/Rainy
5	05-05-2025	30.2	27.2	81.0	70.0	50	Sunny/Rainy
6	06-05-2025	29.5	25.9	81.0	74.0	0	Sunny
7	07-05-2025	30.5	24.7	77.0	71.0	40	Sunny/Rainy
8	08-05-2025	29.1	26.5	79.0	73.0	30	Sunny/Rainy
9	09-05-2025	29	27.1	78.0	72.0	19	Sunny/Rainy
10	10-05-2025	31.3	25.7	87.0	75.0	40.5	Sunny/Rainy
11	11-05-2025	28.1	26.0	84.0	77.0	65.2	Sunny/Rainy
12	12-05-2025	27.1	25.8	88.0	82.0	45	Cloudy/Rainy
13	13-05-2025	29.3	26.2	86.0	77.0	68.0	Cloudy/Rainy
14	14-05-2025	29.1	25.4	90.0	79.0	50.3	Cloudy/Rainy
15	15-05-2025	28.9	26.1	86.0	80.0	5	Cloudy/Rainy
16	16-05-2025	29	26.2	84.0	78.0	7	Cloudy/Rainy
17	17-05-2025	29.4	27.1	82.0	77.0	70	Cloudy/Rainy
18	18-05-2025	30	26.1	84.0	76.0	30.4	Cloudy/Rainy
19	19-05-2025	28.4	27.2	86.0	81.0	28	Cloudy/Rainy
20	20-05-2025	27.7	25.3	91.0	81.0	95.6	Cloudy/Rainy
21	21-05-2025	27.7	24.8	93.0	88.0	45	Cloudy/Rainy
22	22-05-2025	28.8	25.4	92.0	84.0	4.0	Cloudy/Rainy
23	23-05-2025	30.5	27.1	88.0	80.0	0	Sunny
24	24-05-2025	32	27.5	85.0	79.0	0	Sunny/Cloudy
25	25-05-2025	32.4	28.1	83.0	77.0	89	Sunny/Rainy
26	26-05-2025	31.9	29.2	82.0	78.0	25	Sunny/Rainy
27	27-05-2025	33.5	28.8	79.0	71.0	0	Sunny
28	28-05-2025	30.9	27.1	90.0	78.0	45.5	Rainy/Cloudy
29	29-05-2025	29.6	27.3	93.0	87.0	70	Rainy/Cloudy
30	30-05-2025	28.6	26.4	98.0	90.0	85	Rainy/Cloudy
31	31-05-2025	27.1	25.7	99.0	92.0	221.4	Rainy/Cloudy
Total Reinfall of this Month						1254.90	

The maximum & minimum weather records are summarized below:

TEMPERATURE/ RAINFALL PERIOD: 1st May, 2025 to 31st May, 2025				
Temperature		Rainfall		
Maximum (in °C)	Minimum (in °C)	Maximum (in mm)	Minimum (in mm)	Total Days
33.5	24.7	221.4	4.0	25

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

CHAPTER-14
ACCIDENT REPORT

NIL

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

CHAPTER-15

ROAD MAINTENANCE & SAFETY REPORT

The Traffic Safety Arrangements during the execution of works is being carried out by the Concessionaire for safe movement of vehicles on the project highway. The Concessionaire has provided sufficient road signs, temporary barriers, gunny bags filled with soil with reflective stickers etc. at the construction sites.

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

CHAPTER-16

SITE PHOTOGRAPHS



FDD Testing in Embankment Layer



Pot Hole repair in progress

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.



Electric Pole Shifting in progress



Soil Dumping in Embankment Layer in progress

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.



Box Culvert Excavation in Progress 13+065 LHS



Concrete Pouring of Pre-cast Box-culvert Segment

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.



TL sir site visit at ch-10+098 (LVUP)



Concrete Work in Progress at CH-10+098 LHS
