

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

Monthly Progress Report

August - 2025



Authority		National Highways Infrastructure Development Corporation Limited
Independent Engineer		M/s Technocrafts Advisory Services Private Limited in association with M/s MAV Associates LLP
Concessionaire		MKC Badarpur Churaibari Kamakhya (PKG-7) Highways Pvt. Ltd.

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

TABLE OF CONTENTS


CHAPTERS	DESCRIPTIONS	PAGES
	TABLE OF CONTENTS	
	Project Road Location Map / Index Map	
	EXECUTIVE SUMMARY	
	1. The Project Road	
	2. Mobilization	
	3. Pre-Construction Activity	
	4. EPC Contractor	
	5. Design & Drawing	
	6. Work Program	
	7. Quality Control & Material	
	8. Supervision and Monitoring of Project works	
	9. Site Visit and Meeting	
	10. Schedule Completion Date	
	11. Operation and Maintenance (O&M)	
	12. Area of Concern	
	13. Current Issues	
1	INTRODUCTION	
	General	
2	CONTRACT DATA	
3	SALIENT FEATURES OF PROJECT HIGHWAY	
	3.1 Pavement Composition (MCW)	
	3.2 Details of New/ Widening of Structures and Project Facilities	
4	SCOPE OF WORKS AND PROJECT FACILITIES	
	4.1 Scope of Works	
	4.2 Project Facilities	
5	PRE-CONSTRUCTION ACTIVITY	
	5.1 Obligations	
	5.2 Shifting of Utilities	
	5.3 Tree Cutting	
	5.4 Land Acquisition	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

	5.5 Hindrance, Payment Status and LA Status	
6	MOBILIZATION	
	6.1 Manpower Mobilization of Concessionaire	
	6.2 Organization Chart of Concessionaire	
7	DEPLOYMENT OF PLANTS AND EQUIPMENT / PROJECT SET UP PLAN	
	7.1 Plants and Equipment Deployed	
8	DESIGN AND DRAWING	
	8.1 Design	
	8.2 Drawing	
	8.3 Status of Drawings	
9	PROJECT WORK PROGRESS	
	9.1 Work Progress	
	9.2 Structure work Progress	
	9.3 Weightages of Components	
	9.4 S Curve of Project	
	9.5 Detailed Highway & Structure Works Progress	
10	QUALITY CONTROL AND MATERIAL	
	10.1 Quality Control	
	10.2 Site Laboratory	
	10.3 Material Testing	
	10.3.1 Soli and Aggregates	
	10.3.2 Cement	
	10.3.3 Reinforcement Steel	
	10.3.4 Status of Material Sources Approvals & Mix Designs	
	10.3.5 Details of QC Test conducted during the month	
11	CORRESPONDENCE	
12	NON-CONFORMANCE REPORT	
13	WEATHER REPORT	
14	ACCIDENT REPORT	
15	ROAD MAINTENANCE AND SAFETY REPORT	
16	PROJECT PROGRESS PHOTOGRAPHS	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

PROJECT ROAD LOCATION MAP / INDEX MAP

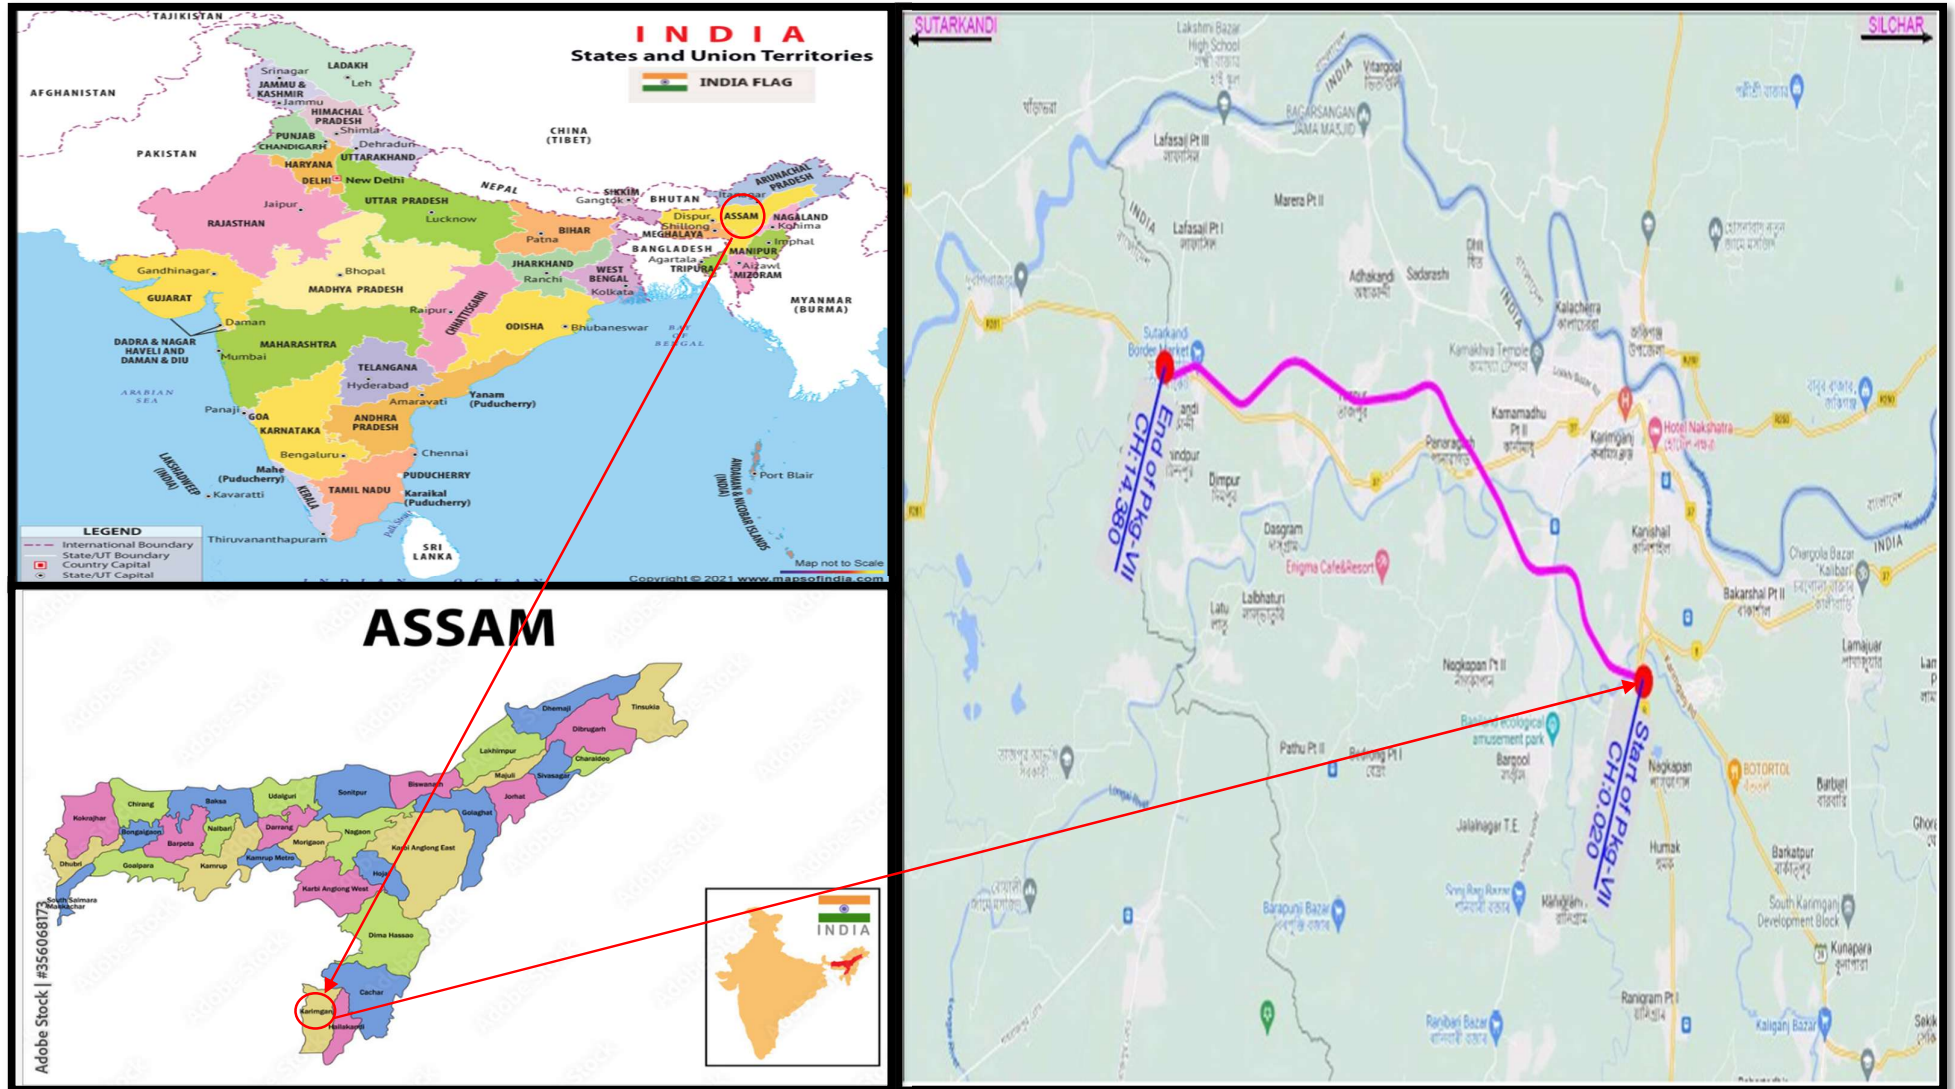

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

EXECUTIVE SUMMARY

The Concessionaire has signed the Concession Agreement with National Highway Infrastructure Development Corporation Limited (NHIDCL) on dated September 17, 2024. This Executive Summary presents the works progress of the Project Highway during the construction period from February 28, 2025 to February 27, 2027.

1. The Project Road:

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

2. Mobilization:

The Concessionaire has mobilized the required Engineers/ Staff Personnel, Machineries/Equipment's, Plants and established main Base Camp at CH: - 5+600 LHS (Darakona).

The details of Key staff personnel deployed are highlighted in the Chapter-6 of this report. The details of deployed Plants and Machineries are included in Chapter-7 of this report.

3. Pre-Construction Activity:

The Details of pre-construction activities have been included in Chapter-5 of this report.

4. EPC Contractor:

MKC Infrastructure Limited The Details of project highway works have been included in Chapter-09 of this report.

5.Design and Drawing

The status of approval of Working Drawings for road works and structures submitted to Authority as on dated 31-08-2025 is given below.

Sr. No.	Description	UoM	Scope	Submitted	Approved	Balance	Remarks
1.	Plan & Profile (MCW)	Km.	14.380	14.380	2.38	12.00	Patially approved only 2.380 kms
2.	Plan & Profile (SR)	Km.	4.16	4.16	0.00	4.16	
3.	RE Wall	SqM.	24984	0.00	0.00	0.000	
4.	ROB	Nos.	1.00	1.0	1.00	0.00	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

5.	Major Bridge	Nos.	3.00	2.00	0.00	0.00	
6.	Minor Bridge	Nos.	8.00	6.00	0.00	6.00	
7.	Underpasses	Nos.	16.00	13.00	12.00	1.00	
8.	Culvert	Nos.	32.00	30.00	25.00	5.00	

The details of design and drawing status have been included in this report on Chapter 8.

7. Work Program:

At the time of commencement of works, the Concessionaire submitted the Stage wise completion schedule Work Program Vide Letter No. MKCIL/ASSAM/PKG-07/162, dated 17.04.2025 for Authority/IE's approval. Based on the monthly works plan, the works is being carried out by the Concessionaire.

8. Quality Control and Material:

The works is being carried out by the Concessionaire as per Quality Assurance Plan submitted to Authority Vide Letter MKCIL/ASSAM/PKG-07/139 on dated 07.04.2025. Each construction activity is being checked/verified as per the RFI's submitted to Authority/ IE by the Concessionaire.

9. Supervision and Monitoring of Project works:

The Authority/ IE along with the concessionaire is supervising and monitoring the execution of works as per requirements of Standard/ Specifications. The monitoring of works is being carried out through the RFI submitted by the Concessionaire and its approval/ rejection after necessary checking/ verification by the Authority/ IE.

10. Site Visit and Meeting:

The Authority/ IE Engineers are regularly visiting the Project Highway.

11. Schedule Completion Date:

As per Schedule-G of the Concession Agreement shall occur on the 730th day from the Appointed Date. The declared Appointed Date being February 28, 2025, the Scheduled completion Date shall occur on February 27, 2027.

12. Operation and Maintenance (O&M):

O&M Obligations – During Operation Period, the Concessionaire shall operate and maintain the project in accordance with this Agreement either by itself, or through the O&M Contractor and if required, modify repair or otherwise make improvements to the Project to comply with the provisions of this Agreement, Applicable Laws and Applicable Permits, and conform to Specifications and Standards and Good industry Practice. The obligations of the concessionaire shall be as per Article 17.

13. Area of Concern/ Availability of site for work:

Procurement of ROW- The existing ROW and the stretches of 11.510 km. are subjected to following:

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

a) Stretches/ Hindered Free Land 11.51 Km out of 14.36 Km:

Stretches/ Hindered Free Land				Encumbrances/ Hindered Land		
Sr. No.	Side	Length (Km)	%	Side	Length (Km)	%
1.	BHS	11.510	80.20%	BHS	2.850	19.80%

b) Hindered due to Tree Cutting:

Description	Total Nos.	Impacted Length (km)	Remarks
Total Trees	407	7.0	

c) Encumbrances due to Religious Structure:

Sr. No.	Types	Chainage	Side	Remarks
1.	Small Temple	2+750	RHS	
2.	Temple	4+150	LHS	
3.	Kabristan	4+300	BHS	
4.	Masjid	4+500	BHS	
5.	Kabristan	7+300	BHS	

d) Details of Hidered Land:

DETAILS OF ENCUMBRANCES WITHIN ROW					
Sr. No	Chainage		Side	Total Length (KM)	Description
	From	To			
1	0+300	0+450	BHS	150.00	Brick Industry
2	2+600	3+000	BHS	400.00	Residential Houses
3	3+450	4+500	BHS	1050.00	Assam Type House Shade
4	5+300	5+650	BHS	350.00	Assam Type residential houses
5	6+500	6+600	BHS	100.00	RCC & Assam Type Houses
6	7+200	7+300	BHS	100.00	Assam/RCC Type Houses
7	9+100	9+400	BHS	300.00	Assam Type residential houses
8	10+700	10+800	BHS	100.00	Assam Type residential houses
9	10+850	10+900	BHS	50.00	Assam Type residential houses

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

10	11+250	11+400	BHS	150.00	Assam Type residential houses
11	11+900	12+300	BHS	400.00	Assam Type residential houses
12	12+400	14+000	BHS	1600.00	Assam Type residential houses
Total Hindered Length				4750.00	

Current Issues:-

- a) Non-availability of land:-** As per the Concession Agreement, 100% of the land is to be handed over to the Concessionaire within 90 days from the Appointed Date. However, only approximately 67% of the land is currently free from encumbrances.
- b) Schedule-G :-**The approval of Schedule-G remains pending as of now on the end of IE/Authority.
- c) Water logging in PROW :-** Due to heavy rainfall, water has accumulated along almost the entire length of the project within the ROW, which has hampered construction activities.
- d) Approval of Material Source:-** Approval from the Independent Engineer is still pending for the proposed material sources, including aggregates, admixtures, cement, and GFRP bars.

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

CHAPTER-1

INTRODUCTION

General

The NHIDCL proposes to implement the development, maintenance, and management of the Spur from NH-8 near Karimganj to Sutarkandi (India-Bangladesh border) Km. 0.020 to Km. 14.380 into 4-lane access controlled corridor. The proposed project road has been selected to improve connectivity and reduce travel time from Assam to Tripura. Also, this connectivity will improve international road connectivity between India and Bangladesh. To achieve the above task, NHIDCL has appointed M/s. Aarvee Associates Architects Engineers and Consultants Pvt. Ltd. The Letter of Acceptance was communicated vide letter No. NHIDCL / Assam / DPR / SilcharChuraibari /222542/2581 and the agreement was signed on September 1st, 2023.

This executive summary is submitted along with the Final detailed project report to cover the key aspects of the project.

Project Overview

As described earlier the project road is a spur to NH-8 near Karimganj and ends at Sutarkandi. The proposed alignment passes through Karimganj district in the state of Assam connecting villages Karimganj, Fakirabazar, Jarpata and Sutarkandi.

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

CHAPTER-2

CONTRACT DATA

Sr. No.	Items	Description
1.	Name of Project	4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.
2.	Project Length	14.250 km
3.	Project Bid Cost	380.26 Cr.
4.	Authority	National Highways & Infrastructure Development Corporation Limited
5.	Independent Engineer	M/s Technocrats Advisory Services Private Limited in association with M/s MAV Associates LLP
6.	Concessionaire	MKC Badarpur Churaibari Kamakhya (PKG-7) Highways Private Limited
7.	Design Consultant	Geo Designs & Research Pvt. Ltd.
8.	DPR Consultant	Aarvee Associates Architects Engineers & Consultants Pvt. Ltd.
9.	LOA No. & Date	NHIDCL/ Assam/ NH-37/ Sil-Churai/ Pkg-VII/ 233357/ 3087 dated 11.03.2024
10.	Date of Concession Agreement	September 17, 2024
11.	Appointed Date	February 28, 2025
12.	Construction Period	730 days (from Appointed Date) [24-Months]
13.	Schedule Completion Date	February 27, 2027
14.	O&M Period	15 Years from the date of COD

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

14	Project Milestone	
	Milestone- I	The Project Milestone-I shall occur on the date falling on the 256th (two hundred and fifty sixth) day from the Appointed Date (i.e., November 11, 2025)- (The concessionaire shall have expended not less than 20% of the total capital cost set forth in the Financial Package and the Concessionaire shall have commenced construction of the Project and achieved 20% Physical Progress)
	Milestone- II	438th Day from Appointed Date (i.e., May 12, 2026)- (Prior to the occurrence of Project Milestone-II, the Concessionaire shall have expended not less than 35% of the total capital cost set forth in the Financial Package. Provided, however, that at least 70% of the expenditure referred to hereinabove shall have been incurred on physical works which shall not include advances of any kind to any person or expenditure of any kind on plant and machinery and the concessionaire shall have commenced construction of the project and achieved 35% Physical Progress.).
	Milestone- III	620th Day from Appointed Date (i.e., November 10, 2026) (The concessionaire shall have commenced construction of all Project Facilities and expended not less than 75% of the total capital cost set forth in the Financial Package and the concessionaire shall have commenced construction of the Project and achieved 75% Physical Progress).
	Scheduled Completion Date	730th Day from Appointed Date (i.e., February 27, 2027) The concessionaire shall have completed the Project in accordance with the Concession Agreement.

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

CHAPTER -3

SALIENT FEATURES OF PROJECT HIGHWAY

3.1 Pavement Composition (For Main Carriage Way/ Service Road)

Section	Design Chainage		Stretch in Km.	Pavement Composition in mm.						
	From	To		Sub-Grade	R-GSB	R-WMM	DBM	BC	DLC	PQC
MCW	00+020	12+900	12.880	500.00	200.00	180.00	50.00	40.00	-	-
	12+900	14+380	1.480	500.00	150	-	-	-	150	180
				Sub-Grade	GSB	R-WMM	DBM	BC		
Service Road				500.00	200.00	180.00	50.00	30.00		

3.2 Details of New/ Widening of Structures and Project Facilities to be constructed along the project Highway:

Sr. No.	Description		Unit	As per CA	Remarks
1.	Railway over Bridge	New Construction	Nos.	1	
2.	Major Bridge	New Construction	Nos.	3	
3.	Minor Bridge	New Construction	Nos.	7	
		Reconstruction	Nos.	1	
4.	VUP	New Construction	Nos.	2	
5.	LVUP	New Construction	Nos.	9	
6.	SVUP	New Construction	Nos.	1	
7.	Box Underpass	New Construction	Nos.	4	
8.	Box Culvert	New Construction	Nos.	28	
		Reconstruction	Nos.	4	
9.	Hume Pipe Culvert	New Construction	Nos.	20	
10.	Bus Bay		Nos.	2	
11.	Major Junction		Nos.	2	
12.	Minor Junction		Nos.	4	
13.	W-beam Single faced metal crash barrier		Rmt.	17602	
14.	Drain (covered)		Rmt.	2960	

CHAPTER -4

SCOPE OF THE WORKS AND PROJECT FACILITIES

4.1 Scope of Works

The Schedule-B of the Concession Agreement specifies the scope of works. The broad scope of the works includes the following:

- Reconstruction of existing 2 lane carriageway to 4 lane divided carriageway including strengthening existing carriageway by providing bituminous overlays in accordance with the Specifications and Standards.
- Construction of 1- ROB, 3- Major Bridge, 8- Minor Bridge, 16- Underpasses, 52- Culverts.
- Construction of Slip Road of 4.16 Km

4.2 Project Facilities

The Schedule-C of the Concession Agreement specifies the project facilities to be constructed for the project highway. The project facilities include the following:

- a) Toll Plaza
- b) Roadside Furniture
 - i. Kilometer and Hectometer Stones
 - ii. Traffic Signs
 - iii. Overhead Sign
 - iv. Road Marking
 - v. Road Delineators
 - vi. Reflective Pavement Markers & Solar Studs
 - vii. Traffic Impact Attenuators
 - viii. Boundary wall and Fencing
- c) Operation and Maintenance centres
- d) Way side Amenities/ Service Areas
- e) Truck Lay-byes
- f) Bus Bay and Bus Shelter
- g) Pedestrian Facilities
- h) Highway Lighting
- i) Rainwater Harvesting
- j) Environmental Management Plan
- k) Land Scaping and Tree Plantation
- l) Advanced Traffic Management System (ATMS)
- m) Highway Petrol Unit
- n) Emergency Medical Services
- o) Crane Services

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

CHAPTER -5

PRE-CONSTRUCTION ACTIVITIES

5.1 Obligations

Obligations of Authority-

Sr. No.	Clause No.	Obligation	Status	Remark/ Reference
1	Clause 4.1.2	Condition Precedent	Done	MKCIL/ASSAM/PKG-07/261
2	Article 11	Utilities, Associated Roads and Trees	In Progress	
3	Clause 18.1.2	Safety Consultant	Not done	
4	Article 21	Appointment of Independent Engineer	Done	Partially Mobilized
5	Clause 10.3	Joint Memorandum	Done	

Obligations of Concessionaire-

Sr. No.	Clause No.	Obligation	Status	Remark/ Reference
1	Clause 9.1	Performance Security	Done	
2	Article 11	Shifting and Relocation Electrical Utilities	In Progress	
3	Article 26	Insurance	Done	
4	Clause 4.1.3 (Schedule-E)	Applicable Permits	Done	
5		A permission of State Govt. for boulders extraction	Done	
6		Permission of Village Panchayet and Pollution Board for installation of crushers	Done	
7		License for use of explosives	N/A	
8		Permission of the State Govt. from drawing water from river/ reservoir	N/A	
9		Labour Licence	Done	
10	Clause 12.1	Quality Assurance Plan	Done	MKCIL/ASSAM/PKG-07/139 dt. 07.04.2025
11		Construction Methodology	Done	MKCIL/ASSAM/PKG-07/150 dt. 14.04.2025

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

5.2 Shifting of Utilities

The project works includes shifting/relocation of various utility services along the project road. The details of the utilities/ Hindrances are required to be shifted/ relocated/ removed along the Project Highway is summarized below:

Sl. No.	Utility/ Hindrance Type	Unit	Nos.	Remarks
1.	HT/ LT Lines (including Transformer if any)	Nos.	88.00	In progress
2.	HT/ LT crossing	Nos.	65.00	In progress
3.	Water Pipelines	Kms	4.00	In progress
4.	Water Pipeline Crossing	Nos.	14.00	In progress

5.3 Tree Cutting

The tree cutting status is given below for the project highway.

Sr. No.	Description	Total	Remarks
1.	Total Number of Trees	407.00	
2.	Total Felling of Trees	47.00	
3.	Balance Trees	360.00	

5.4 Land Acquisition

The detailed working of Existing ROW, Proposed ROW and Land to be Acquired along the project highway are submitted by NHIDCL vide Joint Handover Memorandum on dated 28th of February ,2025.

The detail of affected area for construction of the project road including various project facilities which requires prime attention to accelerate the work progress is given below.

HINDRANCE LIST – CHAINAGE WISE DETAILS

DETAILS OF ENCUMBRANCES WITHIN ROW					
Sr. No	Chainage		Side	Total Length (KM)	Description
	From	To			
1	0+300	0+450	BHS	150.00	Brick Industry
2	2+600	3+000	BHS	400.00	Residential Houses
3	3+450	4+500	BHS	1050.00	Assam Type House Shade
4	5+300	5+650	BHS	350.00	Assam Type residential houses
5	6+500	6+600	BHS	100.00	RCC & Assam Type Houses

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

6	7+200	7+300	BHS	100.00	Assam/RCC Type Houses
7	9+100	9+400	BHS	300.00	Assam Type residential houses
8	10+700	10+800	BHS	100.00	Assam Type residential houses
9	10+850	10+900	BHS	50.00	Assam Type residential houses
10	11+250	11+400	BHS	150.00	Assam Type residential houses
11	11+900	12+300	BHS	400.00	Assam Type residential houses
12	12+400	14+000	BHS	1600.00	Assam Type residential houses
Total Hindered Length				4750.00	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

CHAPTER -6

MOBILIZATION

6.1 Manpower Mobilization of Concessionaire

Sr. No.	Name of Employee	Designation	Department
1	Satish Kumar Pandey	Sr. GM	HQ
2	Ashish Kumar Pandey	Project Manager	Project
3	Dhirendra Thapa	Asst. Manager	HR/Admin
4	Saurabh Kumar	Sr. Executive	HR/Admin
5	Golu Meena	Supervisor (Mess)	HR/Admin
6	Shyam babu Singh	Manager	Liaison
7	Deepak Sharma	Executive	Liaison
8	Jagdish Pandey	Asst. Manager	Billing and Planning
9	Ranjan Akash Jha	Sr. Engineer	Billing
10	Surajit Samanta	Engineer	Billing
11	Vageesh Tripathi	Senior Engineer	Structure
12	Ranjan Kumar	Senior Engineer	Structure
13	Souvik Paul	Engineer	Structure
14	Deepak Chauhan	Engineer	Structure
15	Ankit Chaurasia	Supervisor	Structure
16	Avneesh Kumar Pandey	Dy. Manager	Highway
17	Samarjeet Singh	Engineer	Highway
18	Rishab Pal	Senior Engineer	Highway
19	Tapas Basak	Engineer	Highway
20	Jay Prakash Singh	Senior Supervisor	Highway
21	Anmol	Supervisor	Highway
22	Md. Mohbub Ahmed	Supervisor	Highway
23	Imrat Ahirwar	Supervisor	Highway
24	Yogendra Rai	Supervisor	Highway
25	Ratan Thakur	Supervisor	Highway
26	Krishna Singh	Supervisor	Highway
27	Jayanta Mallick	Sr. Surveyor	Survey
28	Koushik Rout	Sr. Surveyor	Survey
29	Amit Singh	Surveyor	Survey
30	Subrata Dinda	Sr. Manager	P & M
31	Amit Bhaduria	Executive	P & M
32	Ramkaran Sahu	Engineer	P & M
33	Deepak Thakur	Executive	P & M
34	Amit Tiwari	Supervisor	P & M
35	INDRAJIT MAJUMDER	Supervisor	P & M
36	Prabhakar Kumar	Jr. Engineer	P & M
37	Subham Kar	Supervisor	P & M
38	Surajit Das	Asst. Manager	Store
39	Pankaj Baser	Jr. Executive	Store
40	Amit Sikarwar	Sr. Executive	Store
41	Deepak Purty	Jr. Executive	Store
42	Sujeet Sharma	Supervisor	Store
43	Sumanta Datta	Supervisor	Store
44	Milan Samanta	Supervisor	Store
45	Ravi Shankar Tripathi	Sr. Manager	QA/QC
46	Subham Singh	Asst. Engineer	QA/QC
47	Daya Shankar	Lab Tech.	QA/QC
48	Ramprakash Mishra	Lab Tech.	QA/QC
49	Ranjan Kumar	Engineer	QA/QC

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

50	Kapil Sharma	Executive	Accounts
----	--------------	-----------	----------

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

CHAPTER-7

DEPLOYMENT OF PLANTS AND EQUIPMENT / PROJECT SET UP PLAN

7.1 Plants and Equipment Deployed

S.no	Equipment type	UNIT	QTY	Remarks
1	LMV	Nos.	7	
2	TIPPER	Nos.	28	
3	MOBILE CRANE	Nos.	2	
4	SOIL COMPACTOR	Nos.	5	
5	EXCAVATOR	Nos.	10	
6	BACK HOE LOADER	Nos.	4	
7	DIESEL DISPENCER	Nos.	2	
8	TRANSIT MIXER	Nos.	10	
9	TRACTOR	Nos.	2	
10	GRADER	Nos.	3	
11	BABY ROLLER	Nos.	1	
12	HM PLANT	Nos.	1	
13	BATCHING PLANT	Nos.	1	
14	RE BLOCK PLANT	Nos.	1	
15	DG	Nos.	2	
16	TRAILER	Nos.	1	
17	CRUSHER	Nos.	1	
18	WATER TANKER	Nos.	1	
19	LOADER	Nos.	1	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

CHAPTER-8

DESIGN AND DRAWING

The project highway has been designed for four lane divided carriageway facility with provision of central raised median of 1.6m. The Concession Agreement envisages design of the project highway by the Concessionaire. The scope of design includes the design for road works, structure works and other project facilities. The drawings need to be prepared and approved for execution of each component of the project highway.

8.1 Design

The design of road works e.g., plans and profiles, cross sections and other miscellaneous items are being prepared by the Concessionaire for approval and execution of works accordingly. Similarly, the design of various structures e.g., Major bridge, Minor bridges, Vehicular Underpasses, Box Culverts, Hume Pipe Culverts etc. are also being prepared by the Concessionaire for review by Authority/ IE.

8.2 Drawings

As per requirement of the Contract Agreement various drawings are being prepared for execution and completion of the works. The working drawings of road works and structure works are being prepared by the Concessionaire and submitted to the Authority/ Independent Engineer prior to execution of works at site.

8.3 Status of Approval of Drawings

The status of drawing submission and approval of GAD for road and structure works as on August-31, 2025, is enclosed in this chapter of the report.

Road Works

S N	Description	Unit	Total	Submitted	Approval	Balance	Remarks
1.	Plan & Profile MCW	Km	14.360	14.360	2.380	12.000	
2.	Plan & Profile SR	Km	4.164	4.164	0.000	0.000	
3.	Typical Cross Section	Nos	1.00	1.00	0.00	0.00	
4.	Pavement Design Report	Nos	1.00	1.00	1.00	0.00	
5.	RE Wall	Nos	20820.00	-	-	-	
6.	Major Junction	Nos	2.00	-	-	-	
7.	Minor Junction	Nos	4.00	-	-	-	
8.	Bus Bay Drawing	Nos	2.00	-	-	-	
9.	Road Signage Plan	Km	14.360	-	-	-	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

Structure Works:-

Structure				
Description	Total Nos	Submitted	Approved	Balance
Box Underpass	4	4	4	0.00
SVUP	1	1	0	1.00
LVUP	9	8	8	0.00
VUP	2	0	0	0.00
MNB	8	6	0	6.00
MJB	3	2	0	2.00
ROB	1	1	1	0.00
Box Culvert	32	30	25	5.00

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

CHAPTER-9
PROJECT WORK PROGRESS

9.1 Work Progress:


Progress as per Schedule G for the month August-2025.

Schedule-G								
Item	Stage for measurement of Physical Progress	Unit	Qty.	Weightage in percentage to the contract price	Unit Rate	Qty	Physical Progress (%)	Value of Physical Progress(%)
Road works including culverts, minor bridges, underpasses, overpasses, approaches to ROB/RUB/ Major Bridges/ Structures (but excluding service roads)	B- New 4 Lane Realignment/Bypass							
	(1) Earthwork upto top of Sub-grade	L-Km	27.23	28.70%	4,00,78,960.71	0.13	0.46%	0.13%
	(2) Granular work (Sub-base, base, shoulder)							
	(a) GSB	L-Km	27.23	4.12%	57,51,143.99			
	(b) WMM	L-Km	24.27	2.74%	42,88,948.20			
	(c) Shoulder	L-Km	27.23	0.69%	9,57,102.64			
	(4) Bituminous Work							
	(a) DBM	L-Km	24.27	1.89%	29,66,516.06			
	(b) BC	L-Km	24.27	1.25%	19,51,962.03			
	(5) Rigid Pavement (MCW)							
	(a) DLC	L-Km	2.96	0.35%	44,75,433.79			
	(b) PQC	L-Km	2.96	0.83%	1,06,67,741.47			
	Sub Total-B							
	C- New Culverts, Minor Bridges, underpasses, overpasses on existing road, realignment, bypasses:							
	1) Culverts (Precast)							
	a) On Casting (40%)	No.	64.00	1.82%	10,83,196.14	17.00	26.56%	0.48%
	b) On Erection (60%)	No.	64.00	2.73%	16,24,794.22	5.00	7.81%	0.21%
	2) Minor Bridge							
	a) Foundation	No.	22.00	2.76%	47,78,175.33			
	b) Sub-Structure	No.	22.00	1.27%	21,95,967.62			
	c) Super-Structure (including Crash Barrier etc. Complete) If pre-cast girders/segments are used, 40% of the weightage of the stage in percentage to the bid project cost is assigned to the casting of such precast girders/ segments.							
	c-i) Precast Girder - On Casting (40%)	No.	6.00	0.72%	45,47,436.78			
	c-ii) Slab - after Completion of Slab (60%)	No.	16.00	1.08%	25,57,933.19			
	5) Grade Separated Structures							
	a) Underpasses (Box Underpass, SVUP, LVUP, VUP)							
	i) Foundation	No.	38.00	5.32%	53,22,182.07	8.00	21.05%	1.12%
	ii) Sub-Structure	No.	38.00	3.61%	36,16,174.69	6.00	15.79%	0.57%
	b) Super-Structure (including Crash Barrier/Wearing coat etc. Complete) If pre-cast girders/segments are used, 40% of the weightage of the stage in percentage to the bid project cost is assigned to the casting of such precast girders/ segments.							
	- Girder Type - Precast Girder (40%)	No.	6.00	1.41%	89,64,598.35			
	- Girder Type - Cast in situ superstructure (60%)	No.	32.00	2.12%	25,21,293.29	2.00	6.25%	0.13%
Major Bridge works and ROB/RUB	C- New Major Bridges							
	(1) Foundation (Pile Foundation)	No.	24.00	5.92%	93,84,097.57			
	(2) Sub-structure	No.	24.00	1.62%	25,59,815.73			
	(3) Super-structure (including crash barriers etc. complete) If pre-cast girders/segments are used, 40% of the weightage of the stage in percentage to the bid project cost is assigned to the casting of such precast girders/ segments.							
	-Super-structure - Precast Girder (40%)	No.	18.00	1.10%	23,16,837.65			
	-Super-structure - Cast in situ superstructure (60%)	No.	18.00	1.65%	34,75,256.47			
	D- New rail-road bridges							
	(a) ROB							
	(1) Foundation	No.	10.00	2.50%	95,15,158.71			
	(2) Sub-structure	No.	10.00	1.06%	40,47,650.45			
	(3) Super-structure (including crash barriers etc. complete) If pre-cast girders/segments are used, 40% of the weightage of the stage in percentage to the bid project cost is assigned to the casting of such precast girders/ segments.							
	-Super-structure - Precast Girder (40%)	No.	8.00	0.90%	42,71,286.31			
	-Super-structure - Cast in situ superstructure (60%)	No.	8.00	1.35%	64,06,929.46			
	Sub Total-C							
Structures (Elevated Section, Reinforced earth)	4) Reinforced Earth Wall (includes Approaches of ROB, Underpasses, Over passes, Flyover etc.)							
	i) Re Block Casting (5%)	Sq.m	20,820.00	0.03%	60.60			
	ii) Re Block Erection (95%)	Sq.m	20,820.00	0.63%	1,151.33			
Electrical and Public Health Utilities	UTILITY SHIFTING							
	HT/LT lines (including Transformers if any)	Km	4.36	0.04%	3,36,550.04	2.00	45.87%	0.02%
	HT/LT crossings	No.	65.00	1.03%	6,05,167.46	18.00	27.69%	0.29%
	Water pipeline	Km	4.65	0.03%	2,24,664.82	2.00	43.01%	0.01%
	Water pipeline crossings	No.	14.00	0.06%	1,64,442.40			
Other Works	OTHER WORKS							
	i) Service Road / Slip Road	L-Km	4.164	0.96%	87,79,204.05			
	ii) Road Side Drain	L-Km	2.96	0.44%	56,10,789.71			
	iv) - Road signs, markings, Km Stone, Safety devices							
	(a) Road signs, markings, Km Stone	L-Km	14.36	0.30%	8,04,517.48			
	(b) Concrete Crash Barrier/W Beam Crash Barrier in Road work	L-Km	30.90	2.42%	29,75,950.78			
	v) - Project Facilities							
	(a) Bus bay	No.	2.00	0.08%	15,06,243.98			
	(b) Rain Water Harvesting	No.	28.00	0.17%	2,25,984.04			
	vii) Protection Work							
	(a) Boulder Piling on Slope / Slope Protection Work	L-Km	4.32	2.32%	2,04,40,582.47			
	(b) Precast Toe Wall / Retaining Wall							
	-On Casting (40%)	L-Km	13.81	4.38%	1,20,73,559.83			
	-On Erection (60%)	L-Km	13.81	6.58%	1,81,10,339.75			
	viii) Miscellaneous							
	(a) Street Lighting	No.	280.00	0.10%	13,253.97			
	(b) Junction/Interchange	No.	6.00	0.21%	13,07,460.45			
	(c) Precast Boundary Wall							
	-On Casting (40%)	L-Km	27.23	0.17%	2,34,974.06			
	-On Erection (60%)	L-Km	27.23	0.25%	3,52,461.09			
	(d) ATMS, HTMS, Traffic Aid Posts, Medical aid Posts, Vehicle Rescue Posts, Telecom System	L-Km	28.72	0.29%	3,80,244.14			
Grand Total >>>				100.00%				2.97%

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

9.2 S Curve

S Curve

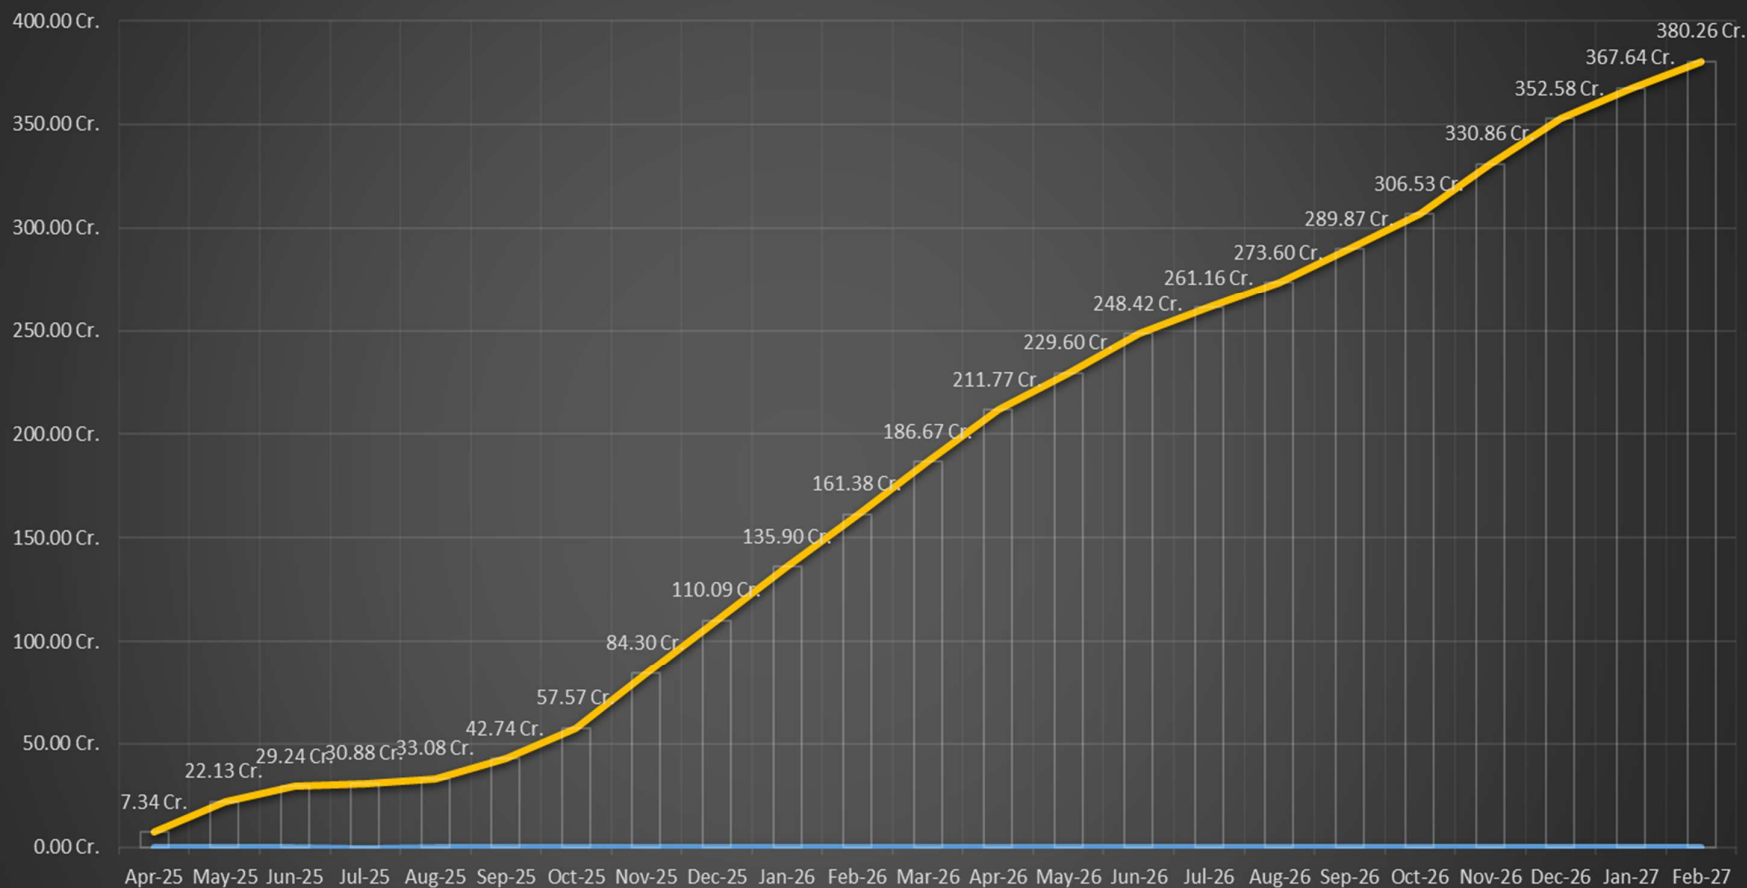


	Apr-25	May-25	Jun-25	Jul-25	Aug-25	Sep-25	Oct-25	Nov-25	Dec-25	Jan-26	Feb-26	Mar-26	Apr-26	May-26	Jun-26	Jul-26	Aug-26	Sep-26	Oct-26	Nov-26	Dec-26	Jan-27	Feb-27
Plan in %	1.93%	3.89%	1.87%	0.43%	0.58%	2.54%	3.90%	7.03%	6.78%	6.79%	6.70%	6.65%	6.60%	4.69%	4.95%	3.35%	3.27%	4.28%	4.38%	6.40%	5.71%	3.96%	3.32%
Cumulative Amount	7.34 Cr	22.13 Cr	29.24 Cr	30.88 Cr	33.08 Cr	42.74 Cr	57.57 Cr	84.30 Cr	110.09 Cr	135.90 Cr	161.38 Cr	186.67 Cr	211.77 Cr	229.60 Cr	248.42 Cr	261.16 Cr	273.60 Cr	289.87 Cr	306.53 Cr	330.86 Cr	352.58 Cr	367.64 Cr	380.26 Cr

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

9.3 Weightages

Work Description	% of Each sub components	Amount (Cr.)
Sub Grade	28.70%	1,09,15,10,416.04
Granular Work	7.54%	28,68,02,317.28
Bituminous Work	3.14%	11,93,91,137.27
Rigid Pavement	1.18%	4,48,23,798.78
Culverts	4.56%	17,33,11,383.05
Minor Bridges	5.83%	22,16,42,696.68
Grade Separated Structures	12.47%	47,41,26,532.16
Major Bridge	10.28%	39,09,11,613.49
ROB	5.81%	22,10,53,817.77
RE Wall	0.66%	2,52,32,255.77
Utility Shifting	1.16%	4,41,50,128.16
Slip Road	0.96%	3,65,56,605.68
Road Side Drain & Median Drain	0.44%	1,66,07,937.55
Road Signs, Marking, Km Stone, & etc.	2.72%	10,35,21,653.80
Project Facilities	0.25%	93,40,041.20
Protection Work	13.28%	50,51,42,969.52
Miscellaneous Work	1.01%	3,84,74,695.83
Total	100.00%	3,80,26,00,000.00

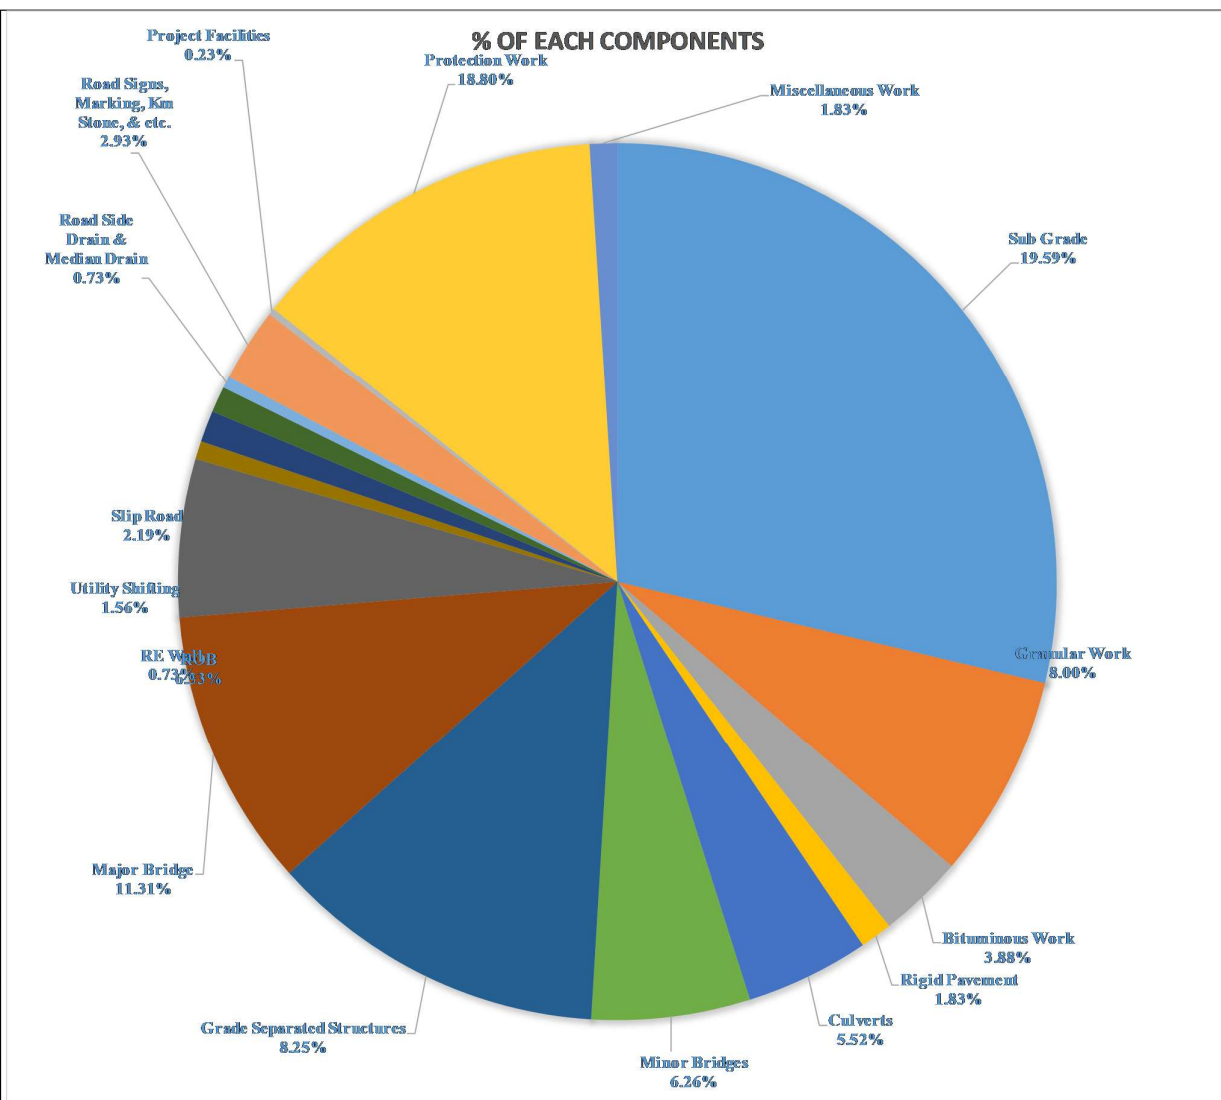

9.4 Highway Progress:

Page 25 of 50

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

RHS		LHS	
Chainage	BC DBM R-WMM R-GSB Sub-Grade Embankment C&G	Chainage	BC DBM R-WMM R-GSB Sub-Grade Embankment C&G
5+030		4+030	
5+040		4+040	
5+050		4+050	
5+060		4+060	
5+070		4+070	
5+080		4+080	
5+090		4+090	
5+100		4+100	
5+110		4+110	
5+120		4+120	
5+130	BC 5+126	4+130	
5+140		4+140	
5+150		4+150	
5+160		4+160	
5+170		4+170	
5+180		4+180	
5+190		4+190	
5+200		4+200	
5+210		4+210	
5+220		4+220	
5+230		4+230	
5+240		4+240	
5+250		4+250	
5+260		4+260	
5+270		4+270	
5+280		4+280	
5+290		4+290	
5+300		4+300	
5+310		4+310	
5+320		4+320	
5+330		4+330	
5+340		4+340	
5+350		4+350	
5+360		4+360	
5+370		4+370	
5+380		4+380	
5+390		4+390	
5+400		4+400	
5+410		4+410	
5+420		4+420	
5+430		4+430	
5+440		4+440	
5+450		4+450	
5+460		4+460	
5+470		4+470	
5+480		4+480	
5+490		4+490	
5+500		4+500	
5+510		4+510	
5+520		4+520	
5+530		4+530	
5+540		4+540	
5+550		4+550	
5+560		4+560	
5+570		4+570	
5+580		4+580	
5+590		4+590	
5+600		4+600	
5+610		4+610	
5+620		4+620	
5+630		4+630	
5+640		4+640	
5+650		4+650	
5+660		4+660	
5+670		4+670	
5+680		4+680	
5+690		4+690	
5+700		4+700	
5+710		4+710	
5+720		4+720	
5+730		4+730	
5+740		4+740	
5+750		4+750	
5+760		4+760	
5+770		4+770	
5+780		4+780	
5+790		4+790	
5+800		4+800	
5+810		4+810	
5+820		4+820	
5+830		4+830	
5+840		4+840	
5+850		4+850	
5+860		4+860	
5+870		4+870	
5+880		4+880	
5+890		4+890	
5+900		4+900	
5+910		4+910	
5+920		4+920	
5+930		4+930	
5+940		4+940	
5+950		4+950	
5+960		4+960	
5+970		4+970	
5+980		4+980	
5+990		4+990	
6+000		5+000	
6+010		5+010	
6+020		5+020	

MJB 5+322
3 x 37.50

MJB 5+322
3 x 37.50

LVP 5+414 (1x12.0)

LVP 5+414 (1x12.0)

BC 5+126

BC 5+126

BC 5+126

BC 5+126

BC 3+418

BC 3+418

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

		RHS		Chainage		LHS	
	BC			C&G	6+030		BC
	DBM			Embankment	6+040		DBM
	R-WMM			Sub-Grade	6+050		R-WMM
				R-GSB	6+060		R-GSB
					6+070		Sub-Grade
					6+080		Embankment
					6+090		
					6+100		
					6+110		
					6+120		
					6+130		
					6+140		
					6+150		
					6+160		
					6+170		
					6+180		
					6+190		BC 6+190
					6+200		
					6+210		
					6+220		
				6+230			
				6+240			
				6+250			
				6+260			
				6+270			
				6+280			
				6+290			
				6+300			
				MNB 6+313 (1x15.0)		MNB 6+313 (1x15.0)	
				6+320			
				6+330			
				6+340			
				6+350			
				6+360			
				6+370			
				6+380			
				6+390			
				6+400			
				6+410			
				6+420			
				6+430			
				6+440			
				6+450			
				6+460			
				6+470			
				6+480			
				6+490			
				6+500			
				6+510			
				6+520			
				6+530			
				6+540			
				6+550			
				6+560			
				6+570			
				6+580			
				6+590			
				6+600			
				6+610			
				6+620			
				6+630			
				BC 6+642		BC 6+642	
				6+650			
				6+660			
				6+670			
				6+680			
				6+690			
				6+700			
				6+710			
				6+720			
				6+730			
				6+740			
				6+750			
				6+760			
				6+770			
				6+780			
				6+790			
				6+800			
				6+810			
				6+820			
				6+830			
				6+840			
				6+850			
				6+860			
				6+870			
				6+880			
				6+890			
				6+900			
				6+910			
				6+920			
				6+930			
				6+940			
				6+950			
				6+960			
				6+970			
				6+980			
				6+990			
				7+000			
				7+010			
				7+020			

[illegible]

RHS	LHS
BC	BC
DBM	DBM
R-WMM	R-GSB
Sub-Grade	Sub-Grade
Embankment	Embankment
C&G	C&G
Chainage	Chainage
8+030	8+030
8+040	8+040
8+050	8+050
8+060	8+060
8+070	8+070
8+080	8+080
8+090	8+090
8+100	8+100
8+110	8+110
8+120	8+120
8+130	8+130
8+140	8+140
8+150	8+150
8+160	8+160
8+170	8+170
8+180	8+180
BC 8+188	BC 8+188
8+200	8+200
8+210	8+210
8+220	8+220
8+230	8+230
8+240	8+240
8+250	8+250
8+260	8+260
8+270	8+270
8+280	8+280
8+290	8+290
8+300	8+300
8+310	8+310
8+320	8+320
8+330	8+330
8+340	8+340
8+350	8+350
8+360	8+360
8+370	8+370
8+380	8+380
8+390	8+390
8+400	8+400
8+410	8+410
8+420	8+420
8+430	8+430
8+440	8+440
8+450	8+450
8+460	8+460
8+470	8+470
8+480	8+480
8+490	8+490
8+500	8+500
8+510	8+510
8+520	8+520
8+530	8+530
8+540	8+540
8+550	8+550
8+560	8+560
8+570	8+570
BC 8+576	BC 8+576
8+590	8+590
8+600	8+600
8+610	8+610
8+620	8+620
8+630	8+630
8+640	8+640
8+650	8+650
8+660	8+660
8+670	8+670
8+680	8+680
8+690	8+690
8+700	8+700
8+710	8+710
8+720	8+720
8+730	8+730
8+740	8+740
8+750	8+750
8+760	8+760
8+770	8+770
8+780	8+780
8+790	8+790
8+800	8+800
8+810	8+810
8+820	8+820
8+830	8+830
8+840	8+840
8+850	8+850
8+860	8+860
8+870	8+870
8+880	8+880
8+890	8+890
8+900	8+900
8+910	8+910
8+920	8+920
8+930	8+930
8+940	8+940
8+950	8+950
8+960	8+960
8+970	8+970
8+980	8+980
8+990	8+990
MNB 9+003 (166.0)	MNB 9+003 (166.0)
9+000	9+000
9+010	9+010
9+020	9+020

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

	LHS						Chainage	RHS					
	BC	DBM	R-WMM	R-GSB	Sub-Grade	Embankment		BC	DBM	R-WMM	R-GSB	Sub-Grade	Embankment
							9+030						
							9+040						
							9+050						
							9+060						
							9+070						
							9+080						
							9+090						
							9+100						
							9+110						
							9+120						
							9+130						
							9+140						
							9+150						
							9+160						
							9+170						
							9+180						
							9+190						
							9+200						
							9+210						
							9+220						
							9+230						
							9+240						
							9+250						
							9+260						
							9+270						
							9+280						
							9+290						
							9+300						
							9+310						
							9+320						
							9+330						
							9+340						
							9+350						
							9+360						
							9+370						
							9+380						
							9+390						
							9+400						
							9+410						
							9+420						
							9+430						
							9+440						
							9+450						
							9+460						
							9+470						
							9+480						
							9+490						
							9+500						
							9+510						
							9+520						
							9+530						
							9+540						
							9+550						
							9+560						
							9+570						
							9+580						
							9+590						
							9+600						
							9+610						
							9+620						
							9+630						
							9+640						
							9+650						
							9+660						
							9+670						
							9+680						
							9+690						
							9+700						
							9+710						
							9+720						
							9+730						
							9+740						
							9+750						
							9+760						
							9+770						
							9+780						
							9+790						
							9+800						
							9+810						
							9+820						
							9+830						
							9+840						
							9+850						
							9+860						
							9+870						
							9+880						
							9+890						
							9+900						
							9+910						
							9+920						
							9+930						
							9+940						
							9+950						
							9+960						
							9+970						
							9+980						
							9+990						
							10+000						
							10+010						
							10+020						

	LHS						Chainage	RHS					
	BC	DBM	R-WMM	R-GSB	Sub-Grade	Embankment		BC	DBM	R-WMM	R-GSB	Sub-Grade	Embankment
							10+030						
							10+040						
							10+050						
							10+060						
							10+070						
							10+080						
							10+090						
							10+100						
							10+110						
							10+120						
							10+130						
							10+140						
							10+150						
							10+160						
							10+170						
							10+180						
							10+190						
							10+200						
							10+210						
							10+220						
							10+230						
							10+240						
							10+250						
							10+260						
							10+270						
							10+280						
							10+290						
							10+300						
							10+310						
							10+320						
							10+330						
							10+340						
							10+350						
							10+360						
							10+370						
							10+380						
							10+390						
							10+400						
							10+410						
							10+420						
							10+430						
							10+440						
							10+450						
							10+460						
							10+470						
							10+480						
							10+490						
							10+500						
							10+510						
							10+520						
							10+530						

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

[illegible][illegible][illegible]

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

9.5.1 Status of Box Culvert

S N	LHS												Box Culvert Chainage	RHS											
	Protection Work	Parapet Wall	Top Slab	Top Haunch	Wall Final Lift	Wall 2nd Lift	Wall 1st Lift	Haunch	Raft	PCC/Granular Bed	Layout & Excavation	Abutment		Layout & Excavation	PCC/Granular Bed	Raft	Haunch	Wall 1st Lift	Wall 2nd Lift	Wall Final Lift	Top Haunch	Top Slab	Parapet Wall	Protection Work	
1												A1	00+043	A1											
2												A2	00+207	A2											
												A1		A1											
3												A2	00+341	A2											
												A1		A1											
4												A2	01+254	A2											
												A1		A1											
5												A2	01+652	A2											
												A1		A1											
6												A2	01+973	A2											
												A1		A1											
7												A2	02+143	A2											
												A1		A1											
8												A2	02+440	A2											
												A1		A1											
9												A2	03+418	A2											
												A1		A1											
10												A2	03+646	A2											
												A1		A1											
11												A2	03+925	A2											
												A1		A1											
12												A2	04+018	A2											
												A1		A1											
13												A2	04+340	A2											
												A1		A1											
14												A2	04+847	A2											
												A1		A1											
15												A2	05+126	A2											
												A1		A1											
16												A2	05+920	A2											
												A1		A1											
17												A2	06+190	A2											
												A1		A1											
18												A2	06+642	A2											
												A1		A1											
19												A2	07+668	A2											
												A1		A1											
20												A2	07+832	A2											
												A1		A1											
21												A2	08+188	A2											
												A1		A1											
22												A2	08+576	A2											
												A1		A1											
23												A2	09+543	A2											
												A1		A1											
24												A2	09+779	A2											
												A1		A1											
25												A2	10+529	A2											
												A1		A1											
26												A2	11+073	A2											
												A1		A1											
27												A2	11+921	A2											
												A1		A1											
28												A2	12+223	A2											
												A1		A1											
29												A2	12+663	A2											
												A1		A1											
30												A2	13+065	A2											
												A1		A1											
31												A2	13+380	A2											
												A1		A1											
32												A2	13+740	A2											
												A1		A1											

1	Not Available	1
2	In Progress	
3	Completed	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

9.5.2 Status of Minor Bridge

SN	LHS												Minor Bridge Chainage	RHS												
	Miscellaneous Item	Crash Barrier	Approach Slab	Desk Slab	PSC Girder	Pedestal	Dirt Wall	Abutment Cap	Abutment Wall	Abutment Pile Cap	Abutment Pile	Layout & Excavation		Abutment	Layout & Excavation	Abutment Pile	Abutment Pile Cap	Abutment Wall	Abutment Cap	Dirt Wall	Pedestal	PSC Girder	Desk Slab	Approach Slab	Crash Barrier	Miscellaneous Item
1													A1	00+742	A1											
													A2		A2											
2													A1	01+768	A1											
													A2		A2											
3													A1	06+313	A1											
													A2		A2											
4													A1	07+306	A1											
													A2		A2											
5													A1	09+003	A1											
													A2		A2											
6													A1	09+293	A1											
													A2		A2											
7													A1	11+363	A1											
													A2		A2											
8													A1	14+195	A1											
													A2		A2											

1	Not Available	1
2	In Progress	
3	Completed	

9.5.3 Status of Major Bridge

[illegible]

1	Not Available	1
2	In Progress	
3	Completed	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

9.5.4 Status of ROB

SN	LHS											Major Bridge & ROB Chainage	RHS																			
	Miscellaneous Item	Crash Barrier	Approach Slab	Desk Slab	PSC Girder	Pedestal	Dirt Wall	Pier Cap	Pier Column	Abutment/ Pier Cap	Abutment Wall		Abutment/ Pier Pile Cap	Abutment/ Pier Pile	Layout & Excavation	Abutment	Abutment/ Pier Pile Cap	Abutment/ Pier Pile	Layout & Excavation	Abutment	Abutment/ Pier Pile Cap	Abutment Wall	Abutment/ Pier Cap	Pier Column	Pier Cap	Dirt Wall	Pedestal	PSC Girder	Desk Slab	Approach Slab	Crash Barrier	Miscellaneous Item
1															A1				A1													
															P1				P1													
															P2				P2													
															P3				P3													
															A2				A2													

1	Not Available	1
2	In Progress	
3	Completed	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

9.5.5 Status of Underpass

SN	LHS											LVUP & SVUP Chainage	RHS												
	Miscellaneous Item	Crash Barrier	Approach Slab	Top Slab Bracket	Top Slab Haunch	RCC Top Slab	Abutment Wall	Bottom Slab Haunch	Raft	PCC/Granular Bed	Layout & Excavation		Abutment	Abutment	Layout & Excavation	PCC/Granular Bed	Raft	Bottom Slab Haunch	Abutment Wall	RCC Top Slab	Top Slab Haunch	Top Slab Bracket	Approach Slab	Crash Barrier	Miscellaneous Item
1												A1	01+142	A1											
												A2		A2											
2												A1	03+886	A1											
												A2		A2											
3												A1	04+212	A1											
												A2		A2											
4												A1	05+414	A1											
												A2		A2											
5												A1	07+213	A1											
												A2		A2											
6												A1	09+332	A1											
												A2		A2											
7												A1	10+098	A1											
												A2		A2											
8												A1	10+834	A1											
												A2		A2											
9												A1	12+310	A1											
												A2		A2											
1												A1	SVUP	A1											
												A2	03+728	A2											

1	Not Available	1
2	In Progress	
3	Completed	

CHAPTER-10

QUALITY CONTROL AND MATERIAL

10.1 Quality Control

The execution of works is mainly governed by the specified Technical Specifications for the project. The quality control of the works is required to be monitored on daily basis both at site and in the laboratory. Standard formats have been devised to control the required quality of the works. The Concessionaire Engineers are monitoring the required quality control works and maintaining the records accordingly for each item of works being executed.

10.2 Site Laboratory

The Site Laboratory is established at Base Camp located at CH: -5+600. All the required material tests are being conducted in the laboratory for the project road.

10.3 Materials Testing & Third Party Test

The testing to be carried out in the site laboratory includes tests of soil, aggregates, cement, steel, sand, embankment fill, sub grade, granular subbase and cement concrete. The details of test conducted up to 31 August, 2025 are enclosed.

10.3.1 Soil and Aggregates

The test reports for borrow area earth for available borrow area are approved & test reports for Aggregates are also approved for the available Quarry. Test reports for new borrow area earth are submitted to IE for approval.

10.3.2 Cement

The Concessionaire is using approved sources of Cement as Black Tiger (OPC 53 Grade), Dalmia Cement (OPC 53 Grade), Star Cement (OPC 53 Grade), Amrit Cement (OPC 53 Grade) & Max Cement (OPC 53 Grade) for the project work.

10.3.3 Reinforcement Steel

The Concessionaire is using approved sources of TMT from M/s Rashmi Metaliks Limited, M/s Shyam Steel Industries limited, M/s SRMB Srijan Private Limited, M/s Shyam Metalics and Energy Limited.

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

10.3.4 Status of materials source approval & Mix Design

Cement				
Sr. No.	Brand Name	Letter No.	Status	IE Letter No.
1.	Black Tiger Cement	MKCIL/ASSAM/PKG-07/106 dt. 24.03.2025		
2.	Dalmia Cement	MKCIL/ASSAM/PKG-07/107 dt. 24.03.2025	Approved	TASPL-MAV/NH-37/MKCIL/2025/MAY/34
3.	Max Cement	MKCIL/ASSAM/PKG-07/108 dt. 24.03.2025		
4.	Star Cement	MKCIL/ASSAM/PKG-07/109 dt. 24.03.2025		
5.	Amrit Cement	MKCIL/ASSAM/PKG-07/110 dt. 24.03.2025		

Reinforcement Steel				
Sr. No.	Brand Name	Letter No.	Status	IE Letter No.
1.	Rashmi Metaliks Limited	MKCIL/ASSAM/PKG-07/111 dt. 24.03.2025	Principle Approved	TASPL-MAV/NH-37/MKCIL/2025/MAY/27
2.	Shyam Steel industries Ltd.	MKCIL/ASSAM/PKG-07/112 dt. 24.03.2025	Principle Approved	TASPL-MAV/NH-37/MKCIL/2025/MAY/26
3.	SRMB Srijan Pvt. Ltd.	MKCIL/ASSAM/PKG-07/113 dt. 24.03.2025	Principle Approved	TASPL-MAV/NH-37/MKCIL/2025/MAY/32
4.	Shyam Metalics & Energy Ltd.	MKCIL/ASSAM/PKG-07/132 dt. 04.04.2025		
5.	Elegant steel	MKCIL/ASSAM/PKG-07/167 dt. 19.04.2025	Approved	TASPL-MAV/NH-37/MKICL/2025/AUG/59

Admixture				
Sr. No.	Brand Name	Letter No.	Status	IE Letter No.
1.	Berger Paints Pvt. Ltd.	MKCIL/ASSAM/PKG-07/101 dt. 24.03.2025		
2.	CHRYSO India Pvt. Ltd	MKCIL/ASSAM/PKG-07/102 dt. 24.03.2025		
3.	CICO Technologies Ltd.	MKCIL/ASSAM/PKG-07/103 dt. 24.03.2025		
4.	FOSROC Chemicals (India) Ltd.	MKCIL/ASSAM/PKG-07/104 dt. 24.03.2025		
5.	Vista Chemtech Pvt. Ltd.	MKCIL/ASSAM/PKG-07/105 dt. 24.03.2025		

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

Monthly Laboratory Report

Summary of Quality Control Test For The Month of AUGUST-2025																	
Sr.No.	Name of test	Reference as per IS/ MoRT&H	Frequency of Tests	Total Tests Conducted upto Previous Month			No. of Tsts Conducted during this Month			No. of Tests Conducted upto this Month			No. of Tests cChecked by IE			% Checked by IE	Remarks
				Tested	Passed	Failed	Tested	Passed	Failed	Tested	Passed	Failed	Tested	Passed	Failed		
LAB & FIELD TEST'S																	
(I). OGL Samples		IRC 36-2010															
1.1	Free Swelling Index (FSI)	IS : 2720 (P-40)	1 Test / Every 500 m Interval's	30	30	0	0	0	0	30	30	0	0	0	0	0.00	
1.2	Grain size analysis	IS : 2720 (P-4)	1 Test / Every 500 m Interval's	30	30	0	0	0	0	30	30	0	0	0	0	0.00	
1.3	Liquid limits (LL)	IS : 2720 (P-5)	1 Test / Every 500 m Interval's	30	30	0	0	0	0	30	30	0	0	0	0	0.00	
1.4	Plasticity Index (PI)	IS : 2720 (P-5)	1 Test / Every 500 m Interval's	30	30	0	0	0	0	30	30	0	0	0	0	0.00	
1.5	Proctor test (MDD & OMC)	IS : 2720 (P-8)	1 Test / Every 500 m Interval's	30	30	0	0	0	0	30	30	0	0	0	0	0.00	
1.6	California Bearing Ratio Test (CBR)	IS : 2720 (P-16)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
1.7	Field Compaction Test (OGL)	IS : 2720 (P-28)	1 Set / 3000 Sqm. (1Set = 10 Piv's)	323	310	13	0	0	0	323	310	13	0	0	0	0.00	
(II). Borrow area Samples (EMB/SG)		MoRT&H (Clause-305)															
2.1	Free Swelling Index (FSI)	IS : 2720 (P-40)	2 Test's / 3000 Cum.	36	36	0	0	0	0	0	0	0	0	0	0	0.00	
2.2	Grain size analysis (GSA)	IS : 2720 (P-4)	2 Test's / 3000 Cum.	36	36	0	0	0	0	0	0	0	0	0	0	0.00	
2.3	Liquid limits (LL)	IS : 2720 (P-5)	2 Test's / 3000 Cum.	36	36	0	0	0	0	0	0	0	0	0	0	0.00	
2.4	Plasticity Index (PI)	IS : 2720 (P-5)	2 Test's / 3000 Cum.	36	36	0	0	0	0	0	0	0	0	0	0	0.00	
2.5	Proctor test (MDD & OMC)	IS : 2720 (P-8)	2 Test's / 3000 Cum.	36	36	0	0	0	0	0	0	0	0	0	0	0.00	
2.6	California Bearing Ratio Test (CBR)	IS : 2720 (P-16)	1 Test's / 3000 Cum.	18	18	0	0	0	0	0	0	0	0	0	0	0.00	
2.7	Field Compaction Test (Emb)	IS : 2720 (P-28)	1 Set / 3000 Sqm. (1Set = 10 Piv's)	297	275	22	0	0	0	0	0	0	0	0	0	0.00	
2.8	Field Compaction Test (Subgrade)	IS : 2720 (P-28)	1 Set / 2000 Sqm. (1Set = 10 Piv's)	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
(III). Coarse Agg. for Concrete Work's		MoRT&H Table -900-6															
4.1	Gradation of Coarse Aggregate	IS : 2386 (P-1)	1 Test / Every day's work	99	82	17	26	26	0	125	108	17	6	6	0	23.08	
4.2	Flakiness Index (FI)	IS : 2386 (P-1)	1 Test for source / Weekly	22	18	4	4	4	0	26	22	4	2	2	0	50.00	
4.3	Aggregate Impact Value (A.I.V)	IS : 2386 (P-4)	1 Test for source / Weekly	22	18	4	4	4	0	26	22	4	2	2	0	50.00	
4.4	Specific Gravity	IS : 2386 (P-3)	1 Test / Source	3	3	0	0	0	0	3	3	0	0	0	0	0.00	
4.5	Water Absorption	IS : 2386 (P-3)	1 Test / Source	3	3	0	0	0	0	3	3	0	0	0	0	0.00	
4.6	Deleterious Constituents	IS : 2386 (P-2)	1 Test / As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
4.7	Moisture correction	IS : 2386 (P-3)	1 Test / Day	71	71	0	26	26	0	97	97	0	6	6	0	23.08	
4.8	Soundness	IS : 2386 (P-5)	1 Test / Source	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
4.9	Alkali Aggregate Reactivity	IS : 2386 (P-7)	1 Test / Source	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
(IV). Fine Agg. for Concrete		MoRT&H Table -900-6															
5.1	Gradation	IS : 383	1 Test / Every day's work	77	77	0	26	26	0	103	103	0	6	6	0.0	23.08	
5.2	Specific Gravity	IS : 2386 (P-3)	1 Test / Source	3	3	0	0	0	0	3	3	0	0	0	0	0.00	
5.3	Water Absorption	IS : 2720 (P-3)	1 Test / Source	3	3	0	0	0	0	3	3	0	0	0	0	0.00	
5.4	Silt Content	IS : 383	1 Test / Weekly	18	18	0	4	4	0	22	22	0	2	2	0.0	50.00	
5.5	Moisture correction	IS : 2386 (P-3)	1 Test / Every day's work	71	71	0	26	26	0	97	97	0	6	6	0.0	23.08	
(V). Concrete Cube's Compressive Strength Test		IS: 516															
▲ Grade of Concrete : M-10 PCC																	
6.1	for 7 days	IS : 516	As per Frequency MoRT&H Table 1700-09	15	15	0	6	6	0	21	21	0	1	1	0	16.67	
6.2	for 28 days	IS : 516	As per Frequency MoRT&H Table 1700-09	33	33	0	2	2	0	35	35	0	00	05	0	0.00	
▲ Grade of Concrete : M-15 PCC																	
6.3	for 7 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
6.4	for 28 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
▲ Grade of Concrete : M-20 PCC																	
6.5	for 7 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
6.6	for 28 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
▲ Grade of Concrete : M-20 RCC																	
6.7	for 7 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
6.8	for 28 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
▲ Grade of Concrete : M-20 for KERB																	
6.9	for 7 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
6.1	for 28 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
▲ Grade of Concrete : M-25 RCC																	
6.11	for 7 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	8	8	0	8	8	0	0	0	0	0.00	
6.12	for 28 days	IS : 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00	
▲ Grade of Concrete : M-30 RCC																	
6.13	for 7 days	IS : 516	As per Frequency MoRT&H Table 1700-09	62	62	0	20	20	0	82	82	0	4	4	0	20.00	
6.14	for 28 days	IS : 516	As per Frequency MoRT&H Table 1700-09	114	114	0	49	49	0	163	163	0	7	7	0	14.29	
▲ Grade of Concrete : M-35 RCC																	
6.15	for 7 days	IS : 516	As per Frequency MoRT&H Table 1700-09	12	12	0	4	4	0	16	16	0	1	1	0	25.00	
6.16	for 28 days	IS : 516	As per Frequency MoRT&H Table 1700-09	24	24	0	24	24	0	48	48	0	5	5	0	20.83	

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

Grade of Concrete : M-35 Pile																
6.17	for 7 days	IS: 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00
6.18	for 28 days	IS: 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00
Grade of Concrete : M-35 RE BLOCK																
6.19	for 7 days	IS: 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00
6.2	for 28 days	IS: 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00
Grade of Concrete : M-40 RCC																
6.21	for 7 days	IS: 516	As per Frequency MoRT&H Table 1700-09	0	0	0	1	1	0	1	1	0	0	0	0	0.00
6.22	for 28 days	IS: 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00
Grade of Concrete : M-45 RCC/PSC																
6.23	for 7 days	IS: 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00
6.24	for 28 days	IS: 516	As per Frequency MoRT&H Table 1700-09	0	0	0	0	0	0	0	0	0	0	0	0	0.00
Grouting of PSC Girders																
6.25	for 7 days	IS: 516	As per Frequency MoRT&H	0	0	0	0	0	0	0	0	0	0	0	0	0.00
6.26	for 28 days	IS: 516	As per Frequency MoRT&H	0	0	0	0	0	0	0	0	0	0	0	0	0.00
(VI). Common																
7.1	Finess of Cement	IS: 4031 (P-1)	1 Test Every Batch of Cement	5	5	0	7	7	0	12	12	0	2	2	0	28.57
7.2	Normal Consistency	IS: 4031 (P-4)	1 Test Every Batch of Cement	5	5	0	7	7	0	12	12	0	2	2	0	28.57
7.3	Initial Setting Time	IS: 4031 (P-5)	1 Test Every Batch of Cement	5	5	0	7	7	0	12	12	0	2	2	0	28.57
7.4	Final Setting time	IS: 4031 (P-5)	1 Test Every Batch of Cement	5	5	0	7	7	0	12	12	0	2	2	0	28.57
7.5	Compressive Strength (03 Days)	IS: 516	1 Test Every Batch of Cement	6	3	0	7	7	0	13	10	0	2	2	0	28.57
7.6	Compressive Strength (07 Days)	IS: 516	1 Test Every Batch of Cement	4	2	0	7	7	0	11	9	0	2	2	0	28.57
7.7	Compressive Strength (28 Days)	IS: 516	1 Test Every Batch of Cement	3	2	0	1	1	0	4	3	0	1	1	0	100.00
7.8	Soundness	IS: 4031 (P-3)	1 Test Every Batch of Cement	0	0	0	0	0	0	0	0	0	0	0	0	0.00
7.9	Specific Gravity	IS: 4031 (P-11)	1 Test Every Batch of Cement	0	0	0	0	0	0	0	0	0	0	0	0	0.00
(VII). Granular Sub-Base (GSB) MoRT&H Clause - 401																
8.1	Gradation	Table 400-2	1 Test /400 Cum.	0	0	0	0	0	0	0	0	0	0	0	0	0.00
8.2	Liquid limits (LL)	IS: 2720 (P-5)	1 Test /400 Cum.	0	0	0	0	0	0	0	0	0	0	0	0	0.00
8.3	Plasticity Index (PI)	IS: 2720 (P-5)	1 Test /400 Cum.	0	0	0	0	0	0	0	0	0	0	0	0	0.00
8.4	Moisture Prior to Compaction Test	IS: 2720 (P-2)	1 Test /400 Cum.	0	0	0	0	0	0	0	0	0	0	0	0	0.00
8.5	Proctor test (MDD & OMC)	IS: 2720 (P-8)	1 Test Per Source / As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
8.6	California Bearing Ratio Test (CBR)	IS: 2720 (P-16)	1 Test Per Source / As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
8.7	Water Absorption	IS: 2720 (P-3)	1 Test Per Source / As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
8.8	Aggregate Impact Value (AIV)	IS: 2386 (P-4)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
8.9	Field Compaction Test (GSB)	IS: 2720 (P-28)	1 Set / 1000 Sqm. (1Set = 3 Pit's)	0	0	0	0	0	0	0	0	0	0	0	0	0.00
(VIII). Cement Treated Sub Base (CTSB) MoRT&H Clause - 403 & IRC-37: 2018																
9.1	Gradation	MoRT&H Table 400-4	1 Test 400 Cum.	0	0	0	0	0	0	0	0	0	0	0	0	0.00
9.2	Liquid limits (LL)	IS: 2720 (P-5)	1 Test 400 Cum.	0	0	0	0	0	0	0	0	0	0	0	0	0.00
9.3	Plasticity Index (PI)	IS: 2720 (P-5)	1 Test 400 Cum.	0	0	0	0	0	0	0	0	0	0	0	0	0.00
9.4	Proctor test (MDD & OMC)	IS: 2720 (P-8)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
9.5	Unconfined Compressive Strength (UCS)	IS: 516	3 Specimens each 400 ton/ Minimum 2 tests per day	0	0	0	0	0	0	0	0	0	0	0	0	0.00
9.6	Cement Content	IS: 516	3 Specimens each 400 ton/ Minimum 2 tests per day	0	0	0	0	0	0	0	0	0	0	0	0	0.00
9.7	Flexural Strength	IS: 516	3 Specimens each 400 ton/ Minimum 2 tests per day	0	0	0	0	0	0	0	0	0	0	0	0	0.00
9.8	Soundness Test	BIS: 4332 (P-4)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
9.9	Field Compaction Test (CTSB)	IS: 2720 (P-28)	2 Test's 500 Sqm.	0	0	0	0	0	0	0	0	0	0	0	0	0.00
(IX). Cement Treated Base (CTB) MoRT&H Clause - 403 & IRC-37: 2018																
10.1	Gradation	MoRT&H Table 400-4	1 Test 400 Cum.	0	0	0	0	0	0	0	0	0	0	0	0	0.00
10.2	Proctor test (MDD & OMC)	IS: 2720 (P-8)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
10.3	Unconfined Compressive Strength (UCS)	IS: 516	3 Specimens each 400 ton/ Minimum 2 tests per day	0	0	0	0	0	0	0	0	0	0	0	0	0.00
10.4	Cement Content	IS: 516	3 Specimens each 400 ton/ Minimum 2 Tests per day	0	0	0	0	0	0	0	0	0	0	0	0	0.00
10.5	Flexural Strength	IS: 516	3 Specimens each 400 ton/ Minimum 2 Tests per day	0	0	0	0	0	0	0	0	0	0	0	0	0.00
10.6	Soundness Test	BIS: 4332 (P-4)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
10.7	Field Compaction Test (CTSB)	IS: 2720 (P-28)	2 Test's 500 Sqm.	0	0	0	0	0	0	0	0	0	0	0	0	0.00
(X). Wet Mix Macadam (WMM) MoRT&H-406																
11.1	Gradation	Table 400-13	1 Test /200 Cum.	0	0	0	0	0	0	0	0	0	0	0	0	0.00
11.2	Atterberg limits (LL & PI)	IS: 2720 (P-5)	1 Test /200 Cum.	0	0	0	0	0	0	0	0	0	0	0	0	0.00
11.3	Proctor test (MDD Vs OMC)	IS: 2720 (P-8)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
11.4	Aggregate Impact Value (A.I.V)	IS: 2386 (P-4)	1 Test/ 1000 Cum	0	0	0	0	0	0	0	0	0	0	0	0	0.00
11.5	Combined Flakiness & Elongation (FI & EL)	IS: 2386 (P-1)	1 Test /500 Cum	0	0	0	0	0	0	0	0	0	0	0	0	0.00
11.6	Water Absorption	IS: 2386 (P-3)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
11.7	Soundness	IS: 2386 (P-3)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
11.8	Field Compaction Test (WMM)	IS: 2720 (P-28)	1 Set / 1000 Sqm. (1Set = 3 Pit's)	0	0	0	0	0	0	0	0	0	0	0	0	0.00
(XI). Aggregate Inter Layer (AIL) MoRT&H-406																
12.1	Gradation	Table 400-13	1 Test /200 Cum.	0	0	0	0	0	0	0	0	0	0	0	0	0.00
12.2	Atterberg limits (LL & PI)	IS: 2720 (P-5)	1 Test /200 Cum.	0	0	0	0	0	0	0	0	0	0	0	0	0.00
12.3	Proctor test (MDD & OMC)	IS: 2720 (P-8)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
12.4	Aggregate Impact Value (A.I.V)	IS: 2386 (P-4)	1 Test/ 1000 Cum	0	0	0	0	6	0	6	0	0	0	0	0	0.00
12.5	Combined Flakiness & Elongation (FI & EL)	IS: 2386 (P-1)	1 Test /500 Cum	0	0	0	0	0	0	0	0	0	0	0	0	0.00
12.6	Water Absorption	IS: 2386 (P-3)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
12.7	Soundness	IS: 2386 (P-3)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
12.8	Field Compaction Test (AIL)	IS: 2720 (P-28)	1 Set / 1000 Sqm. (1Set = 3 Pit's)	0	0	0	0	0	0	0	0	0	0	0	0	0.00

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

(XII). Dense Bituminous Macadam (DBM)		MoRT&H-500														
13.1	Binder Content & Gradation	As per MoRT&H	1 Test / 400 Tonnes	0	0	0	0	0	0	0	0	0	0	0	0	0.00
13.2	Mix Combined Gradation	As per MoRT&H	1 Test / 400 Tonnes	0	0	0	0	0	0	0	0	0	0	0	0	0.00
13.3	Marshall Test (In Sets)	ASTM-D-1559	1 Set/ 400 Tonnes	0	0	0	0	0	0	0	0	0	0	0	0	0.00
13.4	Aggregate Impact Value (AIV)	IS : 2386 (P-4)	1 Test / 350 Cum	0	0	0	0	0	0	0	0	0	0	0	0	0.00
13.5	Combined Flakiness & Elongation (FI & EI)	IS : 2386 (P-1)	1 Test / 350 Cum	0	0	0	0	0	0	0	0	0	0	0	0	0.00
13.6	Water Absorption & Specific Gravity	IS : 2386 (P-3)	1 Test/ Source & As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
13.7	Stripping Value	IS : 6241	1 Test/ Source & As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
13.8	Maximum Sp.Gravity(Gmm)	ASTM D 2041	1 Set/ 400 MTMix	0	0	0	0	0	0	0	0	0	0	0	0	0.00
13.9	Density of compacted layer	MoRT&H Sec:900	1 Test / 700 Sqm	0	0	0	0	0	0	0	0	0	0	0	0	0.00
13.10	Soundness	IS : 2386 (P-3)	1 Test/ Source & As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
13.11	Sand equivalent test	IS : 2720 (P-37)	1 Test/ Source & As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
13.12	plasticity Index	MoRT&H Sec:900	1 Test/ Source & As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
13.13	percentage of Fractured face	MoRT&H Sec:900	1 Test/ Source & As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
13.14	Polished Stone Value	BS: 812 (P-114)	1 Test/ Source & As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
(XIII). Bituminous Concrete (BC)		MoRTH-500														
14.1	Binder Content & Gradation	As per MoRT&H	1 Test / 400 Tonnes	0	0	0	0	0	0	0	0	0	0	0	0	0.00
14.2	Mix Combined Gradation	As per MoRT&H	1 Test / 400 Tonnes	0	0	0	0	0	0	0	0	0	0	0	0	0.00
14.3	Marshall Test (In Sets)	ASTM-D-1559	1 Tet/ 400 Tonnes	0	0	0	0	0	0	0	0	0	0	0	0	0.00
14.4	Aggregate Impact Value (AIV)	IS : 2386 (P-4)	1 Test / 350 Cum	0	0	0	0	0	0	0	0	0	0	0	0	0.00
14.5	Combined Flakiness & Elongation (FI & EI)	IS : 2386 (P-1)	1 Test / 350 Cum	0	0	0	0	0	0	0	0	0	0	0	0	0.00
14.6	Water Absorption & Specific Gravity	IS : 2386 (P-3)	1 Test/ Source & As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
14.7	Stripping Value	IS : 6241	1 Test/ Source & As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
14.8	Maximum Sp.Gravity(Gmm)	ASTM D 2041	1 set/ 400 MTMix	0	0	0	0	0	0	0	0	0	0	0	0	0.00
14.9	Density of Compacted Layer	MoRT&H Sec:900	1 test / 700 Sqm	0	0	0	0	0	0	0	0	0	0	0	0	0.00
14.10	Soundness	IS : 2386 (P-3)	1 Test/ Source & As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
14.11	Sand equivalent test	IS : 2720 (P-37)	1 Test/ Source & As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
14.12	plasticity Index	MoRT&H Sec:900	1 Test/ Source & As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
14.13	percentage of Fractured face	MoRT&H Sec:900	1 Test/ Source & As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
14.14	Polished Stone Value	BS: 812 (P-114)	1 Test/ Source & As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
(XIV). Bitumen (VG-40)																
15.1	Softening Point(°C)	IS : 1205	1 Test Per Lot	0	0	0	0	0	0	0	0	0	0	0	0	0.00
15.2	Penetration at 25°C 100gm 5 Sec	IS : 1203	1 Test Per Lot	0	0	0	0	0	0	0	0	0	0	0	0	0.00
15.3	Ductility at 25°C	IS : 1208	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
15.4	Absolute Viscosity at 60°/135°C (CST)	IS : 1206 (P-2)	1 Test Per Lot	0	0	0	0	0	0	0	0	0	0	0	0	0.00
15.5	Kinematic Viscosity at 135°C (CST)	IS : 1206 (P-3)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0
15.6	Specific Gravity at 27°C	IS : 2380 (P-4)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
15.7	Flash Pint	IS : 1209 (IS: 1448 P-69)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0
15.8	Solubility Test	IS : 1216	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0
(XV). MODIFIED BITUMEN (PMB 76E-10)																
16.1	Specific Gravity at 27°C	IS : 2380 (P-4)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
16.2	Softening Point (°C)	IS : 1205	1 Test Per Lot	0	0	0	0	0	0	0	0	0	0	0	0	0.00
16.3	Seperation, Difference in Softening Point (0°C)	IS : 15462: 2019	1 Test Per Lot	0	0	0	0	0	0	0	0	0	0	0	0	0.00
16.4	Elastic Recovery at 15°C	IS : 15462: 2019	1 Test Per Lot	0	0	0	0	0	0	0	0	0	0	0	0	0.00
(XVI). Emulsion (SS-1)																
17.1	Viscosity @ 25°C	IS : 8887:2004	1 Test Per Lot	0	0	0	0	0	0	0	0	0	0	0	0	0
17.2	Water Content	IS : 8887:2004	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0
17.3	Prime coat	IS : 8887:2004	3 test / Day	0	0	0	0	0	0	0	0	0	0	0	0	0.00
(XVII). Emulsion (RS-1)																
18.1	Viscosity @ 50°C	IS : 8887:2004	1 Test Per Lot	0	0	0	0	0	0	0	0	0	0	0	0	0
18.2	Water Content	IS : 8887:2004	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0
18.3	Tack Coat	IS : 8887:2004	3 test / Day	0	0	0	0	0	0	0	0	0	0	0	0	0.00
(XVIII). Lean Concrete (DLC)		MoRT&H-600														
13.1	Gradation	Table 600-1	1 test / day	0	0	0	0	0	0	0	0	0	0	0	0	0.00
13.2	Field Compaction Test	IS : 2720 (P-28)	1 Set(3 pit) of tests / 2000 sqm.	0	0	0	0	0	0	0	0	0	0	0	0	0.00
13.3	Proctor test (MDD & OMC)	IS : 2720 (P-8)	As required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
13.4	Aggregate Impact Value (AIV)	IS : 2386 (P-4)	As required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
13.5	Flakiness & Elongation (FI & EI)	IS : 2386 (P-1)	As required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
13.6	Water Absorption	IS : 2386 (P-3)	As required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
13.7	Moisture correction	IS : 2386 (P-3)	1 test / Day	0	0	0	0	0	0	0	0	0	0	0	0	0.00
13.8	Compressive Strength (07 day's)	IS : 516	07 days/ Each Day 5 Cube's	0	0	0	0	0	0	0	0	0	0	0	0	0.00

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

(XIX). Pavement Quality Concrete (PQC)			MoRT&H-600													
14.1	Gradation	Table 600-1	1 Test / Day	0	0	0	0	0	0	0	0	0	0	0	0	0.00
14.2	Aggregate Impact Value (A.I.V)	IS: 2386 (P-4)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
14.3	Flakiness 7 Elongation (FI & EI)	IS: 2386 (P-1)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
14.4	Water Absorption	IS: 2386 (P-3)	As Required	0	0	0	0	0	0	0	0	0	0	0	0	0.00
14.5	Slump Test	IS: 1199	1 Test Each Dumper	0	0	0	0	0	0	0	0	0	0	0	0	0.00
14.6	Compressive Strength (07 day's)	IS: 516	Compressive Strength (07 day's)	0	0	0	0	0	0	0	0	0	0	0	0	0.00
14.7	Compressive Strength (28 day's)	IS: 516		0	0	0	0	0	0	0	0	0	0	0	0	0.00
14.8	Flexural Strength (07 day's)	IS: 516		As per Frequency 02 Beam's /150 Cum (Min. 6 Beam's)	0	0	0	0	0	0	0	0	0	0	0	0.00
14.9	Flexural Strength (28 day's)	IS: 516		0	0	0	0	0	0	0	0	0	0	0	0	0.00
THIRD PARTY TESTS (NABL ACCREDITED LABORATORY)																
(XX). Coarse Aggregates																
18.1	Gradation	IS: 2386 (P-1)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
18.2	FI & EI	IS: 2386 (P-1)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
18.3	Aggregate Impact Value	IS: 2386 (P-4)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
18.4	Specific Gravity	IS: 2386 (P-3)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
18.5	Water Absorption	IS: 2386 (P-3)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
18.6	Deleterious Content	IS: 2386 (P-1)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
18.7	L.A.V.	IS: 2386 (P-4)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
18.8	Alkali Aggregate Reactivity	IS: 2386 (P-7)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
18.9	Soundness	IS: 2386(P-5)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
18.10	Petrographic Examination	IS: 2386 (P-8)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
18.11	Stone Polished Value	BS-812 (P-114)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
(XXI). Fine Aggregates																
19.1	Gradation	IS: 383	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
19.2	Specific Gravity	IS: 2386 (P-3)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
19.3	Water Absorption	IS: 2386 (P-3)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
19.4	Deleterious Content	IS: 2386 (P-1)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
19.5	Silt Content	IS: 2386 (P-4)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
19.6	Alkali Aggregate Reactivity	IS: 2386 (P-7)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
19.7	Soundness	IS: 2386(P-5)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
19.8	Organic Impurities	IS: 2386 (P-8)	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
19.9	Fineness Modulus	IS: 383	1 Test / Source	2	2	0	0	0	0	2	2	0	0	0	0	0.00
(XXII). TMT Bar's (Steel)																
20.1	Physical properties	IS: 1786	< 10mm - 1 sample/25 MT, 10-16mm-1sample/35 MT,	1	1	0	0	0	0	1	1	0	0	0	0	0.00
20.2	Chemical properties	IS: 1786	> 16mm - 1 sample/45 MT	1	1	0	0	0	0	1	1	0	0	0	0	0.00
20.3	Factory Visit	IS: 1786	Elegant Steel Jointly	1	1	0	0	0		1	1	0	1	1	0	#DIV/0!
(XXIII). Construction Water																
21.1	Suitability for construction	IS: 456	1 Test Per Source / As Required	1	1	0	0	0	0	1	1	0	0	0	0	0.00
(XXIV). Chemical Admixture																
22.1	Physical & Chemical properties	IS: 9103	1 Test/ Per Lot	1	1	0	0	0	0	1	1	0	0	0	0	0.00
(XXV). Cement (OPC-53 Grade)																
23.1	Physical & Chemical properties	IS: 8112	1 Test / Source	3	3	0	0	0	0	3	3	0	0	0	0	0.00
(XXVI). Soil - Borrow Area																
24.1	Mechanical	IS: 2720 (P-39)	1 Test / Source	0	0	0	0	0	0	0	0	0	0	0	0	0.00
(XXVII). NP-4 Hume Pipe Test																
25.1	600 MM	IS: 458	1 test per Lot /of 50 Pipes	0	0	0	0	0	0	0	0	0	0	0	0	0.00
(XXVIII). Bitumen (Emulsion)																
26.1	Bitumen Emulsion SS-1	IS: 8887	1 Test/ Per Lot	0	0	0	0	0	0	0	0	0	0	0	0	0.00
26.2	Bitumen Emulsion RS-1	IS: 8887	1 Test/ Per Lot	0	0	0	0	0	0	0	0	0	0	0	0	0.00
(XXIX). Bitumen (VG-40)																
27.1	Bitumen VG-40	IS: 73	1 Test/ Per Lot	0	0	0	0	0	0	0	0	0	0	0	0	0.00
(XXX). Bitumen (PMB)																
28.1	Bitumen PMB	IS: 15462-2019	1 Test/ Per Lot	0	0	0	0	0	0	0	0	0	0	0	0	0.00
(XXXI). Curing Compound																
29.1	Physical & Chemical properties	ASTM C309	1 Test/ Per Lot	0	0	0	0	0	0	0	0	0	0	0	0	0.00

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

**CHAPTER-11
CORRESPONDENCE**

11.1 Outward Letter

Sr. No.	Letter No.	Date	Subject	To
1	MKCIL/ASSAM/P KG-07/309	05.08.2025	Submission of Monthly Progress Report for the month of July-2025	TL
2	MKCIL/ASSAM/P KG-07/318	11.08.2025	Joint Inspection identification for Extraction of Soil for Road Works	GM (PMU Karimganj)
3	MKCIL/ASSAM/P KG-07/319	11.08.2025	Joint Inspection identification for Extraction of Soil for Road Works	GM (PMU Karimganj)
4	MKCIL/ASSAM/P KG-07/320	11.08.2025	Joint Inspection identification for Extraction of Soil for Road Works	GM (PMU Karimganj)
5	MKCIL/ASSAM/P KG-07/321	11.08.2025	Joint Inspection identification for Extraction of Soil for Road Works	GM (PMU Karimganj)
6	MKCIL/ASSAM/P KG-07/322	11.08.2025	Joint Inspection identification for Extraction of Soil for Road Works	GM (PMU Karimganj)
7	MKCIL/ASSAM/P KG-07/323	11.08.2025	Joint Inspection identification for Extraction of Soil for Road Works	GM (PMU Karimganj)
8	MKCIL/ASSAM/P KG-07/325	12.08.2025	Regarding Submission of Design and Drawing for Major Bridge at Ch. 05+322 (3x37.5m).	TL
9	MKCIL/ASSAM/P KG-07/327	14.08.2025	Regarding Submission of GAD for Precast Box Culvert at Ch.13+740 (1x2x2).	TL
10	MKCIL/ASSAM/P KG-07/330	18.08.2025	Regarding Submission of Revised Plan and Profile with TCS for Main Carriageway & Service Road	TL
11	MKCIL/ASSAM/P KG-07/331	18.08.2025	Regarding Submission of Revised Test Pile Drawing of Major Bridge at Ch. 02+893	TL
12	MKCIL/ASSAM/P KG-07/336	22.08.2025	Closure of NCR – Non-Compliance with Safety Norms at Chainage 12+800 to 13+500 (LHS)	TL
13	MKCIL/ASSAM/P KG-07/340	28.08.2025	Request for In-Principal Approval of Additional Bituminous Maintenance Work of Town Portion and Other length of Existing Road which is not in scope of Concessionaire as per Concession Agreement	GM (PMU Karimganj)
14	MKCIL/ASSAM/P KG-07/341	28.08.2025	Regarding Submission of Design and Drawing for Precast Box Culvert at Ch.12+223 (1x2x2).	TL
15	MKCIL/ASSAM/P KG-07/345	29.08.2025	Regarding Submission of Design and Drawing for Box Culvert at Ch. 00+043 & 06+642 (1x3x2).	TL
16	MKCIL/ASSAM/P KG-07/346	29.08.2025	Regarding Submission of GAD for Precast Box Culvert at Ch. 03+418 (1x2x2).	TL
18	MKCIL/ASSAM/P KG-07/348	30.08.2025	Proposal for Change of Scope (COS) for Construction of Rigid Pavement in Karimganj Town Portion due to Severe Highway Distress"	GM (PMU Karimganj)

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

11.2 Inward Letter (NHIDCL & TASPL)

Sr. No.	Letter No.	Date	Subject	From
1	TASPL-MAV/NH-37/MKICL/2025/MAY/53	05.08.2025	Reg. non-compliance with safety norms at location 12+800 to 13+500	TASPL
2	TASPL-MAV/NH-37/MKICL/2025/AUG/55	08.08.2025	Approval of Elegant Steel.	TASPL
3	TASPL-MAV/NH-37/MKICL/2025/AUG/59	11.08.2025	Submission of Physical & Chemical Test Report – Elegant Steel. –Reg	TASPL
4	TASPL-MAV/NH-37/MKICL/2025/AUG/60	14.08.2025	Reg. Observation on Design & Drawings at CH. CH-0+207, CH-0+341, CH.1+768, CH 2+893 & CH 4+340	TASPL
5	TASPL-MAV/NH-37/MKICL/2025/AUG/65	29.08.2025	Part Approval of Plan and Profile -Chainage 12+000 to 14+380	TASPL
6	TASPL-MAV/NH-37/MKICL/2025/AUG/66	28.08.2025	Submission of observation of MPR for the month of july-2025	TASPL

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

CHAPTER-12

NON-CONFORMANCE REPORT

NIL

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

**CHAPTER-13
WEATHER REPORT**

Sl no.	Date	Temperature (In °c)		Humidity (In %)		Rainfall (mm)	Weather Condition	Remarks
		Minimum	Maximum	Minimum	Maximum			
1	01-08-2025	27.2	29.6	78.0	84.0	45.40	Cloudy/Rainy	
2	02-08-2025	27.1	28.4	79.0	82.0	41.20	Cloudy/Rainy	
3	03-08-2025	28.1	29.3	77.0	83.0	38.60	Cloudy/Rainy	
4	04-08-2025	27.1	29.5	77.0	85.0	48.30	Cloudy/Rainy	
5	05-08-2025	27.0	28.9	74.0	88.0	44.60	Cloudy/Rainy	
6	06-08-2025	27.3	29.4	77.0	90.0	38.20	Cloudy/Rainy	
7	07-08-2025	27.2	29.1	78.0	89.0	7.40	Cloudy/Rainy	
8	08-08-2025	27	28.8	76.0	84.0	22.30	Cloudy/Rainy	
9	09-08-2025	27.3	29.1	78.0	87.0	18.80	Cloudy/Rainy	
10	10-08-2025	27.5	29.4	79.0	88.0	28.20	Cloudy/Rainy	
11	11-08-2025	26.5	29.7	78.0	89.0	42.40	Cloudy/Rainy	
12	12-08-2025	27.2	30.4	79.0	90.0	36.30	Cloudy/Rainy	
13	13-08-2025	27.1	30.2	80.0	88.0	30.50	Cloudy/Rainy	
14	14-08-2025	27.2	29.9	77.0	87.0	0.00	Sunny	
15	15-08-2025	26.9	30.4	79.0	86.0	14.40	Cloudy/Rainy	
16	16-08-2025	26.5	29.2	73.0	88.0	18.50	Cloudy/Rainy	
17	17-08-2025	26.9	31.4	75.0	89.0	0.00	Sunny	
18	18-08-2025	27.1	30.2	76.0	90.0	21.20	Cloudy/Rainy	
19	19-08-2025	26.8	31.5	74.0	88.0	12.10	Cloudy/Rainy	
20	20-08-2025	27.8	30.8	73.0	91.0	24.20	Cloudy/Rainy	
21	21-08-2025	27.9	31.3	76.0	90.0	15.40	Cloudy/Rainy	
22	22-08-2025	28.6	30.0	75.0	81.0	24.30	Cloudy/Rainy	
23	23-08-2025	29.7	32.1	69.0	79.0	0.00	Sunny	
24	24-08-2025	29.1	33.7	63.0	78.0	0.00	Sunny	
25	25-08-2025	30	32.9	67.0	75.0	42.20	Cloudy/Rainy	
26	26-08-2025	30.1	33.4	63.0	73.0	8.40	Cloudy/Rainy	
27	27-08-2025	28.3	31.0	74.0	79.0	54.40	Cloudy/Rainy	
28	28-08-2025	28.7	31.4	75.0	80.0	48.60	Cloudy/Rainy	
29	29-08-2025	29.3	31.5	72.0	78.0	18.40	Cloudy/Rainy	
30	30-08-2025	28.6	31.2	73.0	80.0	0.00	Sunny	
31	31-08-2025	31.5	33.6	67.0	76.0	0.00	Sunny	

Rainfall Data				
Sr.no.	Description	Total Rainfall	Up to previous month	This month
1	Rainfall	3349.5	2605.2	744.30

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

The maximum & minimum weather records are summarized below:

TEMPERATURE/ RAINFALL PERIOD: 1st August, 2025 to 31st August, 2025				
Temperature		Rainfall		
Maximum (in ° C)	Minimum (in ° C)	Maximum (in mm)	Minimum (in mm)	Total Days
33.7	26.5	54.5	0	25

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

CHAPTER-14
ACCIDENT REPORT

NIL

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

CHAPTER-15

ROAD MAINTENANCE & SAFETY REPORT

The Traffic Safety Arrangements during the execution of works is being carried out by the Concessionaire for safe movement of vehicles on the project highway. The Concessionaire has provided sufficient road signs, temporary barriers, gunny bags filled with soil with reflective stickers etc. at the construction sites.

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.

CHAPTER-16

PROJECT PROGRESS PHOTOGRAPHS



1. Concrete pouring work for Toe wall Ch. 10+050



2. Reinforcement work at Ch.4+212 (LVUP)

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.



3. Reinforcement work at Ch.4+212 (LVUP)



4. Level Checking work for SG top at Ch.- 12+900 to 13+200

4-L of NH 37 from design Ch 0+000 on NH-8 near Karimganj to design Chainage 14+250 near Sutarkandi (Spur Connectivity to Indo/Bangladesh Border) Silchar-Churaibari Pkg-7 in the State of Assam on HAM mode.



5.Reinforcement work at Ch.10+098 (LVUP)



6. Utility shifting work at Ch. 13+380
